## Traffic Control & Staging (Overview)

Vehicles

**One (1) Travel Lane in Each Direction** 

**Traffic Crossovers** 

**Turn Lane Restrictions at Intersections** 

Pedestrians & Bicycles


Existing - Temporary - Proposed - Detoured

Boats

**Restrictions during Bridge Structure Construction** 

Railroad Crossings

**Complete Closures for Crossing Construction** 

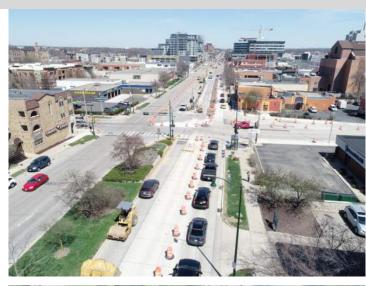



# Traffic Control & Staging (Stage 1: October 2025 - November 2025)

### **Traffic:**


One Lane in Each Direction
Intersections Open
Existing Capital City Trail Open

### **Construction:**

Traffic Crossovers
Temporary Pavement
Storm Sewer Connections
Temporary Traffic Signals



# Traffic Control & Staging (Stage 2: November 2025 - July 2026)

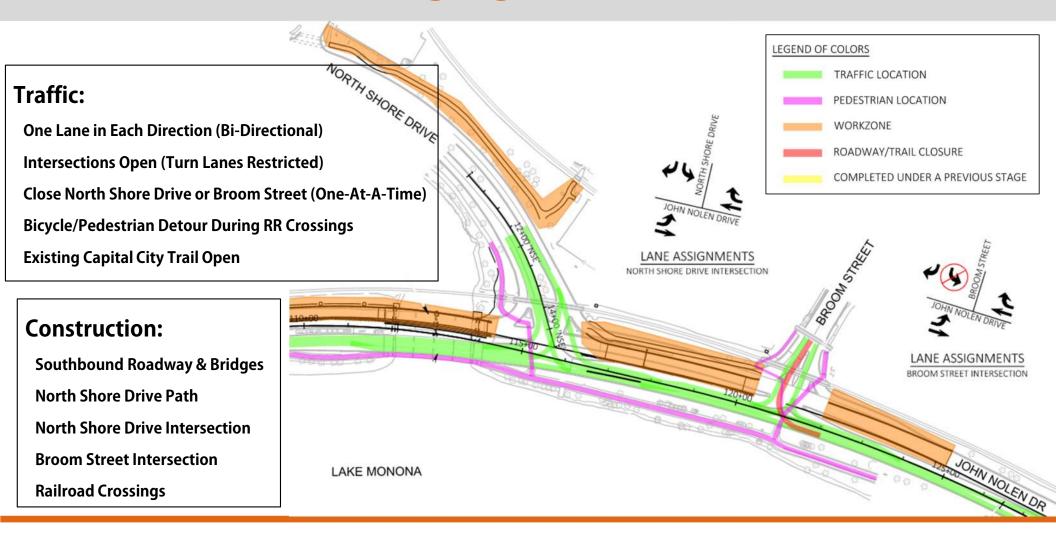

## Traffic Control & Staging (Railroad Crossing Detours)

#### **North Shore Drive (Summer 2026)**

Roadway Closure: 60 Calendar Days Sidewalk Closure: 10 Calendar Days




#### **Broom Street (Summer 2026)**

Roadway Closure: 50 Calendar Days Sidewalk Closure: 10 Calendar Days



Legend
Work Zone
Detour Route
Railroad Crossing Construction

# Traffic Control & Staging (Stage 3: July 2026 - June 2027)

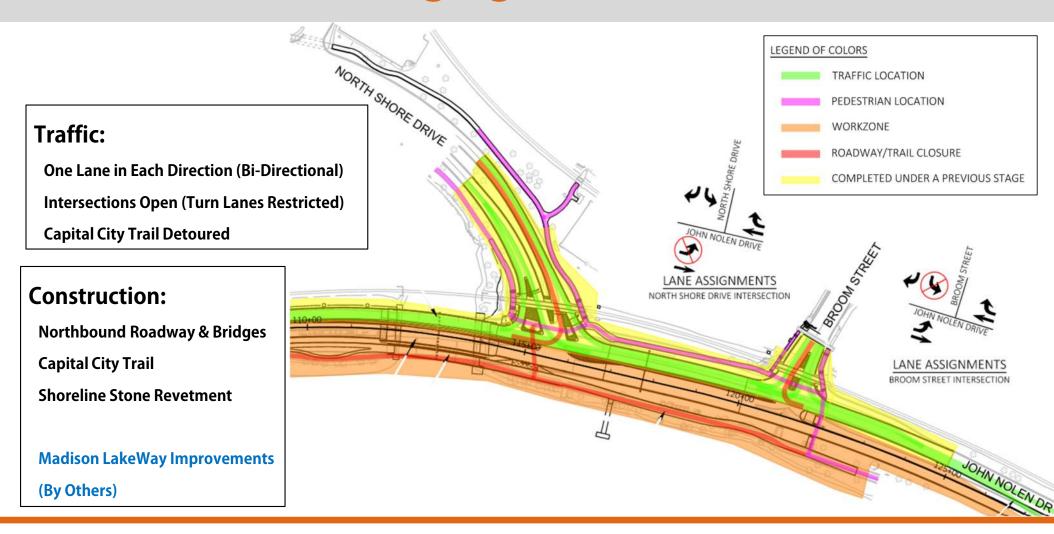

### Traffic Control & Staging (Capital City Trail Detour)



### **Capital City Trail Closure**

(Approximately July 2026 to July 2027)

Legend
Work Zone
Detour Route
Capital City Trail Construction

# Traffic Control & Staging (Stage 4: June 2027 - July 2027)

### **Traffic:**

One Lane in Each Direction
Intersections Open
Capital City Trail Detoured

### **Construction:**

Median


**Final HMA Surface & Finishing** 

**Madison LakeWay Improvements** 


(By Others)




### Traffic Control & Staging (Boat Navigation)

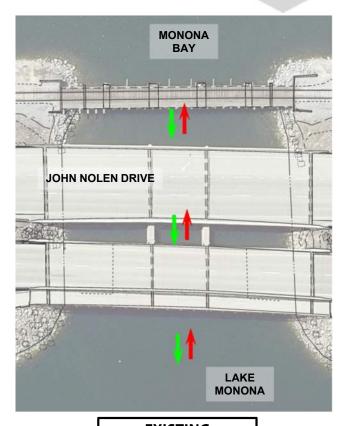

EXISTING
(SHARE MIDDLE SPAN)

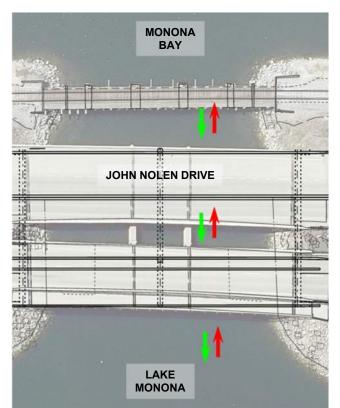

DURING CONSTRUCTION
(SHARE EXTERIOR SPAN)

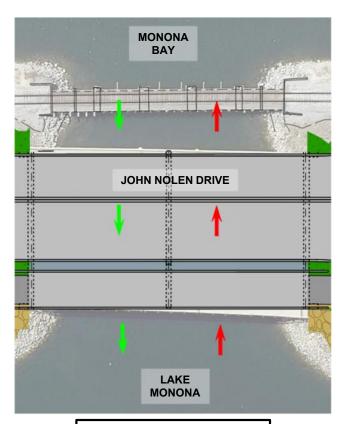

AFTER CONSTRUCTION
(SEPARATE OWN SPAN)
