


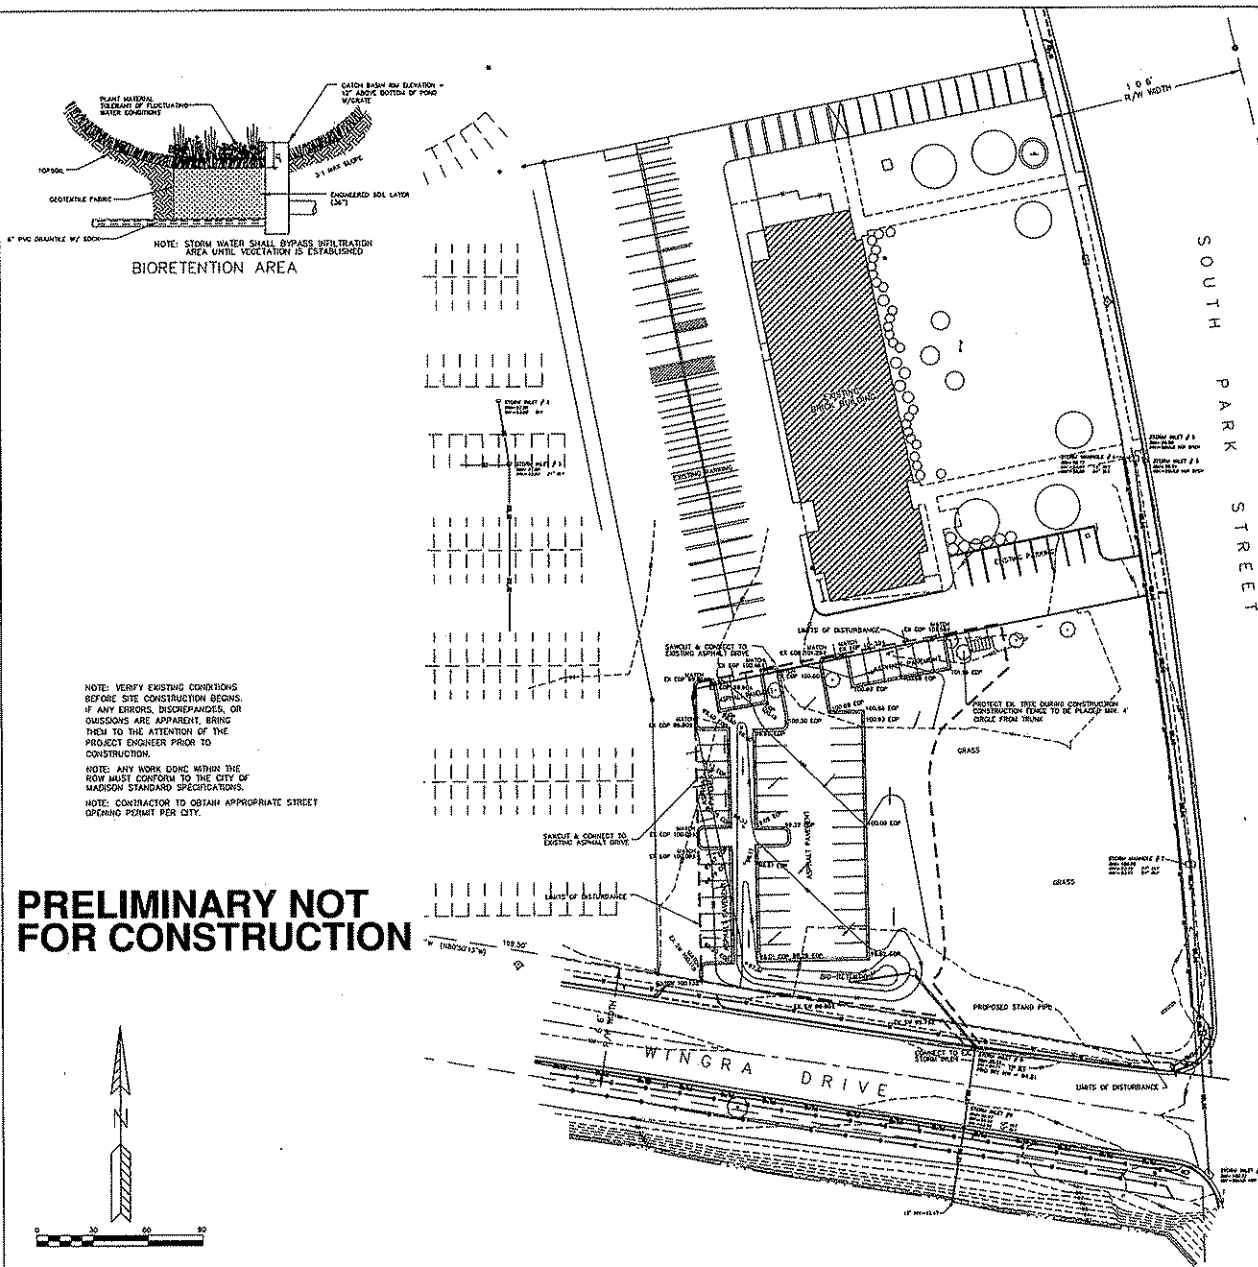

GENERAL NOTES

STONE CONSTRUCTION ENTRANCES SHALL BE INSTALLED PRIOR TO ANY CONSTRUCTION. EROSION CONTROL DEVICES SHALL BE INSTALLED PRIOR TO GRADING OPERATIONS AND SHALL BE PROPERLY MAINTAINED FOR MAXIMUM EFFECTIVENESS UNTIL VEGETATION IS ESTABLISHED.

SILT FENCE & STOCKPILES SHALL BE FIELD LOCATED BY THE CONSTRUCTION MANAGER. SILT FENCE SHALL BE PLACED DOWN-SLOPE AT LEAST 10 FEET FROM SILT STOCKPILES FOR PROTECTION. SILT STOCKPILES LEFT INACTIVE FOR MORE THAN 14 DAYS SHALL BE STABILIZED WITH SEED & MULCH, EROSION MAT, POLYMER, OR COVERED WITH TARPS OR SIMILAR MATERIAL.

CUT AND FILL SLOPES SHALL BE NO GREATER THAN 3:1.

ADDITIONAL EROSION CONTROL MEASURES WILL BE INSTALLED AS NEEDED.

AFTER ROUGH GRADING HAS BEEN COMPLETED STRAW MULCH OR EROSION MATTING SHALL BE PLACED ON SLOPES 4:1 OR GREATER.

PLACE TYPE D INLET PROTECTION IN EACH INLET BEFORE CONSTRUCTION.



ANY DISTURBED AREA THAT REMAINS INACTIVE FOR GREATER THAN 7 DAYS SHALL BE STABILIZED WITH TEMPORARY STABILIZATION METHODS SUCH AS TEMPORARY SEEDING, SOIL TREATMENT, OR MULCH.

RESTORATION

ALL DISTURBED AREAS SHALL RECEIVE A MINIMUM OF SIX (6) INCHES OF TOPSOIL. FERTILIZER, SEED, AND MULCH. RESTORATION WILL OCCUR AS SOON AFTER THE DISTURBANCE AS PRACTICAL. SEED MIXTURE 40 (PER SECTION 830 OF D.O.T. SPECIFICATIONS) APPLIED AT A RATE OF 5 POUNDS PER 1000 SQ. FT. WILL BE USED ON ALL AREAS EXCEPT BIORETENTION AREAS. THE BIORETENTION AND AREAS SHALL BE PLANTED PER THE CITY OF MADISON SPECIFICATIONS AND ACCORDING TO THE LANDSCAPE PLAN. SEE SHEET L101.

FERTILIZER SHALL BE PLACED PER A SOIL TEST.

- 1. FERTILIZER SHALL BE PLACED PER A SOIL TEST.
- 2. FERTILIZER SHALL BE PLACED PER A SOIL TEST.

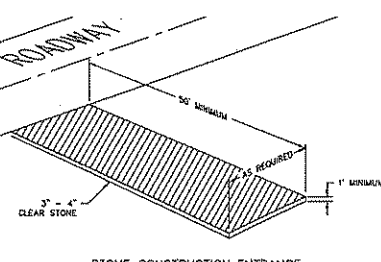

LEGEND

- DISTANCE ARROWS
- SPOT ELEVATION
- EXISTING THICK CONTOURS
- EXISTING CONTOURS
- PROPOSED WORK CONTOURS
- PROPOSED CONTOURS

LIMITS OF DISTURBANCE = 24,500 SQ. FT.
PROPOSED ADDITIONAL IMPERVIOUS = 12,100 SQ. FT.



CONSULTANT

DATE: 07/23/2010
PROJECT: GRADING AND EROSION CONTROL PLAN
PROJECT TITLE: MADISON LABOR TEMPLE PARKING EXPANSION
PROJECT LOCATION: MADISON, WI

REVISION	DATE	DESCRIPTION
	07/23/07	ISSUED PERMITTING WALL
	06/24/08	REVISED SITE
Drawn By	G	
Checked By	M	
	01/22/09	
Job No.	GA09	
This document contains confidential or proprietary information of Hays Corporation. Neither this document nor the information herein shall be reproduced, distributed, or disclosed, either in whole or in part except as specifically authorized by Hays Corporation.		
© 2003		

