ROUTING: Routine	Contract Routing Form	printed on: 12/05/2014					
Contract between: and Dept. or Division: Name/Phone Number:	and Dept. or Division: Engineering Division Name/Phone Number:						
Project: Wingra Creek Pa	arkway PH e						
Contract No.: 6832 Enactment No.: RES-14-00 Dollar Amount: 1,030,846	,						
(Please DATE before rout:	ing)						
Signatures Required	Date Received	Date Signed					
City Clerk	12-5-14	12.5-14					
Director of Civil Rights	12-8-2014	12/12/14/100					
Risk Manager	12-15-14	12/16/14 RESV					
Finance Director	1 12-16-14 W						
City Attorney	15cp 12-17-14	112-17-14					
Mayor	1 12 -18 14	1=118/14					
Please return signed Cont Room 103, City-County Bui Original + 2 Copi	tracts to the City Clerk's Cilding for filing. PO#81	office 1536832 12/17/14 KUSV					
12/05/2014 14:13:56 enjag	o - S Swenson 266-4862						

Plane caron to superior con copies of scanness

Dis Rights: OK / Problem - Hold
Prev Wage: AA / Agency // No
Contract Value: See a bove
AA Plan: About Addendum #
Type: POS / Dwp / Sbolv / Gov't /
Grant / PW / Goal / Loan / Agrmt

<u>Sign In</u>

Legislative Information Center Home

Legislation

Meetings

Common Council

Boards, Commissions and Committees

Members

O Share 引知 II...) 图 RSS (多 Alerts)

Details

Reports

Awarding Public

File #:

36107 Version: 1

Name:

Works Contract No.

6832, Wingra Creek

Parkway, Phase 3.

Type:

Resolution

Status:

Passed

WORKS

File created:

11/7/2014

In control:

BOARD OF PUBLIC

On agenda:

12/2/2014

Final action:

12/2/2014

Enactment date:

12/3/2014

Enactment #:

RES-14-00882

Title:

Awarding Public Works Contract No. 6832, Wingra Creek Parkway, Phase 3.

Sponsors:

BOARD OF PUBLIC WORKS

Attachments:

1. Contract 6832.pdf

History (3)

Text

3 records Gr	oup	Export		,		-
Date	Ver.	Action By	Action	Result	Action Details	Watch
12/2/2014	1	COMMON COUNCIL	of Change Control Cont		Not available	Not available
11/19/2014	1	BOARD OF PUBLIC WORKS			Not available	Not available
11/7/2014	1	Engineering Division	Refer		Action details	Not available

		•
	`	
	e e e e e e e	

CONTRACT NO. 6832 WINGRA CREEK PARKWAY, PHASE 3

SPEEDWAY SAND & GRAVEL, INC.

\$1,030,846.42

Acct. No. ESTM-58290-810268-00-53W0312 Contingency 8%± Sub Total	983,070.67 78,649.33 ,061,720.00
Acct. No. CS53-58240`-810375-00-53W0312 Contingency 8%± Plan & Prep 15%± Sub Total	\$47,775.75 3,822.00 7,162.25 \$58,760.00

GRAND TOTAL

\$1,120,480.00

			• •

Wisconsin Office of the Commissioner of Insurance Licensed Producer Search*

Thursday, December 4, 2014

REZ

MOSCA, ELIZABETH MIDDLETON WI

Year of Birth: 1957

Status: Active

License Number: 2530156

NPN**: 12305256

Effective Date: 11-18-2008 Expiration Date: 03-31-2015

License Type: Resident Intermediary Indv

CE Compliance: 03-31-2015

Lines of Authority

Line of Authority	Residency	Effective Date	Status
Property	Resident	11-25-2008	Active
Casualty	Resident	11-18-2008	Active

Appointments and Terminations

	alification pe/Status	Effective 1 Date	Termination Date	Termination Reason
American Casualty Company of Reading, Pennsylvania	CAS/Active CAS/Inactive	05-21-2013 01-08-2009	09-29-2010	Vol. Surrender per Agent Rast
	PROP/Active	05-21-2013		Agent Nyst
	PROP/Inactive	01-08-2009	09-29-2010	Vol. Surrender per Agent Rqst
American Economy Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
American Fire and Casualty Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
American States Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
Berkley Regional Insurance Company	CAS/Active PROP/Active	01-12-2009 01-12-2009		
Colonial American Casualty and Surety Company	CAS/Active PROP/Active	05-14-2013 05-14-2013		
Consolidated Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	•	Canceled Canceled
Continental Casualty Company	CAS/Active CAS/Inactive	05-21-2013 01-08-2009	09-29-2010	Vol. Surrender per

			•		
SCHOOL STATE OF SECURITY SANS					Agent Rqst
Name of the last		PROP/Active	05-21-2013		MAC TERROPAWARE
		PROP/Inactive	01-08-2009	09-29-2010	Vol. Surrender per Agent Rqst
· ·	Continental	CAS/Active	05-21-2013		
and the same of	Insurance Company,	PROP/Active	05-21-2013		
The Control of the Co	The	revolutions of a raily man to quest ambitudes of more unbanganic street, the appeal semilies and simplest	$(a_{1},a_{2},a_{3},a_{4},a_{5},a_{$	and the second s	
- Control of the last of the l	Fidelity and Deposit	CAS/Active	05-14-2013	The state of the s	
order Committee	Company of Maryland	PROP/Active	05-14-2013		
CV C					
Nechhaorana	First National Insurance Company	CAS/Inactive	01-18-2010	08-25-2014	Canceled
COMMENSOR	of America	PROP/Inactive	01-18-2010	08-25-2014	Canceled
THE PERSON NAMED IN	First Sealord Surety,	CAS/Inactive	09-17-2009	02-08-2012	Canceled
- Distantion	Inc.	C/(S/Indecive	03 17 2003	02 00 2012	331133133
***************************************	General Insurance	CAS/Inactive	01-18-2010	08-25-2014	Canceled
	Company of America	PROP/Inactive	01-18-2010	08-25-2014	Canceled
	Connits Do Inc	CAS/Active	01-14-2009		
	Granite Re, Inc.	CAS/Active			
	Guarantee Company of North America USA, The	CAS/Inactive	01-22-2009	12-28-2011	Vol. Surrender per Agent Rqst
	Hawkeye-Security	CAS/Inactive	01-18-2010	08-25-2014	Canceled
and the state of t	Insurance Company	PROP/Inactive	01-18-2010	08-25-2014	Canceled
	Indiana Insurance	CAS/Inactive	01-18-2010	08-25-2014	Canceled
	Company	PROP/Inactive	01-18-2010	08-25-2014	Canceled
	Liberty Mutual	CAS/Inactive	02-04-2010	08-25-2014	Canceled
	Insurance Company	3. (3) 2. (4.4)			
	Merchants Bonding	CAS/Active	05-03-2013		•
	Company (Mutual)	CAS/Inactive	12-03-2008	10-12-2010	Canceled
	Merchants National Bonding, Inc.	CAS/Active	05-03-2013		
	Midwestern	CAS/Inactive	01-18-2010	08-25-2014	Canceled
	Indemnity Company,	PROP/Inactive	01-18-2010	08-25-2014	Canceled
	The				·
	National Fire	CAS/Active	05-21-2013	* .	
	Insurance Company of Hartford	CAS/Inactive	01-08-2009	09-29-2010	Vol. Surrender per Agent Rqst
		PROP/Active	05-21-2013		
		PROP/Inactive	01-08-2009	09-29-2010	Vol. Surrender per Agent Rqst
	 Netherlands	CAS/Inactive	01-18-2010	08-25-2014	Canceled
	\		•	· ·	

	•				
	Insurance Company, The	PROP/Inactive	01-18-2010	08-25-2014	Canceled
	Ohio Casualty Insurance Company, The	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
ACCOUNT AND ADDRESS OF THE PARTY OF THE PART	Ohio Security Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
The state of the s	Old Republic Insurance Company	CAS/Active CAS/Inactive	12-30-2010 12-20-2008	07-06-2010	Canceled
THE PERSON NAMED AND PARTY OF THE PE	Old Republic Surety Company	CAS/Active CAS/Inactive	12-30-2010 12-20-2008	07-06-2010	Canceled
THE PERSON NAMED IN COLUMN NAM	Peerless Indemnity Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
TOTAL PARTICIPATION OF THE PERSON NAMED IN COLUMN	Peerless Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
	SAFECO Insurance Company of America	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
STATE OF THE PROPERTY OF THE PERSON NAMED IN	SAFECO Insurance Company of Illinois	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
STATE OF THE PROPERTY OF THE PARTY OF THE PA	Star Insurance Company	CAS/Inactive PROP/Inactive	07-06-2010 07-06-2010	04-19-2011 04-19-2011	Canceled Canceled
THE PROPERTY OF THE PARTY OF TH	Transportation Insurance Company	CAS/Active PROP/Active	05-21-2013 05-21-2013		
	United Fire & Casualty Company	CAS/Active PROP/Active	10-03-2013 10-03-2013		
Charles on the Control of	Valley Forge Insurance Company	CAS/Active PROP/Active	05-21-2013 05-21-2013		
PATRACTOR STREET, STRE	West American Insurance Company	CAS/Inactive PROP/Inactive	01-18-2010 01-18-2010	08-25-2014 08-25-2014	Canceled Canceled
STATE OF THE PROPERTY OF THE P	West Bend Mutual Insurance Company	CAS/Active PROP/Active	08-08-2011 08-08-2011		
AND DESCRIPTION OF THE PROPERTY OF THE PROPERT	Western National Mutual Insurance Company	CAS/Active PROP/Active	04-03-2014 04-03-2014		
The state of the s	Western Surety Company	CAS/Active CAS/Inactive	09-25-2013 01-08-2009	10-28-2010	Vol. Surrender per Agent Rast
Navigora and a second	Zurich American	CAS/Active	05-14-2013		

Insurance Company PROP/Active 05-14-2013

- * Photocopies of this report provided to an insurer should be confirmed on-line for accuracy.
- ** NPN = National Producer Number assigned by the National Insurance Producer Registry to assist with nonresident licensing in the future.

\$1,030,846.42 FILE

BID OF SPEEDWAY SAND & GRAVEL, INC.

2014

PROPOSAL, CONTRACT, BOND AND SPECIFICATIONS

FOR

WINGRA CREEK PARKWAY, PHASE 3

CONTRACT NO. 6832 PROJECT NO. 53W0312

IN

MADISON, DANE COUNTY, WISCONSIN

AWARDED BY THE COMMON COUNCIL MADISON, WISCONSIN ON **DECEMBER 2, 2014**

> CITY ENGINEERING DIVISION 1600 EMIL STREET MADISON, WISCONSIN 53713

https://bidexpress.com/login

			i.	
	•			

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

INDEX

SECTION A: ADVERTISEMENT FOR BIDS AND INSTRUCTIONS TO BIDDERS	A-
SECTION B: PROPOSAL SECTION	B-′
SECTION C: SMALL BUSINESS ENTERPRISE	C-1
SECTION D: SPECIAL PROVISIONS	D-1
SECTION E: BIDDER'S ACKNOWLEDGEMENT	E-1
SECTION F: DISCLOSURE OF OWNERSHIP & BEST VALUE CONTRACTING	F-1
SECTION G: BID BOND	G-1
SECTION H: AGREEMENT	H-1
SECTION I: PAYMENT AND PERFORMANCE BOND	
SECTION J: PREVAILING WAGE RATES	J-1

This Proposal, and Agreement have been prepared by:

CITY ENGINEERING DIVISION
CITY OF MADISON
MADISON, DANE COUNTY, WISCONSIN

Robert F. Phillips, P.E., City Engineer

RFP: ss

SECTION A: ADVERTISEMENT FOR BIDS AND INSTRUCTIONS TO BIDDERS

REQUEST FOR BID FOR PUBLIC WORKS CONSTRUCTION CITY OF MADISON, WISCONSIN

A BEST VALUE CONTRACTING MUNICIPALITY

PROJECT NAME:	WINGRA CREEK PARKWAY, PHASE 3
CONTRACT NO.:	6832
SBE GOAL	14%
BID BOND	5%
PRE BID MEETING (1:00 P.M.)	OCTOBER 31, 2014
PREQUALIFICATION APPLICATION DUE (1:00 P.M)	OCTOBER 31, 2014
BID SUBMISSION (1:00 P.M.)	NOVEMBER 7, 2014
BID OPEN (1:30 P.M.)	NOVEMBER 7, 2014
PUBLISHED IN WSJ	10/24/14 & 10/31/14

PRE BID MEETING: Representatives of the Affirmative Action Department will be present to discuss the Small Business Enterprise requirements at 1600 Emil Street, Madison Wisconsin.

PREQUALIFICATION APPLICATION: Forms are available on our website, www.cityofmadison.com/business/pw/forms.cfm. If not currently prequalified in the categories listed in Section A, an amendment to your Prequalification will need to be submitted prior to the same due date. Postmark is not applicable.

BIDS TO BE SUBMITTED by hand to 1600 EMIL ST., MADISON, WI 53713 or online at www.bidexpress.com.

THE BID OPENING is at 1600 EMIL ST., MADISON, WI 53713.

STANDARD SPECIFICATIONS

The City of Madison's Standard Specifications for Public Works Construction - 2014 Edition, as supplemented and amended from time to time, forms a part of these contract documents as if attached hereto.

These standard specifications are available on the City of Madison Public Works website, www.citvofmadison.com/Business/PW/specs.cfm.

The Contractor shall review these Specifications prior to preparation of proposals for the work to be done under this contract, with specific attention to Article 102, "BIDDING REQUIREMENTS AND CONDITIONS" and Article 103, "AWARD AND EXECUTION OF THE CONTRACT." For the convenience of the bidder, below are highlights of three subsections of the specifications.

SECTION 102.1: PRE-QUALIFICATION OF BIDDERS

In accordance with Wisconsin State Statutes 66.0901 (2) and (3), all bidders must submit to the Board of Public Works proof of responsibility on forms furnished by the City. The City requires that all bidders be qualified on a biennial basis.

Bidders must present satisfactory evidence that they have been regularly engaged in the type of work specified herein and they are fully prepared with necessary capital, materials, machinery and supervisory personnel to conduct the work to be contracted for to the satisfaction of the City. All bidders must be pre-

qualified by the Board of Public Works for the type of construction on which they are bidding prior to the opening of the bid.

In accordance with Section 39.02(9)(a)I. of the General Ordinances, all bidders shall submit in writing to the Affirmative Action Division Manager of the City of Madison, a Certificate of Compliance or an Affirmative Action Plan at the same time or prior to the submission of the proof of responsibility forms.

The bidder shall be disqualified if the bidder fails to or refuses to, prior to opening of the bid, submit a Certificate of compliance, Affirmative Action Plan or Affirmative Action Data Update, as applicable, as defined by Section 39.02 of the General Ordinances (entitled Affirmative Action) and as required by Section 102.11 of the Standard Specifications.

SECTION 102.4 PROPOSAL

No bid will be accepted that does not contain an adequate or reasonable price for each and every item named in the Schedule of Unit Prices.

A lump sum bid for the work in accordance with the plans and specifications is required. The lump sum bid must be the same as the total amounts bid for the various items and it shall be inserted in the space provided.

All papers bound with or attached to the proposal form are considered a part thereof and must not be detached or altered when the proposal is submitted. The plans, specifications and other documents designated in the proposal form will be considered a part of the proposal whether attached or not.

A proposal submitted by an individual shall be signed by the bidder or by a duly authorized agent. A proposal submitted by a partnership shall be signed by a member/partner or by a duly authorized agent thereof. A proposal submitted by a corporation shall be signed by an authorized officer or duly authorized registered agent of such corporation, and the proposal shall show the name of the State under the laws of which such corporation was chartered. The required signatures shall in all cases appear in the space provided thereof on the proposal.

Each proposal shall be placed, together with the proposal guaranty, in a sealed envelope, so marked as to indicate name of project, the contract number or option to which it applies, and the name and address of the Contractor or submitted electronically through Bid Express (www.bidexpress.com). Proposals will be accepted at the location, the time and the date designated in the advertisement. Proposals received after the time and date designated will be returned to the bidder unopened.

The Bidder shall execute the Disclosure of Ownership form. REFER TO SECTION F.

SECTION 102.5: BID DEPOSIT (PROPOSAL GUARANTY)

All bids, sealed or electronic, must be accompanied with a Bid Bond equal to at least 5% of the bid or a Certificate of Annual/Biennial Bid Bond or certified check, payable to the City Treasurer. Bid deposit of the successful bidders shall be returned within forty-eight (48) hours following execution of the contract and bond as required.

PREVAILING WAGE RATES

Prevailing Wage Rates may be required and are attached in Section J of the contract. See Special Provisions to determine applicability.

Bidders for this Contract(s) must be Pre-Qualified for at least one of the following type(s) of construction denoted by an \boxtimes

<u>Buil</u>	ding Demolition				
101	☐ Asbestos Removal	110 Building Demolition			
120	House Mover				
. .					
Stre	et, Utility and Site Construction				
201	☐ Asphalt Paving	270 Retaining Walls, Reinforced Concrete			
205	☐ Blasting	275 🔲 Sanitary, Storm Sewer and Water Main			
210	Boring/Pipe Jacking	Construction			
215	☐ Concrete Paving	276 Sawcutting			
	Con. Sidewalk/Curb & Gutter/Misc. Flat Work	280 Sewer Lateral Drain Cleaning/Internal TV Insp.			
220		the state of the s			
221	Concrete Bases and Other Concrete Work				
222	Concrete Removal	290 Sewer Pipe Bursting			
225	☑ Dredging	295 🔲 Soil Borings			
230	☐ Fencing	300 🔲 Soil Nailing			
235	Fiber Optic Cable/Conduit Installation	305 Storm & Sanitary Sewer Laterals & Water Svc.			
240	☐ Grading and Earthwork	310 Street Construction			
	Horizontal Saw Cutting of Sidewalk	315 Street Lighting			
241		318 Tennis Court Resurfacing			
.242	Infrared Seamless Patching				
245	Landscaping, Maintenance	320 Traffic Signals			
250	□ Landscaping, Site and Street	325 🔲 Traffic Signing & Marking			
251	☐ Parking Ramp Maintenance	332 Tree pruning/removal			
252	Pavement Marking	333 Tree, pesticide treatment of			
255	Pavement Sealcoating and Crack Sealing	335 Trucking			
	Petroleum Above/Below Ground Storage	340 Utility Transmission Lines including Natural Gas,			
260		Electrical & Communications			
	Tank Removal/Installation	·			
262	Playground Installer	399 Other			
265	Retaining Walls, Precast Modular Units				
Brid	ge Construction				
501	☐ Bridge Construction and/or Repair				
Build	ding Construction				
401	Floor Covering (including carpet, ceramic tile installation,	437 Metals			
	rubber, VCT	440 Painting and Wallcovering			
400		445 Plumbing			
402	Building Automation Systems				
403	Concrete	450 Pump Repair			
404	☐ Doors and Windows	455 Pump Systems			
405	☐ Electrical - Power, Lighting & Communications	460 Roofing and Moisture Protection			
410	Elevator - Lifts	464 Tower Crane Operator			
412	Fire Suppression	461 Solar Photovoltaic/Hot Water Systems			
413	Furnishings - Furniture and Window Treatments	465 Soil/Groundwater Remediation			
		466 ☐ Warning Sirens			
415					
420	General Building Construction, \$250,000 to \$1,500,000	470 Water Supply Elevated Tanks			
425	☐ General Building Construction, Over \$1,500,000	475 Water Supply Wells			
428	Glass and/or Glazing	480 🔲 Wood, Plastics & Composites - Structural &			
429	Hazardous Material Removal	Architectural			
430	Heating, Ventilating and Air Conditioning (HVAC)	499 Other			
433	Insulation - Thermal				
435	☐ Masonry/Tuck pointing	$a \in \mathbb{N}$			
~	1 0				
Stat	e of Wisconsin Certifications				
1	☐ Class 5 Blaster - Blasting Operations and Activities 2500 feet	and closer to inhabited buildings for quarries, open pits and			
	road cuts.				
2	Class 6 Blaster - Blasting Operations and Activities 2500 feet	and closer to inhabited buildings for trenches, site			
_	excavations, basements, underwater demolition, underground	Lexicavations or structures 15 feet or less in height			
•	Class 7 Blaster - Blasting Operations and Activities for structure.	rea greater than 15 in height bridges towers and any of			
3					
	the objects or purposes listed as "Class 5 Blaster or Class 6 B	Blaster".			
4	☐ Petroleum Above/Below Ground Storage Tank Removal and	Installation (Attach copies of State Certifications.)			
5	Hazardous Material Removal (Contractor to be certified for as	bestos and lead abatement per the Wisconsin Department			
	of Health Services, Asbestos and Lead Section (A&LS).) See	the following link for application:			
	www.dhs.wisconsin.gov/Asbestos/Cert. State of Wisconsin Performance of Asbestos Abatement Certificate must be				
_	attached.	Verker as administered by the International Society of			
6	☐ Certification number as a Certified Arborist or Certified Tree V	volver as authinistered by the international society of			
	Arboriculture				
7	☐ Pesticide application (Certification for Commercial Applicator	For Hire with the certification in the category of turf and			
	landscape (3.0) and possess a current license issued by the I	DATCP)			
8	☐ State of Wisconsin Master Plumbers License.				
	—				

SECTION B: PROPOSAL

Please refer to the Bid Express Website at https://bidexpress.com look up contract number and go to Section B: Proposal Page

You can access all City of Madison bid solicitations for FREE at www.bidexpress.com

Click on the "Register for Free" button and follow the instructions to register your company and yourself. You will be asked for a payment subscription preference, since you may wish to bid online someday. Simply choose the method to pay on a 'per bid' basis. This requires no payment until / unless you actually bid online. You can also choose the monthly subscription plan at this time. You will, however, be asked to provide payment information. Remember, you can change your preference at anytime. You will then be able to complete your free registration and have full access to the site. Your free access does not require completion of the 'Digital ID' process, so you will have instant access for viewing and downloading. To be prepared in case you ever do wish to bid online, you may wish to establish your digital ID also, since you cannot bid without a Digital ID.

If you have any problems with the free registration process, you can call the bidexpress help team, toll free at 1-888-352-2439 (option 1, option1).

SECTION C: SMALL BUSINESS ENTERPRISE

Instructions to Bidders City of Madison SBE Program Information

2 Small Business Enterprise (SBE) Program Information

2.1 Policy and Goal

The City of Madison reaffirms its policy of nondiscrimination in the conduct of City business by maintaining a procurement process which remains open to all who have the potential and ability to sell goods and services to the City. It is the policy of the City of Madison to allow Small Business Enterprises (SBE) maximum feasible opportunity to participate in City of Madison contracting. The bidder acknowledges that its bid has been submitted in accordance with the SBE program and is for the public's protection and welfare.

Please refer to the "ADVERTISEMENT FOR BIDS" for the goal for the utilization of SBEs on this project. SBEs may participate as subcontractors, vendors and/or suppliers, which provide a commercially useful function. The dollar value for SBE suppliers or 'materials only' vendors shall be discounted to 60% for purposes of meeting SBE goals.

A bidder which achieves or exceeds the SBE goal will be in compliance with the SBE requirements of this project. In the event that the bidder is unable to achieve the SBE goal, the bidder must demonstrate that a good faith effort to do so was made. Failure to either achieve the goal or demonstrate a good faith effort to do so will be grounds for the bidder being deemed a non-responsible contractor ineligible for award of this contract.

A bidder may count towards its attainment of the SBE goal only those expenditures to SBEs that perform a commercially useful function. For purposes of evaluating a bidder's responsiveness to the attainment of the SBE goal, the contract participation by an SBE is based on the percentage of the total base bid proposed by the Contractor. The total base bid price is inclusive of all addenda.

Work performed by an SBE firm in a particular transaction can be counted toward the goal only if it involves a commercially useful function. That is, in light of industry practices and other relevant considerations, does the SBE firm have a necessary and useful role in the transaction, of a kind for which there is a market outside the context of the SBE Program, or is the firm's role a superfluous step added in an attempt to obtain credit towards goals? If, in the judgment of the Affirmative Action Division, the SBE firm will not perform a commercially useful function in the transaction, no credit towards goals will be awarded.

The question of whether a firm is performing a commercially useful function is completely separate from the question of whether the firm is an eligible SBE. A firm is eligible if it meets the definitional criteria and ownership and control requirements, as set forth in the City of Madison's SBE Program.

If the City of Madison determines that the SBE firm is performing a commercially useful function, then the City of Madison must then decide what that function is. If the commercially useful function is that of an SBE vendor / supplier that regularly transacts business with the respective product, then the City of Madison will count 60% of the value of the product supplied toward SBE goals.

To be counted, the SBE vendor / supplier must be engaged in selling the product in question to the public. This is important in distinguishing an SBE vendor / supplier, which has a regular trade with a variety of customers, from a firm which performs supplier-like functions on an <u>ad hoc</u> basis or for only one or two contractors with whom it has a special relationship.

A supplier of bulk goods may qualify as an eligible SBE vendor / supplier if it either maintains an inventory or owns or operates distribution equipment. With respect to the distribution equipment; e.g., a fleet of trucks, the term "operates" is intended to cover a situation in which the supplier leases the equipment on a regular basis for its entire business. It is not intended to cover a situation in which the firm simply provides drivers for trucks owned or leased by another party; e.g., a prime contractor, or leases such a party's trucks on an <u>ad hoc</u> basis for a specific job.

If the commercially useful function being performed is not that of a qualified SBE vendor / supplier, but rather that of delivery of products, obtaining bonding or insurance, procurement of personnel, acting as a broker or manufacturer's representative in the procurement of supplies, facilities, or materials, etc., only the fees or commissions will apply towards the goal.

For example, a business that simply transfers title of a product from manufacturer to ultimate purchaser; e. g., a sales representative who re-invoices a steel product from the steel company to the Contractor, or a firm that puts a product into a container for delivery would not be considered a qualified SBE vendor / supplier. The Contractor would not receive credit based on a percentage of the cost of the product for working with such firms.

Concerning the use of services that help the Contractor obtain needed supplies, personnel, materials or equipment to perform a contract: only the fee received by the service provider will be counted toward the goal. For example, use of a SBE sales representative or distributor for a steel company, if performing a commercially useful function at all, would entitle the Contractor receiving the steel to count only the fee paid to the representative or distributor toward the goal. This provision would also govern fees for professional and other services obtained expressly and solely to perform work relating to a specific contract.

Concerning transportation or delivery services: if an SBE trucking company picks up a product from a manufacturer or a qualified vendor / supplier and delivers the product to the Contractor, the commercially useful function it is performing is not that of a supplier, but simply that of a transporter of goods. Unless the trucking company is itself the manufacturer or a qualified vendor / supplier in the product, credit cannot be given based on a percentage of the cost of the product. Rather, credit would be allowed for the cost of the transportation service.

The City is aware that the rule's language does not explicitly mention every kind of business that may contribute work on this project. In administering these programs, the City would, on a case-by-case basis, determine the appropriate counting formula to apply in a particular situation.

2.2 Contract Compliance

Questions concerning the SBE Program shall be directed to the Contract Compliance Officer of the City of Madison Department of Civil Rights, Affirmative Action Division, 210 Martin Luther King, Jr. Blvd., Room 523, Madison, WI 53703; telephone (608) 266-4910.

2.3 Certification of SBE by City of Madison

The Affirmative Action Division maintains a directory of SBEs which are currently certified as such by the City of Madison. Contact the Contract Compliance Officer as indicated in Section 2.2 to receive a copy of the SBE Directory or you may access the SBE Directory online at www.cityofmadison.com/dcr/aaTBDir.cfm.

All contractors, subcontractors, vendors and suppliers seeking SBE status must complete and submit the **Targeted Business Certification Application** to the City of Madison Affirmative Action Division by the time and date established for receipt of bids. A copy of the Targeted Business Certification Application is available by contacting the Contract Compliance Officer at the address and telephone indicated in Section 2.2 or you may access the Targeted Business Certification Application online at www.cityofmadison.com/dcr/aaTBDir.cfm. Submittal of the Targeted Business Certification Application by the time specified does not guarantee that the applicant will be certified as a SBE eligible to be utilized towards meeting the SBE goal for this project.

2.4 Small Business Enterprise Compliance Report

2.4.1 Good Faith Efforts

Bidders shall take all necessary affirmative steps to assure that SBEs are utilized when possible and that the established SBE goal for this project is achieved. A contractor who self performs a portion of the work, and is pre-qualified to perform that category of work, may subcontract that portion of the work, but shall not be required to do so. When a bidder is unable to achieve the established SBE goal, the bidder must demonstrate that a good faith effort to do so was made. Such a good faith effort should include the following:

- 2.4.1.1 Attendance at the pre-bid meeting.
- 2.4.1.2 Using the City of Madison's directory of certified SBEs to identify SBEs from which to solicit bids.
- 2.4.1.3 Assuring that SBEs are solicited whenever they are potential sources.
- 2.4.1.4 Referring prospective SBEs to the City of Madison Affirmative Action Division for certification.
- 2.4.1.5 Dividing total project requirements into smaller tasks and/or quantities, where economically feasible, to permit maximum feasible SBE participation.
- 2.4.1.6 Establishing delivery schedules, where requirements permit, which will encourage participation by SBEs.
- 2.4.1.7 Providing SBEs with specific information regarding the work to be performed.
- 2.4.1.8 Contacting SBEs in advance of the deadline to allow such businesses sufficient time to prepare a bid.
- 2.4.1.9 Utilizing the bid of a qualified and competent SBE when the bid of such a business is deemed reasonable (i.e. 5% above the lowest bidder), although not necessarily low.
- 2.4.1.10 Contacting SBEs which submit a bid, to inquire about the details of the bid and confirm that the scope of the work was interpreted as intended.

2.4.2 Reporting SBE Utilization and Good Faith Efforts

The Small Business Enterprise Compliance Report is to be submitted by the <u>bidder</u> with the bid: This report is due by the specified bid closing time and date. Bids submitted without a completed SBE Compliance Report as outlined below

shall be deemed non-responsible and the bidder ineligible for award of this contract.

- 2.4.2.1 If the Bidder <u>meets or exceeds</u> the goal established for SBE utilization, the Small Business Enterprise Compliance Report shall consist of the following:
 - 2.4.2.1.1 **Cover Page**, Page C-6; and
 - 2.4.2.1.2 **Summary Sheet,** C-7.
- 2.4.2.2 If the bidder <u>does not meet</u> the goal established for SBE utilization, the Small Business Enterprise Compliance Report shall consist of the following:
 - 2.4.2.2.1 **Cover Page**, Page C-6;
 - 2.4.2.2.2 **Summary Sheet,** C-7; and
 - 2.4.2.2.3 **SBE Contact Report,** C-8 and C-9. (A <u>separate</u> Contact Report must be completed for <u>each applicable</u> SBE which is <u>not</u> utilized.)

2.5 Appeal Procedure

A bidder which does not achieve the established goal and is deemed <u>non-responsible</u> for failure to demonstrate a good faith effort to achieve such goal and subsequently denied eligibility for award of contract may, within 72 hours of receiving such notification, appeal that decision to a special appeals committee composed of three (3) members of the Affirmative Action Commission, three (3) members of the Board of Public Works and a seventh member appointed by the Mayor. All appeals must be made in writing to the City Engineer and <u>received</u> within 72 hours of City of Madison's notice. Postmark not applicable.

2.6 SBE Requirements After Award of the Contract

The successful bidder shall identify SBE subcontractors, suppliers and vendors on the subcontractor list in accordance with the specifications. The Contractor shall submit a detailed explanation of any variances between the listing of SBE subcontractors, vendors and/or suppliers on the subcontractor list and the Contractor's SBE Compliance Report for SBE participation.

No change in SBE subcontractors, vendors and/or suppliers from those SBEs indicated in the SBE Compliance Report will be allowed without prior approval from the Engineer and the Affirmative Action Division. The contractor shall submit in writing to the City of Madison Affirmative Action Division a request to change any SBE citing specific reasons which necessitate such a change. The Affirmative Action Division will use a general test of reasonableness in approving or rejecting the contractor's request for change. If the request is approved, the Contractor will make every effort to utilize another SBE if available.

The City will monitor the project to ensure that the actual percentage commitment to SBE firms is carried out.

2.7 SBE Definition and Eligibility Guidelines

A Small Business Enterprise is a business concern awarded certification by the City of Madison. For the purposes of this program a Small Business Enterprise is defined as:

- An independent business operated under a single management. The business may not be a subsidiary of any other business and the stock or ownership may not be held by any individual or any business operating in the same or a similar field. In determining whether an entity qualifies as a SBE, the City shall consider all factors relevant to being an independent business including, but not limited to, the date the business was established, adequacy of its resources for the work in which it proposes to involve itself, the degree to which financial, equipment leasing and other relationships exist with other ineligible firms in the same or similar lines of work. SBE owner(s) shall enjoy the customary incidents of ownership and shall share in the risks and profits commensurate with their enjoyment interests, as demonstrated by an examination of the substance rather than form or arrangements that may be reflected in its ownership documents.
- B. A business that has averaged no more than \$4.0 million in annual gross receipts over the prior three year period and the principal owner(s) do not have a personal net worth in excess of \$1.32 million.

Firm and/or individuals that submit fraudulent documents/testimony may be barred from doing business with the City and/or forfeit existing contracts.

SBE certification is valid for one (1) year unless revoked.

SECTION D: SPECIAL PROVISIONS

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

It is the intent of these Special Provisions to set forth the final contractual intent as to the matter involved and shall prevail over the Standard Specifications and plans whenever in conflict therewith. In order that comparisons between the Special Provisions can be readily made, the numbering system for the Special Provisions is equivalent to that of the Specifications.

Whenever in these Specifications the term "Standard Specifications" appears, it shall be taken to refer to the City of Madison Standard Specifications for Public Works Construction and Supplements thereto.

For this project, payment of prevailing wages (white sheet) shall be required unless the box indicating prevailing wages are not required is checked below.

Prevailing wages shall not be required when this box is checked.

PREVAILING WAGE

If prevailing wages (white sheets) are required, the wages and benefits paid on the contract shall not be less than those specified in the Prevailing Wage Determination included with these contract documents for the following types of work:

\boxtimes	Building or Heavy Construction
\boxtimes	Sewer, Water, or Tunnel Construction
\boxtimes	Local Street or Miscellaneous Paving Constructio
	Residential or Agricultural Construction

When multiple boxes are checked, worker's wages may vary according to the type and area of work performed. It is the responsibility of the Contractor to determine and apply the appropriate wage rate for the specific work assigned.

SECTION 102.12: BEST VALUE CONTRACTING

This Contract shall be considered a Best Value Contract if the Contractor's bid is equal to or greater than \$54,000 for a single trade contract; or equal to or greater than \$264,500 for a multi-trade contract pursuant to MGO 33.07(7).

ARTICLE 104: SCOPE OF WORK

This contract consists of dredging and stabilizing approximately 2000 linear feet of Wingra Creek. The project is located between the Union Pacific Railroad Bridge and Olin Avenue. Work for this project will also include constructing six littoral shelves in a meandering pattern.

In conjunction with this project, the Contractor shall excavate approximately 1700 cubic yards from the John Nolen Retention Pond. This work may be completed prior to, during, or after the channel work.

Following work on the channel and banks, the bike path on the northwest side of the channel will pulverized, shaped, and resurfaced.

The Contractor shall view all associated project sites prior to bidding to become familiar with the existing conditions. It will be the responsibility of the Contractor to work with the utilities located in the right of way to resolve conflicts during the construction process.

SECTION 102.10:

SECTION 105.1: AUTHORITY OF THE ENGINEER

The Engineer shall resolve all questions which arise as to the quality and acceptability of materials furnished, work performed, manner of performance, rate of progress of the work, interpretation of the plans and Specifications, acceptable fulfillment of the contract, compensation, and disputes and mutual rights between Contractors under the Specifications. The Engineer shall determine the amount and quantity of work performed and materials furnished.

All decisions of the Engineer shall, when so requested, be rendered in writing. They shall be final and conclusive in all matters unless within ten (10) days after such decision the Contractor applies in writing to the Board of Public Works for a review of such decision.

Any change proposed by a Contractor in SBE subcontractors, vendors or suppliers from those SBEs indicated on the SBE Compliance Report must be approved by the Engineer and the City's Manager of the Affirmative Action Division (hereafter, AAD). When requested, such decision shall be rendered in writing. Such decisions shall be final and conclusive in all matters unless within ten (10) days after such decision the Contractor or the affected SBE applies in writing to the Board of Public Works for a review of such decision.

In the event the Engineer and the AAD disagree over the proper decision to be made regarding an SBE, the Mayor shall appoint a third person to resolve the disagreement, within 30 days of appointment. The decision thus rendered may be reviewed by the Board of Public Works upon request of the Contractor or the affected SBE as set forth in Sections 105.1 and 105.2 of the City's standard specifications.

SECTION 105.12: COOPERATION BY THE CONTRACTOR

This contract provides the Contractor a significant window in which to complete the defined work. It is not intended that Contractor use the entire time provided. Rather, it is intended that the Contractor complete this work during favorable weather conditions and water levels. The Contractor will be allowed to suspend the project, if necessary, due to weather, channel, or permit conditions. However, for each shutdown required or requested, the Contractor shall provide a shut-down plan, which shall be submitted to the Project Engineer for approval.

The pedestrian bridge is rated to 10,000 lbs. The bridge shall not be used as access to the site, and shall be protected during the project.

The Contractor shall use care around existing trees, plantings, fences, abutments, and other features. Damage to these items during construction shall be repaired or replaced at the Contractor's expense. No trees, other than those shown on the plan or marked in the field shall be removed without the approval of the Engineer.

Several utilities exist on site. The Contractor shall perform a One Call through Digger's Hotline for each site at least three days prior to beginning construction. To ensure that Parks-owned utilities are also marked, include the park name at the beginning of the Marking Instructions field on the ticket, and send a copy of the ticket to the City of Madison Parks Surveyor, Dan Rodman (drodman@cityofmadison.com or (608) 266-6674).

SECTION 105.13: ORDER OF COMPLETION

The Contractor shall begin construction at the upstream project limits, near the Union Pacific Railroad bridge and progress downstream in an orderly manner. Work shall be completed as construction progresses downstream. Specifically, stone shall be placed on the banks as soon as possible following dredging. Littoral Shelves shall be completed individually, and as soon as possible following dredging. Topsoil, seeding, and matting shall occur immediately following littoral shelf construction.

Upland areas used for hauling and stockpiling, do not need to be stabilized until project work is complete, but shall be protected from erosion with silt sock, silt fence, polymer, or as directed by the Construction Engineer.

The Contractor shall submit for approval, a project schedule. If a shut-down is anticipated, the Contractor shall also submit a shut-down plan for approval.

Work can begin as soon as project permits are approved. Please contact Sally Swenson, the Project Engineer, for an updated permit schedule.

The Contractor may complete the John Nolen Retention Pond excavation separately from the channel work. The John Nolen Retention pond excavation shall be completed within the allowed contract time.

Permit stipulations require that no work be completed in the channel between March 15, 2015 and May 15, 2015. The Contractor may choose to work prior to March 15th, prepare the site for a shutdown, and finish at a later date. All proposed construction schedules shall be approved by the Project Engineer.

SECTION 107.7: MAINTENANCE OF TRAFFIC

All traffic control shall conform to Part VI of the Federal Highways Administration's "Manual on Uniform Traffic Control Devices" (MUTCD), the State of Wisconsin Standard Facilities Development Manual (including Chapter 16 – Standard Detail Drawings) and the City of Madison Standards for Sidewalk and Bikeway closures.

The Contractor shall submit an acceptable, complete Traffic Control Plan, including all necessary phases and any required sidewalk or bike route closures, to the office of the City Traffic Engineer, at 215 Martin Luther King Jr. Blvd. Suite 100, Madison, WI 53703, a minimum of five (5) working days prior to the preconstruction meeting. The Traffic Control Plan shall address all requirements of this section of the Special Provisions. The Contractor shall not start work on this project until the Traffic Engineering Division has approved a traffic control plan and traffic control devices have been installed, in accordance with the approved plan. Failure of the Contractor to obtain an approved Traffic Control Plan, as specified above, may prevent the Contractor from starting work and shall be considered a delay of the project, caused by the Contractor. Please contact Luke Peters at lpeters@cityofmadison.com or (608) 267-1969.

The Contractor will be responsible for installing and maintaining traffic control in accordance with the traffic control plan and as directed by the City Traffic Engineer. The Contractor shall install and maintain modifications or additions to the traffic control, as directed by the City Traffic Engineer, at no cost to the City.

The Contractor shall access the site from the bike path adjacent to Wingra Creek Parkway, on the northwest side of the channel, and from the park areas on the southeast side of the channel. The Contractor shall minimize and isolate traffic across the park path on the southeast side of Wingra Creek to minimize damage to the path.

For the majority of the project, bike traffic shall be rerouted to Wingra Creek Parkway. The Contractor shall provide a durable, smooth surface to transition between the existing path and Wingra Creek Parkway.

When working between Stations 0+00 and 2+00 on the northwest side of the channel, the Contractor shall provide a signed detour for the bike path, as shown on Sheet TC-1. The signed detour shall be limited to 30 days in duration and shall occur prior to April 1, 2015, unless the Contractor has an approved traffic control plan stating an alternative time frame.

Bike path traffic on the park path adjacent to Quann Soccer Fields and Quann Park shall be rerouted for the duration of the project. The Contractor shall provide a signed detour, as shown on Sheet TC-2.

The Contractor is permitted to close one lane of traffic on John Nolen Drive for the construction and removal of curb protection, in order to access the John Nolen Retention Pond site. Placement and removal of curb protection shall occur on a weekday during non-peak hours, between 9 am and 3 pm. All travel lanes on John Nolen Drive shall remain open at all other times. Additionally, the Contractor shall take all necessary precautions to keep the travel lanes on John Nolen Drive free of debris, rocks, or other project materials. The Contractor shall provide a traffic control plan for the lane closure on John Nolen Drive, which must be approved by Traffic Engineering prior to the start of work.

SECTION 107.8: NOTIFICATION WHEN CLOSING STREET

The Contractor shall not remove traffic signs. For removal or replacement of traffic and parking signs, contact the City of Madison Traffic Engineering Field Operations, 1120 Sayle Street, 266-4767, 8:00 a.m. to 4:00 p.m., a minimum of twenty-four (24) hours in advance of when any existing signs need to be removed. This service is provided free of charge. If the Contractor removes the signs, the Contractor will be billed for the reinstallation of, and any damage to, the signing equipment.

SECTION 107.13: TREE PROTECTION SPECIFICATIONS

The Contractor is advised to review Article 107.13 of the Standard Specifications for tree protection. Note that Articles 107.13(b) Curb Excavation and Installation, 107.13(c) Sidewalk Excavation and Installation, are not applicable to this project. Other sections are applicable except as provided below.

All trees shall be saved except those trees marked for removal on the plans. It is recognized that grading operations and root cutting of trees within the project limits may need to occur within 5 feet of trees in order to complete the work, but care must be taken in these areas. Roots shall be cut cleanly by using a saw, axe, lopping shears, chain saw, stump grinder, or other means which will produce a clean cut. Exposed roots shall be covered as soon as excavation is complete. The Contractor shall not rip or pull roots out towards the trunk of a tree while excavating with a backhoe. The use of a backhoe to cut roots is NOT acceptable. Grading within 5' of the trees within the construction area, if absolutely required, shall be minimized.

With regard to Article 107.13(f), pruning to accommodate construction equipment invading the tree crown may be done by the Contractor, with advance permission from the Construction Engineer. No pruning will be performed by City Forestry. All pruning shall be done according to ANSI A300 tree pruning specifications.

With regard to Article 107.14(g), no equipment or materials will be allowed to be parked on, or piled on areas within 5 feet of a tree. Construction traffic within 5 feet of a tree will be allowed only where necessary to complete grading operations, as described above, at the discretion of the Construction Engineer.

SECTION 108.2: PERMITS

The following permits have been applied for (each of the two projects has separate permits):

- 1. Army Corps of Engineers Permit for work in public waters -Non-Reporting permit
- 2. WI-DNR Chapter 30 Permit (Applied for but not yet received)
- 3. WI-DNR WRAPP Water Resources Application for Project Permit, formerly known as a Notice of Intent NOI) for construction site erosion control received
- 4. City of Madison Erosion Control and Stormwater Management Permit received

Contractor may not begin work until DNR Chapter 30 permit is received.

It shall be the responsibility of the Contractor to obtain the permits listed below, if required, and to pay all applicable charges and fees associated with these permits.

Wisconsin DNR Dewatering

All permit costs shall be considered incidental to the various Mobilization bid items for the Contract.

The Contractor shall meet the conditions of all permits and must keep a copy of each individual permit on site at all times throughout construction.

With regard to Control of Invasive or Exotic Species, the Chapter 30 permit will stipulate that any equipment or materials that may be in contact with invasive or exotic species must be decontaminated prior to and after work at the project site. It shall be the Contractor's responsibility to comply with decontamination requirements.

The Contractor shall meet the conditions of the permits involving including properly installing and maintaining the erosion control measures shown on the plans, specified in these Special Provisions, or as directed by the Construction Engineer or his designees. This work will be paid for under the appropriate bid items, or if appropriate items are not included in the contract, they shall be paid for as Extra Work.

The City's obtaining these permits is not intended to be exhaustive of all permits that may be required to be obtained by the Contractor for construction of this project. It shall be the responsibility of the Contractor to identify and obtain any other permits needed for construction.

SECTION 109.2: PROSECUTION OF WORK

The Contractor shall begin work on or before <u>January 15, 2015</u>. The contract completion date shall be <u>December 18, 2015</u>. This contract provides the Contractor a significant window in which to complete the defined work. It is not intended that Contractor use the entire time provided. Rather, it is intended that the Contractor complete this work during favorable weather conditions and water levels.

Work shall begin only after the start work letter is received. The Contractor shall limit workdays from 7:00 am to 7:00 pm, Monday through Saturday, unless approved by the Engineer in writing.

Permit stipulations prohibit work in the channel between March 15 and May 15. The Contractor may begin work prior to March 15, provided that a shut-down plan detailing the methods used to stabilize the site, is submitted to and approved by the Project Engineer. Work is permitted to occur in the areas outside of the ordinary high water mark between March 15 and May 15.

BID ITEM 10911: MOBILIZATION

DESCRIPTION

This item shall include all work necessary to mobilize and de-mobilize all equipment, personnel, and incidentals to all portions of this project, including Wingra Creek, Quann Soccer Fields, and the John Nolen Retention Pond.

If a shut-down is required to complete the project, costs associated with preparing a shut-down plan, closing the site for the duration of the shut-down, and re-mobilizing to resume project activities shall be included in this bid item.

METHOD OF MEASUREMENT

Mobilization shall be measured as a Lump Sum.

BASIS OF PAYMENT

Mobilization shall be measured as described above which shall be full compensation for all work, materials, and incidentals required to complete the work as described above.

BID ITEM 20201: E

EXCAVATION CUT

DESCRIPTION

Excavation Cut shall include all excavation from within the limits shown on the plans. Excavation cut shall be limited to the material generated from the John Nolen Retention Pond. All material generated from Wingra Creek shall be paid for via Bid Item 90033, Dredging.

Excavation shall be completed to the dimensions shown on Sheet P-7. This excavation is occurring to provide compensatory cut for fill occurring within the flood plain associated with construction of the littoral shelves. Therefore, it is unnecessary to meet exact grades and locations with this excavation. Survey verification of the excavation will not be required.

It is anticipated that the material generated in the excavation of the John Nolen Retention Pond will not be suitable for use as fill in littoral shelf construction. If topsoil quality soil is generated from this excavation, it may be used as topsoil in other areas of the project after approval from the Project Engineer or Construction Engineer.

The Contractor shall be responsible for determining a suitable off-site disposal location for excess excavated materials, and shall be responsible for hauling unsuitable material away from the site and for placement at the disposal site. This material shall be hauled in water-tight trucks.

A significant quantity of cattail is currently growing in the area of the proposed excavation. The removal of the vegetation is considered incidental to this bid tiem.

Any undercut or excavation directed by the Engineer beyond the limits shown on the plans shall be measured in the field and paid for as Excavation Cut.

Excavation

1700 cy

METHOD OF MEASUREMENT

Excavation Cut within the limits shown on the plans will be paid for based on the Cubic Yard as measured per truck. A uniform 6 percent bulking factor shall be applied to all excavated material; therefore, the Contractor shall remove 1802 cubic yards of material from the site. A per truck quantity will be mutually agreed upon by the Contractor, Construction Engineer, and Project Engineer at the preconstruction meeting.

BASIS OF PAYMENT

Excavation shall be paid for at the contract price for work as described and measured above which shall be full compensation for all labor, tools, equipment, and incidentals necessary to complete this item of work.

BID ITEM 20221:

TOPSOIL

DESCRIPTION

Work under this item shall include placement of topsoil within the seeding limits shown on the drawings or as directed by the Engineer in the field, in accordance with Section 202 of the Standard Specifications. Topsoil shall be placed on all disturbed areas, including on newly constructed littoral shelves, four (4) inches thick per the Standard Specifications. Topsoil materials and placement shall be in accordance with Article 202 – Fill.

Salvaged topsoil from on site meeting the specifications may be reused. In some areas the existing topsoil thickness may be adequate and no additional topsoil may be required; however, scarifying of the

existing topsoil may be required and shall be considered incidental to this bid item. If insufficient topsoil is available on site, the Contractor shall import topsoil.

This bid item is intended to accommodate all topsoil activities, including stripping, stockpiling, and replacing topsoil in the areas adjacent to Wingra Creek. Topsoil maintenance associated with dewatering the dredged materials and regrading of Quann Soccer Fields shall be paid under Bid Item 90004.

Topsoil shall not be stockpiled adjacent to the channel, or at elevations below 848 feet.

METHOD OF MEASUREMENT

Topsoil within the limits shown on the plan set shall be paid per Square Yard, based on "plan quantity" as shown in the contract without measurement thereof. The plan quantity was computed by measuring all areas between the bike path and channel, on both sides of the channel. Additionally, the Topsoil plan quantity includes the design dimensions of the littoral shelves, as topsoil is to be placed on the newly constructed shelves.

BASIS OF PAYMENT

Topsoil shall be paid at the contract price for work as described and measured above, which shall be full compensation for all labor, tools, equipment, and incidentals necessary to complete this item of work, including segregating, stockpiling, and preparing salvaged topsoil, furnishing topsoil from off-site as needed, placing, grading and raking finished surface.

BID ITEM 20401: CLEARING

DESCRIPTION

Work under this item shall include removal of trees indicated on the plans for removal. Prior to construction, trees will be marked in the field with pink paint by City Engineering. Tree sizes noted on the plans are approximate. Any questions or concerns about the removal of particular trees shall be brought promptly to the attention of the Engineer. Clearing shall be as described in the Standard Specifications except as noted below.

All clearing shall be done by sawing trees near the ground line. Under no circumstances is the Contractor permitted to pull trees from the ground or use methods which will significantly disturb existing root systems. Grubbing shall be done with stump grinding equipment, except as noted in Bid Item 20403.

Trees four (4) inches in diameter and smaller, shrubs, brush, windfalls, logs and other vegetation to be removed shall be paid separately under Bid Item 20405 - Brush Clearing. Contractor is strongly encouraged to visit the site prior to bidding in order to become familiar with site access and the quantity of tree removal.

Removal of large tree falls within Wingra Creek will be paid under this bid item.

The Contractor shall be responsible for the proper disposal of the material.

METHOD OF MEASUREMENT

Clearing will be measured per Inch Diameter, as set forth in the Standard Specifications.

BASIS OF PAYMENT

The contract unit price for Clearing per inch diameter shall be payment in full for furnishing all labor and equipment for all clearing actually performed, and for the handling and disposal of all debris resulting from clearing and grubbing.

BID ITEM 20403:

GRUBBING

DESCRIPTION

Work under this item shall include grubbing following removal of trees indicated on the plans for removal, including the trees marked for removal to provide an access route to the John Nolen Retention Pond. Tree sizes noted on the plans are approximate. Only stumps that directly interfere with channel dredging or creek bank grading shall be excavated. All other stumps shall be ground with stump grinding equipment, or cut within 2 inches of the ground surface and treated with an appropriate herbicide. Herbicide application shall occur in accordance with the manufacturer's recommendations and the City of Madison Policy Regarding Pest Management on City Property. The Contractor shall submit for approval documentation of the type of herbicide, along with the MSDS, to the Project Engineer prior to the start of tree removal. Herbicides containing Triclopyr, Glyphosphate, or similar chemicals are recommended. Herbicides containing Picloram will not be approved.

Under no circumstances is the Contractor permitted to pull trees from the ground or use methods which will significantly disturb existing root systems, except as noted above.

Fill required to backfill holes where stumps are removed shall be considered incidental to this bid item.

Trees four (4) inches in diameter and smaller, shrubs, brush, windfalls, logs and other vegetation to be removed shall be paid separately under Bid Item 20405 - Brush Clearing.

METHOD OF MEASUREMENT

Grubbing will be measured per Inch Diameter, as set forth in the Standard Specifications.

BASIS OF PAYMENT

The contract unit price for Grubbing per inch diameter shall be payment in full for furnishing all labor, equipment, and incidentals necessary to excavate, grind, or treat stumps remaining from clearing activities.

BID ITEM 20405:

BRUSH CLEARING

DESCRIPTION

This item shall include clearing of all brush, trees 4 inches in diameter or smaller, fallen logs, debris, and herbaceous vegetation within the grading limits. The Contractor is strongly encouraged to visit the site prior to bidding in order to become familiar with site access and the quantity of brush removal.

Brush clearing shall consist of removing all unmarked small trees, brush, shrubs, and herbaceous vegetation and completely removing them from site. Smaller trees and brush shall be removed within 1 inch below proposed finished grades. Any fill required to backfill holes where stumps are removed shall be considered incidental to this bid item. All clearing shall be done by sawing brush near the ground line. Under no circumstances is the Contractor permitted to pull trees from the ground or use methods which will significantly disturb existing root systems.

This item shall include removal of windfalls, debris, and logs present within the work area. This item shall also include any trimming of trees and brush by contractor to facilitate access, where approved by the Construction Engineer.

The Contractor shall be responsible for the proper disposal of the material.

METHOD OF MEASUREMENT

This item shall be measured as a Lump Sum.

BASIS OF PAYMENT

This work, measured as provided above, will be paid for at the contract price which shall be considered full compensation for furnishing all labor and equipment for all brush clearing performed, and for the handling and disposal of all debris resulting from brush clearing.

BID ITEM 21061:

EROSION MATTING CLASS 1 - URBAN TYPE A

DESCRIPTION

Work under this bid item shall include provision and installation of Class I Urban Type A Erosion Control Revegetative Mat (ECRM). Class I, Urban Type A matting shall be placed on all disturbed areas above the ordinary high water mark adjacent to Wingra Creek. Littoral shelves will be stabilized with Erosion Matting, Class II Type C – Organic matting.

Class I Urban Type A matting shall be placed on all restored haul routes between Wingra Creek and Quann Soccer Fields, but shall be considered incidental to Bid Item 90033, Dredging.

METHOD OF MEASUREMENT

Erosion Matting Class I, Urban Type A within the limits shown on the plan set shall be paid per Square Yard, based on "plan quantity" as shown in the contract without measurement thereof. The plan quantity was computed by measuring all areas between the bike path and existing channel bank, on both sides of the channel. The Contractor shall perform their own calculations to provide additional material necessary for overlapping seams, etc.

BASIS OF PAYMENT

Erosion Matting Class I – Urban Type A shall be paid at the contract price for work as described and measured above, which shall be full compensation for all labor, tools, equipment, and incidentals necessary to provide and install the matting in accordance with manufacturer's recommendations.

BID ITEM 21073:

EROSION MATTING CLASS II, TYPE C - ORGANIC

DESCRIPTION

Work under this bid item shall include provision and installation of Class II, Type C - Organic Erosion Control Revegetative Mat (ECRM). Class II, Type C - Organic matting shall be used in two locations during construction of the littoral shelves. First, Class II matting shall be placed between the existing creek bed and fill material. In this application, Dekowe 900 or GeoCoir 900 shall be selected from the Product Acceptability List. These materials were chosen because they have a smaller weave and are 100% biodegradable. An alternate material that meets these criteria may be proposed for this location, subject to the approval of the Project Engineer.

Class II, Type C – Organic matting shall also be placed over the newly constructed littoral shelves. The Contractor shall toe the Class II matting into the fill material, immediately behind the stone bank stabilization material, in order to provide a stable anchorage for the matting. Class II matting will stop at the edge of the existing bank, and will transition to Class I, Urban Type A matting.

METHOD OF MEASUREMENT

Erosion Matting Class II, Type C - Organic shall be paid per Square Yard, based on "plan quantity" as shown in the contract without measurement thereof. The plan quantity was computed by measuring the approximate design area of the littoral shelves. The Contractor shall perform their own calculations to provide additional material necessary for overlapping seams, etc.

BASIS OF PAYMENT

Erosion Matting Class II, Type C - Organic shall be paid at the contract price for work as described and measured above, which shall be full compensation for all labor, tools, equipment, and incidentals necessary to provide and install the matting in accordance with manufacturer's recommendations.

BID ITEM 90001 - TEMPORARY FENCING

DESCRIPTION

This item includes installation of temporary construction fencing at the locations shown on the drawing, or as directed in the field by the Construction Engineer. The intent of this item is to delineate the area to which the Contractor shall confine their operations, to protect trees, and to direct the public away from construction areas. Minor relocation of fencing may be required as the work progresses. No extra payment shall be made for temporarily opening and re-closing the fence, or minor relocation of the fencing as needed to perform the work.

Construction fencing shall be International Orange color, high-density polyethylene mesh conforming to the following:

- Mesh opening: 1 inch min to 3 inch max
- Height: 4 feet
- Ultimate tensile strength: Avg 3000 lb per 4' width (ASTM D638)

Posts shall be conventional metal "T" or "U" shaped posts. Fencing shall be installed according to the manufacturer's recommendations.

METHOD OF MEASUREMENT

Temporary fencing shall be measured per Linear Foot installed, maintained, and removed in the field.

BASIS OF PAYMENT

Cost for temporary fencing shall be paid at the contract unit price. Price shall include payment for providing and installing temporary fence and appurtenances, maintenance of fencing as required, creating and closing temporary openings as needed, and removal of fencing and appurtenances, including furnishing all labor, tools, equipment, and incidentals necessary to perform the work.

BID ITEM 90002 - CONSTRUCTION SURVEYING

DESCRIPTION

The Contractor shall be responsible for setting and verifying all grades within the dredge area in Wingra Creek, for the construction of the littoral shelves in accordance with the plan set, and for recording the final grades of the regraded Quann Soccer Fields.

The Contractor shall be responsible for configuring the Microstation file to a usable format in order to create nodes, alignments, or other useful data to facilitate surveying and staking.

The Contractor shall use the established horizontal and vertical control points as provided by the City of Madison. The Contractor shall run a level circuit for the project in order to check for accuracy. If GPS is used to establish vertical and horizontal control, the Contractor shall provide a check on accuracy by checking established control locations. If vertical control is established using GPS, the vertical control must be distributed across the site using conventional level circuits.

The vertical datum for this project is National Geodetic Vertical Datum of 1988, 2007 revision.

City Engineering will provide control points and will be checking accuracy to provide quality control.

METHOD OF MEASUREMENT

Construction Surveying shall be measured as a Lump Sum for work completed in the field.

BASIS OF PAYMENT

Construction Surveying shall be measured as described above and shall be paid at the contract unit price, which shall constitute full compensation for all work, materials, and incidentals required to complete the work defined in this bid item.

BID ITEM 90003 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD

DESCRIPTION

Work under this bid item shall include the removal and replacement of beam guard along John Nolen Drive, in order to accommodate access to the John Nolen Retention Ponds. The Contractor may salvage the existing beam guard, provided the materials are in good condition both before after removal. The Construction Engineer shall approve the reuse of all materials. The Contractor need only remove sufficient beam guard to provide access for their equipment.

If existing beam guard cannot be salvaged, the Contractor shall provide sufficient and acceptable materials for replacement of the beam guard. Material provision, as necessary, shall be considered incidental to this bid item.

The beam guard shall be replaced in accordance with Wisconsin DOT Standard Detail Drawing 14 B 15-8, or to match existing conditions.

The current Standard Detail Drawing can be found here:

http://roadwaystandards.dot.wi.gov/standards/fdm/SDD/14b15.pdf#1

METHOD OF MEASUREMENT

Remove and Replace Steel Plate Beam Guard shall be measured per Linear Foot of beam guard removed and replaced in the field.

BASIS OF PAYMENT

Remove and Replace Beam Guard shall be measured as described above and shall be paid at the contract unit price, which shall constitute full compensation for all work, materials, and incidentals required to complete the work defined in this bid item.

BID ITEM 90004 - QUANN SOCCER FIELD TOPSOIL AND SEEDING

DESCRIPTION

Work under this bid item shall include all labor, equipment, materials, and incidentals necessary to strip the existing topsoil from within the grading limits at Quann Soccer field. The topsoil shall be shaped into a stable berm and seeded with No Mow Turf seed mix as defined Article 207 of the Standard Specifications. The seeding shall be completed in accordance with Article 207, including the use of fertilizer and a cover crop, if necessary. Mulching is not necessary for the topsoil berm.

The topsoil berm shall be maintained in good condition for the duration of the project.

After the dredged materials have been graded in accordance with the plans, the topsoil shall be redistributed over all disturbed areas, seeded, fertilized, and matted with straw mulch. The final seeding

Rev. 07/11/2014-6832specs.doc D-11

for the Quann Soccer Fields shall be completed using Sun Terrace Seed Mix in accordance with Article 207 of the Standard Specifications. The Contractor shall note that seeding and placement of the stockpiled topsoil shall be included with this bid item and will not be paid for per the square yard, as is customary on City projects. Prior to seed placement, City Parks shall approve final grading. The Contractor shall contact Richard Bergmann at (608) 513-3567 and have Mr. Bergmann inspect the site.

METHOD OF MEASUREMENT

Quann Soccer Field Topsoil and Seeding shall be measured as a Lump Sum.

BASIS OF PAYMENT

Quann Soccer Field Topsoil and Seeding shall be measured as described above and shall be paid at the contract unit price, which shall constitute full compensation for stripping, stockpiling, temporary seeding, and replacing topsoil on the Quann Soccer Fields. Final seeding and mulching shall be included with this bid item.

BID ITEM 90005 - CHAIN LINK FENCE

DESCRIPTION

This bid item shall include all work, materials, labor, and incidentals required to install new chain link fence along the southwest boundary of the dog park adjacent to Wingra Creek, as shown on the plan set. The chain link fence shall be installed accordance with the detail shown on Sheet D-2. The fence is being removed solely to facilitate construction access. The Contractor may choose to not remove the fence, or salvage any portion of the existing fence. If removed, the fence shall be re-installed in exactly the same configuration as currently exists, including the size and location of the gate. The Construction Engineer shall approve the condition of all reused materials.

METHOD OF MEASUREMENT

Chain Link Fence shall be measured by the Linear Foot of fence installed in the field.

BASIS OF PAYMENT

Chain Link Fence shall be measured as described above and shall be paid for at the unit price, which shall be considered full compensation for furnishing, hauling, stockpiling as needed, and placing the fence and gate. This shall include all equipment, tools, labor, and incidentals necessary to complete the work as set forth in this description.

BID ITEM 90006 - SEEDING - WETLAND EMERGENT

DESCRIPTION

Work under this bid item shall include provision and placement of the seed mix defined below at the locations shown in the plan set. It is the intent that Wetland Emergent seed mix be placed on the portion of littoral shelf (a 10-12 foot strip, approximately) that is immediately adjacent to the channel. Seeding shall be completed in accordance with Article 207 of the Standard Specifications, including the use of fertilizer, polymer, and a cover crop if necessary. Following seeding, the site shall be stabilized with erosion control matting, which shall be paid separately under the appropriate bid item.

The seed mix, as defined below, was provided by Agrecol in Madison, Wisconsin (608-223-3571). The Contractor may choose to use an alternate supplier, but shall submit the seed mix and supplier contact information to the Project Engineer for approval.

Wetland Emergent Seed Mix		• .
4.00 PLS lbs/acre		
113.00 PLS seeds/square foot		
Wildflowers		oz/acre
Acorus calamus	Sweet Flag	5.00
Alisma subcordatum	Common Water Plantain	2.00
Iris virginica	Blue Flag Iris	3.50
Mimulus ringens	Monkey Flower	0.20
Sagittaria latifolia	Arrowhead	2.00 _
Sparganium Eurycarpum	Gian Bur-Reed	6.00
Grasses, Sedges & Rushes		oz/acre
Calamagrostis canadensis	Blue Joint Grass	1.25
Carex Comosa	Bristly Sedge	5.00
Carex crinita	Fringed Sedge	2.00
Carex hystericina	Porcupine Sedge	5.00
Glyceria Grandis	Reed Manna Grass	3.00
· Glyceria striata	Fowl Manna Grass	2.00
Juncus effusus	Common Rush	0.30
Leersia oryzoides	Rice Cut Grass	4.00
Scirpus acutus	Hard-Stemmed Bulrush	1.00
Scirpus atrovirens	Dark-Green Bullrush	2.00
Scirpus cyperinus	Wool Grass	0.75
Scirpus fluviatilis	River Bullrush	2.50
Scirpus pendulus	Red Bullrush	1.00
Scirpus validus	Sotf-Stem Bullrush	2.50
Spartina pectinata	Prairie Cord Grass	13.00

METHOD OF MEASUREMENT

Seeding – Wetland Emergent within the limits shown on the plan set shall be paid per Square Yard, based on "plan quantity" as shown in the contract without measurement thereof.

BASIS OF PAYMENT

Seeding – Wetland Emergent shall be measured as described above and shall be paid at the contract unit price, which shall constitute full compensation for provision and placement of seed as defined in this section and Article 207 of the Standard Specifications.

BID ITEM 90007 - SEEDING - FLOOD PLAIN

DESCRIPTION

Work under this bid item shall include provision and placement of the seed mix defined below at the locations shown in the plan set. It is the intent that Flood Plain seed mix be placed in the transition zone between the ordinary high water mark and the Wetland Emergent seed zone. Seeding shall be completed in accordance with Article 207 of the Standard Specifications, including the use of fertilizer, polymer, and a cover crop if necessary. Following seeding, the site shall be stabilized with erosion control matting, which shall be paid separately under the appropriate bid item.

The seed mix, as defined below, was provided by Agrecol in Madison, Wisconsin. The Contractor may choose to use an alternate supplier, but shall submit a seed mix to the Project Engineer for approval.

Flood Plain Seed Mix		
8.00 PLS lbs/acre		
82.00 PLS seeds/square foot		
Wildflowers		oz/acre
Alisma subcordatum	Common Water Plantain	1.00
Asclepias incarnata	Marsh Milkweed	- 3.00
Aster novae-angliae	New England Aster	1.00
Aster puniceus	Red-Stemmed Aster	1.00
Eupatorium maculatum	Spotted Joe Pye Weed	1.00
Eupatorium perfoliatum	Boneset	0.50
Helenium autumnale	Sneezeweed	0.30
Helianthus grosseserratus	Saw-Tooth Sunflower	0.50
Liatris spicata	Marsh Blazing Star	3.00
Lobelia cardinalis	Cardinal Flower	0.30
Lobelia siphilitica	Great Blue Lobelia	0.35
Pycnanthemum virginianum	Mountain Mint	0.50
Rudbeckia laciniata	Wild Golden Glow	3.00
Silphium perfoliatum	Cupplant	4.00
Solidago riddellii	Riddell's Goldenrod	4.00
Verbena hastata	Blue Vervain	2.00
Venonia fasciculata	Ironweed	4.00
Zizia aurea	Golden Alexanders	4.00
Grasses, Sedges & Rushes		oz/acre
Bromus ciliatus	Fringed Brome	24.00
Carex vulpinoidea	Brown Fox Sedge	4.00
Elymus riparius	River Bank Wild Rye	30.00
Elymus virginicus	Virginia Wild Rye	24.00
Glyceria grandis	Reed Manna Grass	2.00
Leersia oryzoides	Rice Cut Grass	2.00
Scirpus atrovirens	Dark-Green Bullrush	1.00
Scirpus cyperinus	Wool Grass	0.25
Scirpus fluviatilis	River Bullrush	3.00
Scirpus validus	Soft-Stemmed Bullrush	0.30
Spartina pectinata	Prairie Cord Grass	4.00

METHOD OF MEASUREMENT

Seeding – Flood Plain within the limits shown on the plan set shall be paid per Square Yard, based on "plan quantity" as shown in the contract without measurement thereof.

BASIS OF PAYMENT

Seeding – Flood Plain shall be measured as described above and shall be paid at the contract unit price, which shall constitute full compensation for provision and placement of seed as defined in this section and Article 207 of the Standard Specifications.

BID ITEM 90008 - ASPHALT PATH REPAIR (PARK)

DESCRIPTION

Work under this bid item shall include all labor, materials, equipment, and incidentals necessary to repair the asphalt path within Quann Park. It is anticipated that the bike path on the northwest side of the channel will be significantly damaged during construction and will, therefore, be resurfaced. That work is not included in this bid item and will be paid separately. For the most part, the asphalt path within the park (on the southeast side of the channel) can and should be avoided, with the exception of defined crossing areas. This bid item is intended to accommodate repair of the path in locations where repeated crossing occurs. The Contractor shall designate the specific locations to which the path crossing will be limited. The Construction Engineer shall approve all asphalt repair in the park path.

The Contractor shall sawcut the existing pavement at the outer limits of damage and remove the asphalt between the sawcuts. The Contractor shall properly dispose of the removed asphalt.

The Contractor shall import, place, and compact 6 inches of crushed aggregate base course. Three inches of HMA Pavement Type E-0.3 shall be imported and placed in accordance with Section 4 of the Standard Specifications. Compaction with a hand compacter will be acceptable for these repairs.

Path dimensions shall match the existing path. Approximately 0.4 tons of asphalt is estimated for this repair.

METHOD OF MEASUREMENT

Asphalt Repair shall be measured per Square Yards of asphalt repair made in the field.

BASIS OF PAYMENT

Asphalt Repair shall be measured as described above and shall be paid for at the contract unit price, which shall be considered full compensation for sawcutting and removing existing asphalt, importing and placing 6 inches of crushed aggregate base course, and importing and placing 3 inches of HMA Pavement Type E-0.3.

BID ITEM 90030 - STORM/STREAM CONTROL

DESCRIPTION

Work under this item shall include all work, materials, equipment, and incidentals required to control wet and dry weather flow in the channel, from the adjacent storm sewers, and within John Nolen Drive Retention Pond excavation area. The Contractor shall expect water to be present in Wingra Creek at all times. This channel is heavily influenced by the water levels in Lake Monona. Therefore, if the lake level is high, the Contractor shall expect the creek level to be elevated and remain elevated. The Contractor shall take all necessary steps to protect the new structures and channels from damage during construction and to accommodate the existing flows during construction.

This item includes all storm control necessary for all aspects of the Construction. This item is not for control of groundwater.

METHOD OF MEASUREMENT

Storm Control shall be measured as a Lump Sum for all storm control necessary throughout construction.

BASIS OF PAYMENT

Storm Control will be paid for at the contract sum price, which shall be full compensation for all work as provided in the description.

BID ITEM 90031 - SILT CURTAIN

DESCRIPTION

Work under this bid item shall include all work, labor, materials, and incidentals necessary to provide, install, maintain, and remove Silt Curtain in accordance with these special provisions and Wisconsin DNR Conservation Practice Standard 1070, which is attached to these special provisions.

Three layers of silt curtain shall be installed immediately downstream of the project area. The layers of silt curtain shall be between 10 and 15 apart. The curtain shall be installed in a manner that allows water to overtop each layer of curtain in the center of the channel. Please see the detail on Sheet D-2.

Silt Curtain shall be installed perpendicular to flow in Wingra Creek and shall be continuous between opposite banks. The installation shall be free of tears and gaps. Where Silt Curtain installations intersect the creek bank, the Contractor shall minimize gapping.

If a project shut-down occurs, the silt curtain shall be removed from the channel. It shall be reinstalled when work at the site resumes. The Contractor shall be compensated for both installations.

METHOD OF MEASUREMENT

Silt Curtain shall be measured as per Linear Foot of Silt Curtain installed, maintained, and removed in the field. Installations of salvaged Silt Curtain material will be paid as new material, provided it meets the original specifications.

BASIS OF PAYMENT

Silt Curtain shall be measured as described above and shall be paid for at the contract unit price, which shall be considered full compensation for providing, installing, maintaining, and removing Silt Curtain as described above.

BID ITEM 90032 - LIGHT RIPRAP - GLACIAL FIELD STONE

DESCRIPTION

This item includes all work, materials, labor, and incidentals required to provide and install glacial field stone as shown in the plan set and described in these Special Provisions. The stone shall meet the size requirements defined below and shall be comprised of rounded, durable, non-sedimentary material that is not susceptible to freeze-thaw degradation. The stone shall meet the following size requirements:

D50 Median Stone Size	% of Material Smaller than Typical Stone	Typical Stone Equivalent Diameter (Inches)
	70-100	12
•	50-70	9
9	35-50	6
	2-10	4

The Light Riprap Glacial Field Stone shall be placed a minimum of 12 inches deep.

The stone shall be placed on the channel banks after dredging has been completed in the immediate area and shall be placed at a slope of approximately 3:1. The stone shall be underlain with non-woven geotextile fabric. The fabric shall be paid separately under Bid Item 20140.

Rev. 07/11/2014-6832specs.doc D-16

METHOD OF MEASUREMENT

Light Riprap Glacial Field Stone shall be measured per Ton of stone placed in the field. All tickets shall be presented to the City representative on the project within twenty-four (24) hours after delivery of the materials to the project.

BASIS OF PAYMENT

Light Riprap Glacial Field Stone shall be measured as described above and shall be paid for at the contract unit price, which shall be considered full compensation for furnishing, hauling, stockpiling as needed, and placing the material, including all equipment, tools, labor and incidentals necessary to complete the work as set forth in the description.

BID ITEM 90033: DREDGING

DESCRIPTION

Work under this item shall include dredging of sediments from Wingra Creek in the locations shown on the plan set. The Contractor shall submit for approval a dredging and sediment transport plan prior to beginning work in Wingra Creek. Mechanical dredging will be considered an acceptable methodology. The intent of the dredging is to remove sediment accumulated from storm water runoff and sloughing of the stream bank. The Contractor shall remove sediment to an elevation of 841.00.

Regardless of dredging methodology, all material shall be hauled, pumped, or transported to the Quann Soccer Fields, which are southwest of the Quann Dog Park and shown on Sheet O-1 and P-6. Dredged materials that are hauled on city streets shall be transported using water-tight, sealed trucks. Dredged materials hauled on City Park land do not need to be transported in sealed trucks. Dredged materials shall be allowed to dewater in-place within the soccer fields until they are dry enough to be graded to the approximate lines and grades shown on the drawings using standard construction equipment. All work required for dewatering shall be paid under Bid Item 90034.

Dredged material generated between Stations 0+50 and 2+00 is contaminated with low-level polychlorinated biphenyl (PCB) concentrations. This material shall be segregated from all other material generated during dredging activities. It does not need to be contained, rather segregated to ensure an ultimate burial depth of 2 feet or greater during final grading of the Quann Soccer Field.

If trash is encountered in the dredging process, it shall be segregated and properly disposed of by the Contractor. Managing any large trash shall be considered incidental to this bid item.

Final grading of the dredged materials, following dewatering, shall be included in this bid item. Grading shall be completed in accordance with the grading plan shown on Sheet P-6.

All costs related to dredging and grading the channel banks to a 3:1 slope, regardless of method used, shall be included with this bid item. No separate payment shall be made for facilitating access, temporary fills, barges, etc. The Contractor may elect to accomplish dredging by placement of temporary fill in locations

All labor, equipment, materials, and incidentals necessary to restore haul routes between Wingra Creek and Quann Soccer Fields shall be considered incidental to this bid item. This includes final grading of haul routes, topsoiling, seeding, and mulching disturbed areas. Straw mulch will be permitted in restoration locations outside of the grading limits shown on Sheets P-1 through P-4. Seed used outside of the grading limits shown on Sheets P-1 through P-4 shall be Sun Terrace Seed Mix, which shall be placed in accordance with Article 207 of the Standard Specifications.

If the Contractor chooses to use the Quann Park asphalt path as a haul route, damage to the path shall be repaired, or the path resurfaced, as part of this bid item.

METHOD OF MEASUREMENT

Dredging shall be paid per Cubic Yard of material removed from Wingra Creek. This item may be measured per the plan quantity, which was determined from cross-sectional areas. Alternatively, the Contractor may choose to measure the volume by survey. The final volume shall be computed by determining the difference between the original ground surface and the final surface. The Contractor shall be responsible for gathering the final survey of Quann Soccer Field, which shall be checked by City Surveyors.

BASIS OF PAYMENT

Dredging shall be measured as defined above, and shall be paid for at the contract unit price, which shall be considered full compensation for all work, materials, equipment, and incidentals necessary to dredge Wingra Creek to the lines and grades defined in the plan set, to haul the dredged material to Quann Soccer Field, to final grade the dewatered sediment, and to repair and restore all haul routes between Wingra Creek and Quann Soccer Field.

BID ITEM 90034 - DEWATERING (DREDGED MATERIAL)

DESCRIPTION

Dredged materials shall be allowed to dewater in place within the Quann Soccer Fields grading limits, as shown on Sheet P-6, until they are dry enough to be graded to the approximate lines and grades shown on the drawings using standard earth moving equipment.

Dredged materials may require "working" in order for full dewatering to occur. This bid item includes any and all work required to facilitate dewatering of dredged materials, including but not limited to any temporary grading, disking, raking, or multiple handling of dredged materials that may be necessary for drying. The Contractor shall provide a dewatering plan to the Project Engineer for approval one week prior to commencing dredging activities.

Dredged material generated between Stations 0+50 and 2+00 shall remain segregated for the duration of dewatering activities to ensure an ultimate burial depth of 2 feet or deeper during final grading.

Final grading of dredged materials following dewatering shall be paid under Bid Item 90033, Dredging.

METHOD OF MEASUREMENT

Dewatering shall be measured as a Lump Sum for all dewatering activities.

BASIS OF PAYMENT

Dewatering, as measured above, shall be paid at the contract unit price, which shall constitute full compensation for all labor, equipment, materials, and incidentals necessary to complete dewatering activities for the materials dredged from Wingra Creek, as described above.

BID ITEM 90035 - STEPPED STONE REVETMENT (STATION 1+25)

DESCRIPTION

Work under this item shall include all work, materials, labor and incidentals necessary for the Contractor to provide and install 10 linear feet of Stepped Stone Revetment at Station 1+25 in accordance with the Specification that follows, and as shown on Sheet D-1. Filter Fabric and Clear Stone to be used in the revetment installation shall be paid separately, under Bid Items 20140 and 20217, respectively.

CONSTRUCTION METHODS

The Stepped Stone Revetment shall be constructed as shown in the plan set. A suitable foundation, as approved by the Engineer shall be provided to preclude settlement. Filter Fabric shall be installed under the bed, as shown on the drawings. Clear stone and filter fabric shall be installed according to the Standard Specifications. Each stone step shall be firmly set with no rocking or tipping, providing a firm foundation for subsequent layers. Cut stone blocks shall be field cut as required to fit tightly to abutting structures.

- 1. The stepped stone revetment shall be placed by equipment on the surfaces and to the depths specified on the drawings.
- 2. Stone shall be placed tightly together such that at least 60% of all joined faces are in direct contact and no more than 1.5-inch gap exists at any point along the joint. Vertical seams shall be staggered. Chiseling or cutting of the stone may be needed. Any costs for working the stone shall be included in the prices bid.
- 3. The finished surface aesthetic is critical. The stone layers shall follow the requirements noted on the plan. The tread width shall be consistent along each elevation and the stones shall fit snugly together and have no gaps larger than 1.5-inch. Working of stone faces may be required to achieve desired tolerances.
- 4. The intention of the above tolerances is that the work will be generally built to the required elevation, slopes and grades, and that the outer surfaces shall present a neat and aesthetic appearance. Placed material not meeting these intentions shall be removed and/or reworked to the satisfaction of the Owner's Representative. The Contractor is encouraged to look at a similar application of stone steps along the shoreline of Lake Mendota in front of the boathouse at James Madison Park.

QUALITY CONTROL

- A. Stone Quality and Gradation
 - 1. The Contractor is responsible for, and shall establish and maintain, quality control for all work performed at the quarry and at the job site to ensure compliance with the specifications.
 - 2. The Contractor shall provide a quarry inspector for all stepped stone. The inspector's responsibilities shall include, but not be limited to:
 - a. A visual test shall be made at the quarry for elongation, cracks, deterioration and other defects visible to the naked eye on at least two-thirds of the surface area of the stone. Ten percent of the stone checked for cracks shall be wetted and reinspected for minute cracks to determine if they would be detrimental to the stone quality and if additional inspections are necessary on all stone. Stones with cracks that are detrimental to a long-lasting product shall not be shipped to the project site.
 - b. Quarry representative shall pick stones of similar height dimensions for each layer. Stones shall have face and sides perpendicular to each other or angles that will match adjacent stone to achieve a tight fit. Stones intended for each layer shall be marked on the back to identify exact location in the finished work.
 - 3. The Owner's Representative reserves the right to inspect the quarry operations at any time to check for compliance to the specifications.
 - 4. All Stepped Stone shall be produced from the same quarry.

B. Test Section

General

a. The initial stepped stone revetment section will be considered as a test section. The purpose of the test sections will be to establish an in-the-field standard, built in accordance with the requirements of the contract documents, to which the remainder of the stepped stone revetment shall be constructed. The Contractor will make whatever modifications are necessary to placement procedures such that this standard will be achieved consistently during construction of the remainder of the revetment.

2. Execution

- a. The Contractor shall lay out the work, provide any survey control as needed for control of the work beyond the initial stakeout by City
- b. The Contractor shall make every effort to place the stone to the lines, grades and course thicknesses shown on the drawings.
- c. The Contractor's equipment and methods for handling each classification of stone shall be such that all placement requirements of this section are satisfied.

3. Approval

a. The Contractor will be required to rework deficient portions of the test section to meet these requirements. If during construction of the test section, it becomes evident that the Contractor cannot achieve the required neat lines and course thicknesses due to the type of stone being used, modifications to the section will be made. Upon approval, the test section can be incorporated into the remaining work such that removal will not be necessary.

4. Modifications

a. The Contractor will make any necessary modifications to placement equipment and procedures to achieve the specified in-place requirements.

C. Delivery, Storage and Handling

1. General

- a. The Contractor shall exercise care in the transportation of all stone materials to prevent cracking, splitting, spalling, etc., that would otherwise lead to rejection at the job site.
- b. The Contractor shall handle and store bedding stone material to ensure that stockpiles are not contaminated with other soils and materials, and to limit the segregation of material sizes.

PRODUCTS

A. General

1. Materials which have been delivered to the project site and are rejected, whether in stockpile or in place in the structure, shall be removed from the project site at the Contractor's expense. Any damages to approved stone prior to substantial completion,

due to Contractor or subcontractor operations, wave activity, or otherwise, shall be repaired by the Contractor at no additional cost to the Owner.

B. Sources for Stone Blocks

1. The following listed sources have supplied materials that meet the quality requirements specified. All stone shall be produced from the sources listed below and meet the requirements of Article 2.06 and other requirements of these specifications:

Michels Materials, Valders, WI, 920-478-2084 Halquist Stone, Sussex, WI, 800-255-8811 Valders Stone and Marble, Inc., Valders, WI, 800-569-2156

C. Material Quality

All stone shall be highly resistant to weathering and disintegration under freezing and thawing and wetting and drying conditions, and shall be of a quality to ensure permanence of the structure in the climate in which it is to be used. The stone shall be durable, sound, and free from detrimental cracks, seams and other defects which tend to increase deterioration from natural causes or cause breakage in handling and/or placing. A high argillaceous or shale content is often indicative of poorer quality rock being more susceptible to weathering, abrasion, thin bedding, close fracturing and other undesirable rock properties.

D. Other Sources

- 1. If the Contractor elects to use stone from a source not indicated as previously approved by the USACE, the material must be approved by the USACE and the Owner's Representative, prior to its production, for use on this project. This approval process may include any or all of the following, as directed by the Owner's Representative.
 - a. Test samples of the proposed stone shall be obtained by the Contractor at its own expense. Samples selected for testing shall be representative of material formations in the quarry to be used or being used on the project. The representative must be present and agree on the selection of all test samples prior to shipment. The Owner's Representative may personally select all samples if he so elects.
 - b. The samples shall be shipped or delivered by the Contractor, at its expense, to the Local Division Laboratory, U.S. Army Corps of Engineers.
 - c. Tests to which the material may be subject to include one or more of the following: petrographic examination; specific gravity; abrasion; absorption; wetting and drying; freezing and thawing; soundness; compressive strength; expansion; tensile strength; pulse velocity; gradation; water content; dry unit weight and total porosity; elastic moduli; direct shear; and any other tests determined necessary to ensure that the stone is suitable for its intended use.
 - d. The Contractor is responsible for allowing sufficient time for the testing to be completed such that there are no delays in construction.
 - e. If the Contractor elects to use material from a source not previously approved, all costs incurred as a result of testing to verify material acceptability shall be the responsibility of the Contractor.

E. Quarry Operations

- 1. Quarry operations shall be conducted by the Contractor/supplier in a manner that will produce stone conforming to the requirements specified, and may involve selective quarrying, handling and loading as necessary. Blasting and handling of rock shall be controlled by the Contractor/supplier to produce stone of the size ranges and quality specified. Techniques such as the use of proper hole diameter, hole depth, hole angle, burden and spacing distances, types and distribution of explosives, delay interval and sequence, removal of muck piles between each shot and special handling techniques will be required as necessary to produce the specified materials. All specifications of blasting operations shall be specifically designed so that the end product is not damaged from the blasting technique and that the stone is suitable for the intended purpose.
- 2. All sedimentary quarry stone from any source shall be stockpiled at the quarry a minimum of 48 hours prior to shipment to the project site. No stone production shall be allowed prior to 1 April or after 1 November, unless quarry history is available to ensure that durable stone can be quarried in freezing temperatures.

METHOD OF MEASUREMENT

Stepped Stone Revetment (Station 1+25) shall be measured per Linear Foot of steps acceptably completed, as measured along the reference line. Only accepted work will be measured for payment.

BASIS OF PAYMENT

Stepped Stone Revetment (Station 1+25) shall be measured as described above and shall be paid at the contract price which shall be full compensation for all materials, labor and equipment necessary for a complete installation including preparation of the bed and stone steps as defined herein, but not including filter fabric, clear stone, or ECRM above the steps.

BID ITEM 90036 - STEPPED STONE REVETMENT (STATION 6+50)

DESCRIPTION

Work under this item shall include all work, materials, labor and incidentals necessary for the Contractor to provide and install 25 linear feet of Stepped Stone Revetment at Station 6+50 in accordance with the Specification that follows, and as shown on the drawings. Filter Fabric and Clear Stone to be used in the revetment installation shall be paid separately, under Bid Items 20140 and 20217, respectively.

CONSTRUCTION METHODS

The Stepped Stone Revetment shall be constructed as shown in the plan set. A suitable foundation, as approved by the Engineer shall be provided to preclude settlement. Filter Fabric shall be installed under the bed, as shown on the drawings. Clear stone and filter fabric shall be installed according to the Standard Specifications. Each stone step shall be firmly set with no rocking or tipping, providing a firm foundation for subsequent layers. Cut stone blocks shall be field cut as required to fit tightly to abutting structures.

- 5. The stepped stone revetment shall be placed by equipment on the surfaces and to the depths specified on the drawings.
- 6. Stone shall be placed tightly together such that at least 60% of all joined faces are in direct contact and no more than 1.5-inch gap exists at any point along the joint. Vertical seams shall be staggered. Chiseling or cutting of the stone may be needed. Any costs for working the stone shall be included in the prices bid.

Rev. 07/11/2014-6832specs.doc D-22

- 7. The finished surface aesthetic is critical. The stone layers shall follow the requirements noted on the plan. The tread width shall be consistent along each elevation and the stones shall fit snugly together and have no gaps larger than 1.5-inch. Working of stone faces may be required to achieve desired tolerances.
- 8. The intention of the above tolerances is that the work will be generally built to the required elevation, slopes and grades, and that the outer surfaces shall present a neat and aesthetic appearance. Placed material not meeting these intentions shall be removed and/or reworked to the satisfaction of the Owner's Representative. The Contractor is encouraged to look at a similar application of stone steps along the shoreline of Lake Mendota in front of the boathouse at James Madison Park.

QUALITY CONTROL

A. Stone Quality and Gradation

- 1. The Contractor is responsible for, and shall establish and maintain, quality control for all work performed at the quarry and at the job site to ensure compliance with the specifications.
- 2. The Contractor shall provide a quarry inspector for all stepped stone. The inspector's responsibilities shall include, but not be limited to:
 - a. A visual test shall be made at the quarry for elongation, cracks, deterioration and other defects visible to the naked eye on at least two-thirds of the surface area of the stone. Ten percent of the stone checked for cracks shall be wetted and reinspected for minute cracks to determine if they would be detrimental to the stone quality and if additional inspections are necessary on all stone. Stones with cracks that are detrimental to a long-lasting product shall not be shipped to the project site.
 - b. Quarry representative shall pick stones of similar height dimensions for each layer. Stones shall have face and sides perpendicular to each other or angles that will match adjacent stone to achieve a tight fit. Stones intended for each layer shall be marked on the back to identify exact location in the finished work.
- 3. The Owner's Representative reserves the right to inspect the quarry operations at any time to check for compliance to the specifications.
- 4. All Stepped Stone shall be produced from the same quarry.

B. Test Section

1. General

a. The initial stepped stone revetment section will be considered as a test section. The purpose of the test sections will be to establish an in-the-field standard, built in accordance with the requirements of the contract documents, to which the remainder of the stepped stone revetment shall be constructed. The Contractor will make whatever modifications are necessary to placement procedures such that this standard will be achieved consistently during construction of the remainder of the revetment.

Execution

a. The Contractor shall lay out the work, provide any survey control as needed for control of the work beyond the initial stakeout by City.

- b. The Contractor shall make every effort to place the stone to the lines, grades and course thicknesses shown on the drawings.
- c. The Contractor's equipment and methods for handling each classification of stone shall be such that all placement requirements of this section are satisfied.

3. Approval

a. The Contractor will be required to rework deficient portions of the test section to meet these requirements. If during construction of the test section, it becomes evident that the Contractor cannot achieve the required neat lines and course thicknesses due to the type of stone being used, modifications to the section will be made. Upon approval, the test section can be incorporated into the remaining work such that removal will not be necessary.

4. Modifications

The Contractor will make any necessary modifications to placement equipment and procedures to achieve the specified in-place requirements.

C. Delivery, Storage and Handling

1. General

- c. The Contractor shall exercise care in the transportation of all stone materials to prevent cracking, splitting, spalling, etc., that would otherwise lead to rejection at the job site.
- d. The Contractor shall handle and store bedding stone material to ensure that stockpiles are not contaminated with other soils and materials, and to limit the segregation of material sizes.

PRODUCTS

A. General

1. Materials which have been delivered to the project site and are rejected, whether in stockpile or in place in the structure, shall be removed from the project site at the Contractor's expense. Any damages to approved stone prior to substantial completion, due to Contractor or subcontractor operations, wave activity, or otherwise, shall be repaired by the Contractor at no additional cost to the Owner.

C. Sources for Stone Blocks

2. The following listed sources have supplied materials that meet the quality requirements specified. All stone shall be produced from the sources listed below and meet the requirements of Article 2.06 and other requirements of these specifications:

Michels Materials, Valders, WI, 920-478-2084 Halquist Stone, Sussex, WI, 800-255-8811 Valders Stone and Marble, Inc., Valders, WI, 800-569-2156

C. Material Quality

1. All stone shall be highly resistant to weathering and disintegration under freezing and thawing and wetting and drying conditions, and shall be of a quality to ensure

permanence of the structure in the climate in which it is to be used. The stone shall be durable, sound, and free from detrimental cracks, seams and other defects which tend to increase deterioration from natural causes or cause breakage in handling and/or placing. A high argillaceous or shale content is often indicative of poorer quality rock being more susceptible to weathering, abrasion, thin bedding, close fracturing and other undesirable rock properties.

D. Other Sources

- 1. If the Contractor elects to use stone from a source not indicated as previously approved by the USACE, the material must be approved by the USACE and the Owner's Representative, prior to its production, for use on this project. This approval process may include any or all of the following, as directed by the Owner's Representative.
 - a. Test samples of the proposed stone shall be obtained by the Contractor at its own expense. Samples selected for testing shall be representative of material formations in the quarry to be used or being used on the project. The representative must be present and agree on the selection of all test samples prior to shipment. The Owner's Representative may personally select all samples if he so elects.
 - b. The samples shall be shipped or delivered by the Contractor, at its expense, to the Local Division Laboratory, U.S. Army Corps of Engineers.
 - c. Tests to which the material may be subject to include one or more of the following: petrographic examination; specific gravity; abrasion; absorption; wetting and drying; freezing and thawing; soundness; compressive strength; expansion; tensile strength; pulse velocity; gradation; water content; dry unit weight and total porosity; elastic moduli; direct shear; and any other tests determined necessary to ensure that the stone is suitable for its intended use.
 - d. The Contractor is responsible for allowing sufficient time for the testing to be completed such that there are no delays in construction.
 - e. If the Contractor elects to use material from a source not previously approved, all costs incurred as a result of testing to verify material acceptability shall be the responsibility of the Contractor.

E. Quarry Operations

- 1. Quarry operations shall be conducted by the Contractor/supplier in a manner that will produce stone conforming to the requirements specified, and may involve selective quarrying, handling and loading as necessary. Blasting and handling of rock shall be controlled by the Contractor/supplier to produce stone of the size ranges and quality specified. Techniques such as the use of proper hole diameter, hole depth, hole angle, burden and spacing distances, types and distribution of explosives, delay interval and sequence, removal of muck piles between each shot and special handling techniques will be required as necessary to produce the specified materials. All specifications of blasting operations shall be specifically designed so that the end product is not damaged from the blasting technique and that the stone is suitable for the intended purpose.
- 2. All sedimentary quarry stone from any source shall be stockpiled at the quarry a minimum of 48 hours prior to shipment to the project site. No stone production shall be allowed prior to 1 April or after 1 November, unless quarry history is available to ensure that durable stone can be quarried in freezing temperatures.

METHOD OF MEASUREMENT

Stepped Stone Revetment (Station 6+50) shall be measured per Linear Foot of steps acceptably completed, as measured along the reference line. Only accepted work will be measured for payment.

BASIS OF PAYMENT

Costs for Stepped Stone Revetment (Station 6+50) shall be measured as described above and shall be paid at the contract price which shall be full compensation for all materials, labor and equipment necessary for a complete installation including preparation of the bed and stone steps as defined herein, but not including filter fabric, clear stone, or ECRM above the steps.

BID ITEM 90037 - LITTORAL SHELF CONSTRUCTION

DESCRIPTION

Work under this bid item includes all labor, equipment, materials, and incidentals necessary to construct littoral shelves to the lines and grades shown on the plan set.

The Contractor shall place a layer of Erosion Matting Class II, Type C – Organic between the existing creek bed and imported fill. The matting shall be toed-in behind the stone used to armor the banks. The matting placed between the existing creek bed material and the fill shall be Dekowe 900, GeoCoir 900, or approved equal. In this application, Dekowe 900 or GeoCoir 900 shall be selected from the Product Acceptability List. These materials were chosen because they have a smaller weave and are 100% biodegradable. An alternate material that meets these criteria may be proposed for this location, subject to the approval of the Project Engineer. All Erosion Control Matting, Class II, Type C shall be paid separately under that bid item.

Clean fill shall then be placed over the matting to achieve the elevations shown on the plan set. The Contractor shall anticipate settlement between 0.5 and 1 foot in the existing creek bed. An average settlement of 0.75 feet was used to calculate the fill estimate shown below. Provision and placement of fill material shall be considered incidental to this bid item.

Fill: 3864 CY

Four inches of topsoil shall be placed over the fill material. Topsoil shall be paid separately under Bid Item 20221 and shall be placed in accord with Article 202 of the Standard Specifications.

The littoral shelf shall be seeded according to Sheet D-2 and stabilized with Erosion Control Matting Class II, Type C – Organic **immediately following fill and topsoil placement**. Seed shall be placed in accordance with Article 207 of the Standard Specifications. Any Class II, Type C matting listed on the WI DOT Product Acceptability List is acceptable for the surface matting. Seeding and erosion matting shall be paid separately under the appropriate bid items.

The Contractor shall manage their schedule so as not to leave a partially constructed littoral shelf exposed to rainfall, or rising creek levels.

METHOD OF MEASUREMENT

Littoral Shelf shall be measured per Square Foot of shelf constructed.

BASIS OF PAYMENT

Littoral Shelf shall be measured as defined above and shall be paid at the contract unit price, which shall constitute full payment for the construction of the littoral shelves and described above.

Rev. 07/11/2014-6832specs.doc D-26

BID ITEM 90038 - WOODY DEBRIS FISH HABITAT

DESCRIPTION

The Contractor shall provide and install Woody Debris Fish Habitat at the locations shown on the drawings.

This item shall include installation and anchoring of a tree trunk and limbs salvaged from site clearing activities, as shown on the detail in Sheet D-2. Excavation, Fill, Clear Stone, Filter Fabric, Topsoil, Seeding, and ECRM shall be paid separately under their respective bid items, except additional quantities of these items and/or reworking/reconfiguration of these items needed to accommodate installation of the tree trunk, shall be considered incidental to this bid item, and no measurement of these additional quantities shall be made.

Anchorage systems shall consist of anchors, plastic cable, and plastic washers used for installation of ScourstopTM turf reinforcement mats, available from Geo-Synthetics Inc. in Waukesha, WI (<u>www.geo-synthetics.com</u>), or Engineer-approved equivalent. Scourstop turf reinforcement mats are not required for this application – only the anchors are required. For each tree trunk, install two anchors (one on each side of trunk) to sufficient depth to achieve anchoring to the satisfaction of the Engineer, and fasten plastic cable from each anchor securely into a single plastic washer.

An acceptable alternative anchorage system is Manta Ray MR-SR anchors, 1-inch threaded anchor rod, swivel eye, 3/8-inch galvanized steel cable, and appropriately sized cable clips, or approved equal. Two anchors and cables shall be installed per tree.

METHOD OF MEASUREMENT

Woody Debris Fish Habitat shall be measured per Each complete unit as installed in the field.

BASIS OF PAYMENT

Woody Debris Fish Habitat shall be measured as described above and shall be paid for at the contract price which shall be full compensation for all work, materials, labor, tools, equipment and incidentals required for a complete installation as set forth in the description.

BID ITEM 90039 - GEOWEB CREEK ACCESS

DESCRIPTION

This bid item shall include all labor, equipment, materials, and incidentals necessary to provide and install Geoweb GW30V, 6-inch geocell matrix, (http://www.prestogeo.com/slope_protection) or approved equal at the locations and grades shown in the plan set and detailed on Sheet D-1. The geoweb shall be installed per the manufacturer's recommendations.

The Contractor shall install a layer of non-woven geotextile fabric beneath the geoweb installation. Filter fabric shall be paid separately under Bid Item 20140. Manufacturer specified anchors shall be installed in accordance their recommendations (approximately 10% coverage, i.e. 10 anchors per 100 feet of Geoweb). The cells shall be filled with 1-inch clear stone, which shall be considered incidental to this bid item.

The Contractor shall anchor the geoweb installation via a trench at the top of bank. The anchor shall be buried a minimum of two feet within the trench, and shall be anchored into the existing soil. Geoweb within the trench may be filled with backfill material, as opposed to 1-inch clear stone.

METHOD OF MEASUREMENT

Geoweb Creek Access shall be measured per Square Foot of material installed in the field, including material buried within the anchor trench.

BASIS OF PAYMENT

Geoweb Creek Access shall be measured as described above and shall be paid for at the contract unit price which shall constitute full compensation for all work, materials, labor, tools, equipment and incidentals required for a complete installation as set forth in the description.

D-28

Silt Curtain

(1070)

Wisconsin Department of Natural Resources Conservation Practice Standard

I. Definition

A temporary permeable fabric installed in a waterway or waterbody to minimize sediment transport. A silt curtain does not extend to the bottom of the channel and is placed parallel or perpendicular to the direction of flow.

II. Purposes

The purpose of this practice is to provide sediment containment while construction activities are occurring in or directly adjacent to a waterway or waterbody.

III. Conditions Where Practice Applies

This practice applies where construction activities intrude or are directly adjacent to a waterway or waterbody. This includes but is not limited to bridge construction, rip rap placement, utility work, streambank restoration, boat launches and dredging.

Silt curtain is intended for calm water conditions where it will not be subjected to wind, wave, or current. Silt curtains are appropriate to settle out coarse and granular soils where water depth at the time of construction is greater than or equal to 4 feet. For applications in finer sediment or moving water see WDNR Technical Standard 1069 Turbidity Barrier.

IV. Federal, State, and Local Laws

Users of this standard shall be aware of applicable federal, state, and local laws, rules, regulations, or permit requirements governing the use and placement of silt curtains. This standard does not contain the text of federal, state, or local laws.

V. Criteria

This section establishes the minimum standards for design, installation and performance requirements.

- A. Installation Details of construction not listed in the text shall conform to the pertinent requirements of Figure 1.
 - The silt curtain shall be installed before construction activities are initiated in or adjacent to the waterway or waterbody. Install the silt curtain as close to the construction as practical. The curtain shall remain in place and be maintained until the construction activity is completed and the disturbed area is stabilized ¹.
 - 2. The ends of the silt curtain shall be securely anchored and keyed into the shoreline to fully enclose the area where sediment may enter the water.
 - 3. A 2-foot gap shall exist between the weighted lower end of the curtain and the bottom of the waterway or waterbody.
 - 4. Bottom anchors shall be used to hold the silt curtain in the same position relative to the bottom the waterway or waterbody without interfering with the function of the curtain. Anchors shall either be driven into the bottom of the waterway or waterbody or be weighted and attached to the curtain floatation device via an anchor line. Manufacture's recommendations shall be followed for the number and spacing of anchors.
 - 5. Danger buoys shall be used as directed by the Coast Guard or DNR permit when working in navigable waters.

B. Material:

- 1. Reusable components of the silt curtain system shall be clean and free of potential exotic species. Fabric cannot be reused.
- 2. The silt curtain shall be constructed from heavy woven filter fabric to allow water to pass through the barrier yet retain sediment.

Conservation Practice Standards are reviewed periodically and updated if needed. To obtain the current version of this standard, contact your local WDNR office or the Standards Oversight Council office.

WDNR, WI 9/05 All fabric seams shall be heat sealed or sewn. Silt curtain fabric shall conform to the specifications in Table 1.

Table 1

Requirement	Value
Thickness	15 mils (0.38 mm)
Min. grab tensile strength (ASTM D 4632)	120 lb (550 N)
Min. equivalent opening	No. 170 sieve (90 μm)

- 3. Floatation devices shall be flexible, buoyant units contained in an individual floatation sleeve or collar attached to the curtain. Use expanded polystyrene logs or equivalent having a 49 square inch minimum end area. Do not use polystyrene beads or chips. Buoyancy provided by the floatation device shall be sufficient to support the weight of the curtain and maintain a freeboard of at least 3 inches above the water surface level.
- 4. Top load lines shall consist of 5/16 inch steel cable.
- 5. Bottom load lines shall consist of a minimum ¼-inch steel chain incorporated into the bottom hem of the curtain. Larger chain sizes may be used where additional weight to serve as ballast to hold the curtain in a vertical position is required.

VI. Considerations

- A. Sediment that has settled out by the silt curtain should only be removed as directed by the regulatory authority because re-suspension of sediment will likely occur during the removal process. Use of polymers may help prevent resuspension of sediment. See WDNR Technical Standard 1051 Sediment Control Water Application of Polymers for further guidance.
- B. Silt curtains are meant to manage sediment in the waterbody. The best way to prevent sediment from entering the waterbody is through the implementation of effective upland erosion control, stopping sediment transport at its source.

VII. Plans and Specifications

Plans and specifications for installing a silt curtain shall be in keeping with this standard and shall describe the requirements for applying the practice to achieve its intended purpose:

- A. Location of silt curtain.
- B. Material specification conforming to standard.
- C. All plans, standard detail drawings, or specifications shall include schedule for installation, inspection, and maintenance. The responsible party shall be identified.

VIII. Operation and Maintenance

- A. Silt curtains shall be inspected daily and repaired if necessary.
- B. Regardless of upland stabilization conditions silt curtains shall not be removed until the water behind the curtain has equal or greater clarity than the waterway or waterbody. Soil particles shall be allowed to settle for a minimum of 24 hours prior to removal of the curtain.
- C. Care shall be taken when removing the silt curtain to minimize the release or re-suspension of accumulated sediment.
- D. To prevent the spread of exotic species silt curtains shall not be reused on other sites. Bouys and chains can be reused but shall be either disinfected with vinegar or cleaned with hot water greater than 104 deg. F then allowed to completely dry for a minimum period of five days. If there are any questions about the occurrence of zebra mussels, Eurasian watermilfoil, or other aquatic invasive species in a waterbody that you are working in or intend to work in contact your local DNR staff.

IX. References

Virginia Erosion and Sediment Control Handbook, Third Edition, 1992

WisDOT Facilities Development Manual: Chapter 10, Section 10, Subject 43, Silt Screen

X. Definitions

Stabilized (V.A.1): Means that all land disturbing construction activities at the construction site have been completed, and that a uniform perennial vegetative cover has been established with a density of at least 70% of the cover for the unpaved areas and areas not covered by permanent structures, or that employ equivalent stabilization measures.

GENERAL NOTES

DETAILS OF CONSTRUCTION, MATERIALS AND WORKMANSHIP NOT SHOWN ON THIS DRAWING SHALL CONFORM TO THE PERTINENT REQUIREMENTS OF THE STANDARD AND THE APPLICABLE SPECIAL PROVISIONS

- (1) 2' SHALL BE MAINTAINED DURING CONSTRUCTION PERIOD
- (2) USE AS DIRECTED BY COAST GUARD OR WONR PERMIT WHEN WORKING IN NAVIGABLE WATERWAYS


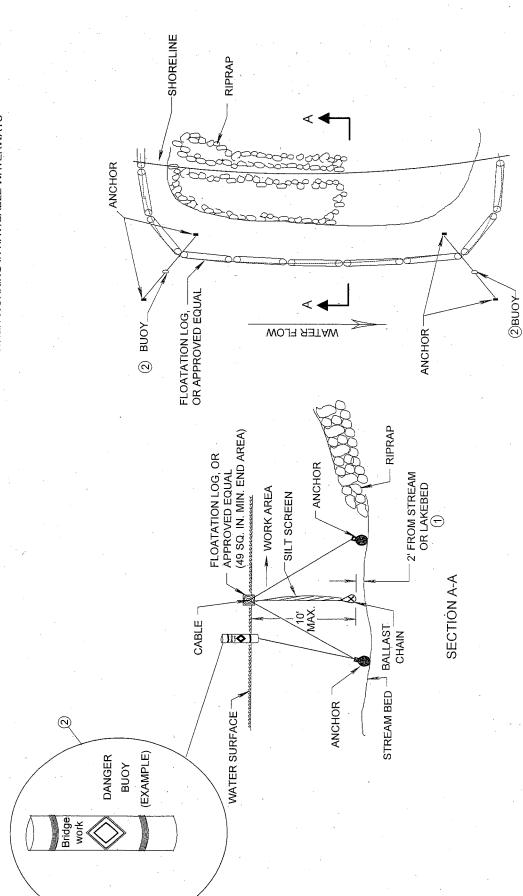


FIGURE 1. SILT CURTAIN PLACEMENT DETAIL

This drawing based on Wisconsin Deptartment of Transportation Standard Detail Drawing 8 E 12-1.

PLAN VIEW

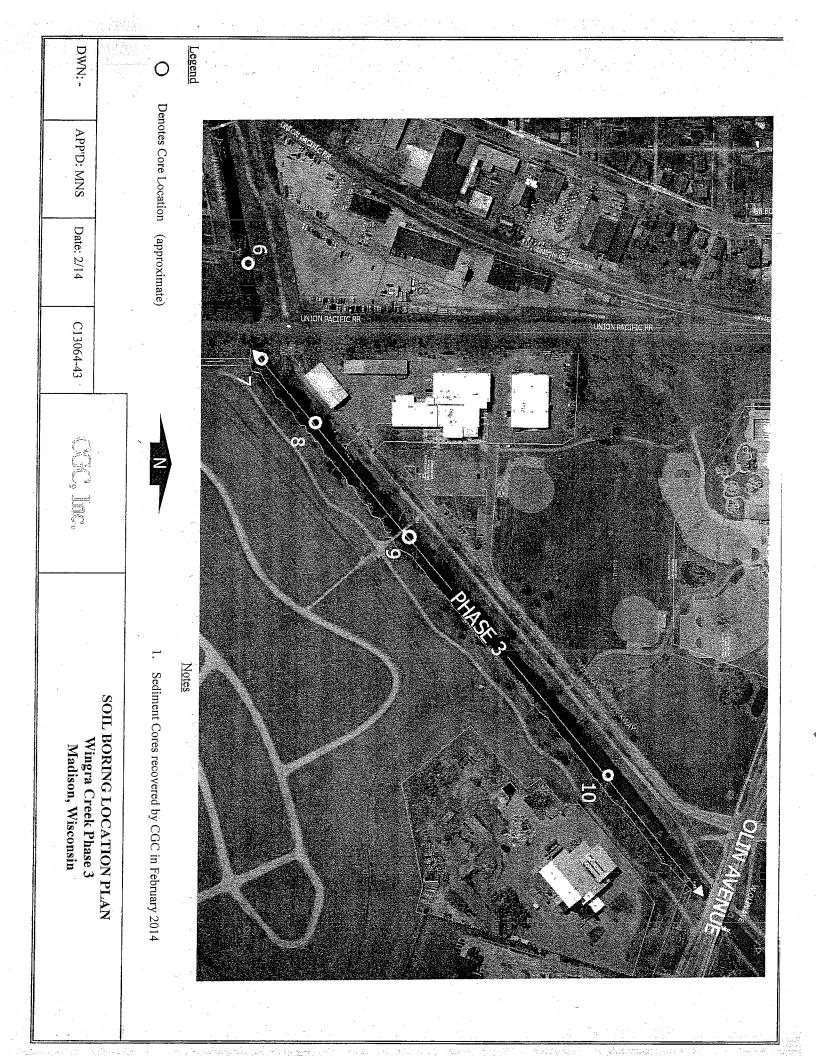

$ln \cap I$

		Boring iv	10.	
Project	Wingra Creek Phase 3	Surface I	Elevation (ft)	***
		Job No.	C1306	4-43
Location	Madison, Wisconsin	Sheet	1 of	1

	2921 Perry Street, Madison, WI 53713 (608) 288-4100, FAX (608) 288-7887												
SAMPLE				VISUAL CLASSIFICATION			SOIL PROPERTIES						
No.	1.1	Rec in.)	Moist	N	Depth (ft)		and Remarks		qu (qa) (tsf)	W	FF	PL	ΓI
							3" ICE/33" WATER						
					<u>i</u>								
<u>.</u>					<u> </u>								
:					<u></u>								
	.				<u> </u>								
]								
			,		<u>├</u>								
					i								
					_	- ,				1			
					} 		Dark Gray Organic SILT to Silty Sand, L	ittle Clay				-	
					Ĺ		_						
										•			
													
			-		1		•						
					1								ا,
j		-			i								
				ŀ	l. 								-
					Ļ.		·						
					1 			-					
i					<u> </u>								
					1			And Andrews				-	
					 -		Gray Fine to Medium SAND, Trace to Lit	ttle Silt				Ì	
							•		~				
-					<u>i</u>		-						
	ļ				l I	irigiri pigi							:
					<u></u>		- -	;					
					-								
								į					
			٥.				End of Sediment Core at 9 ft						
												٥	
				i					*	1		.	*
					10-					·			
	WATER LEVEL OBSERVATIONS GENERAL NOTES												
While		rill:	no	Δ			Upon Completion of Drilling	Start 2/10	0/14 End	2/10/	14	-	-
			ng Drillin					Driller	Chief			ig	
Deptl	h to) Wa	ater	J			<u> </u>	Logger	Editor	ES	F [*]		
Deptl								Drill Method					
The soi	: st	rat ype	ificat s and	ion l	ines rep ransitio	ores on m	ent the approximate boundary between ay be gradual.	Pre-Washed	with TSP	201ntio	N		



Boring No. Surface Elevation (ft) Project Wingra Creek Phase 3 Job No. C13064-43 Location Madison, Wisconsin Sheet 1 of 1

	SAMPIF NUCLIAR OF ACCULICATION SOIL PROPERTIES													
		SA	MPL	.E		VISUAL CLASSIFICATION			IV					
No.	T Y P E	Rec	Moist	N	Depth (ft)		and Remarks		qu (qa) (tsf)	W	ŀľ	PL	LI	
							6" WATER							
			=		[[Brown to Gray Fine to Coarse SAND							
					1	100 Sec.	Dark Gray Organic SILT, Little to Some S	Sand						
	-				<u> </u>						•			
					<u> </u>				-					
					- -									
]									
					- 			—	·					
-							Gray to Brown Sedimentary PEAT to Org SILT, Trace Sand	ganic						
					[] 									
					 							-		
					 		Gray Silty Fine SAND, Trace Organics						-	
					1									
							End of Sediment Core at 6.5 ft	t ·						
					<u></u>									
								•						
			·		 							٠.		
					 - 		-						i	
					 .									
					[[and the second s							
	Ш	·		1.87	10-		WEL OBSEDWATIONS		 SENERA	NIC	TES			
					ATER		EVEL OBSERVATIONS					, 	. ,	
		Drill		<u> </u>		J		Start 2/1 Driller	0/14 End Chief	2/10/		ig		
Dept			Drillin ater	īŔ			<u> </u>	Logger	Editor	ES	F	~D		
Dept	h	to Ca	ive in					Drill Method	Piston S					
Th	e	strat	ificat	ion 1	ines re	prese	ent the approximate boundary between	Pre-Washe	a with TSP:	Solutio	n			



Boring No. 8 Surface Elevation (ft) Project Wingra Creek Phase 3 Job No. **C13064-43** Location Madison, Wisconsin Sheet 1 of 1

2921 Perry Street, Madison, WI 53713 (608) 288-4100, FAX (608) 288-7887								
SAMPLE	VISUAL CLASSIFICATION	SOIL	PRO	PER	TIE	S		
No. P (in.) Moist N Depth	and Remarks	qu (qa) (tsf)	W	ГГ	PL	LI		
	1" ICE/8" WATER							
					,			
	Dark Gray Organic SILT, Little to Some Sand,	-						
	Little Clay							
				,				
			•					
	Gray Silty Fine SAND, Trace Gravel and Organics							
		-						
	(2007) (2007)				'			
5-	#600 #600 #600							
	50000 60000 60000			ļ				
	0.000 10.000 10.000							
	500 500 500			•				
	1997 1998	-			.			
	End of Sediment Core at 6.75 ft	-				Ì		
	End of Sediment Core at 0.73 ft							
			ŀ					
						-		
	-							
10-								
WATER	LEVEL OBSERVATIONS (GENERAL	_ NO	TES				
While Drilling <u>▽</u>	Upon Completion of Drilling Start 2/1	0/14 End	2/10/					
Time After Drilling	Driller	Chief	TCI	Ri	g			
Depth to Water Depth to Cave in		Editor d Piston S						
The stratification lines re		d with TSP S						

The second livery of the secon	The second second
/	_
	\
((
	, 11 1C.7


		Boring No.
Project	Wingra Creek Phase 3	Surface Elevation (ft)
		Job No. C13064-43
Location	Madison. Wisconsin	Sheet 1 of 1

2921 Perry Street, Madison, WI 53713 (608) 288-4100, FAX (608) 288-7887 SOIL PROPERTIES SAMPLE VISUAL CLASSIFICATION and Remarks Depth (qa) Moist (in.) (ft) (tsf) 2" ICE/7" WATER Dark Gray Organic SILT to Silty Sand, Little Clay Gray Lean CLAY End of Sediment Core at 6.75 ft GENERAL NOTES WATER LEVEL OBSERVATIONS Start 2/11/14 End Upon Completion of Drilling While Drilling Driller Chief Rig
Logger Editor ESF
Drill Method Piston Sampler Time After Drilling Depth to Water Depth to Cave in Pre-Washed with TSP Solution The stratification lines represent the approximate boundary between soil types and the transition may be gradual.

I
INC.)

10 Boring No. Surface Elevation (ft) Project Wingra Creek Phase 3 Job No. **C13064-43** Sheet **1** of **1** Madison, Wisconsin Location

2921 Perry Street, Madison, WI 53713 (608) 288-4100, FAX (608) 288-7887						
SAMPLE	VISUAL CLASSIFICATION	SOIL PROPERTIES				
No. P (in.) Moist N De	dia Komarko	qu (qa) W LL PL LI (tsf)				
	3" ICE/9" WATER					
	Dark Gray Organic SILT, Little to Some Sar	nd				
	Gray Lean CLAY, Occasional Sand Partings					
	Thin (<1") Sand Seams noted near 6'					
	End of Sediment Core at 7.0 ft					
)—					
WAT	R LEVEL OBSERVATIONS	GENERAL NOTES				
While Drilling	Dr	art 2/11/14 End 2/11/14 iller Chief Rig				
Depth to Water	¥ Lo	gger Editor ESF				
Depth to Cave in The stratification lines		ill Method Piston Sampler e-Washed with TSP Solution				

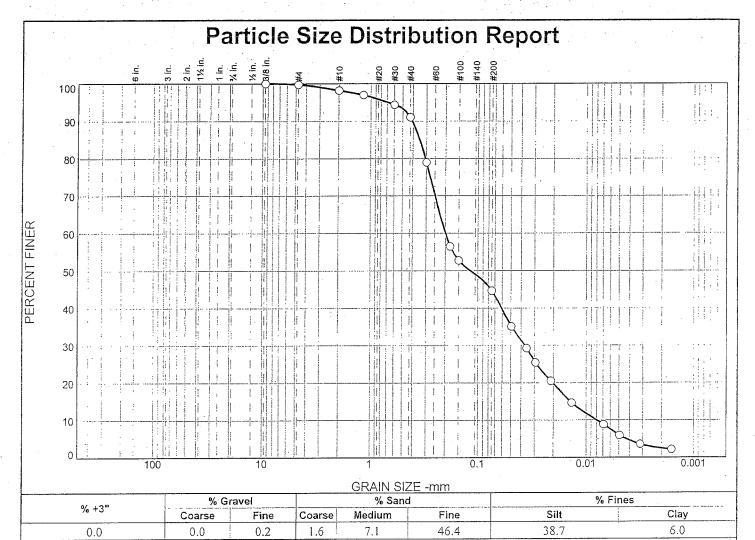

	SIEVE	PERCENT	SPEC.*	PASS?
	SIZE	FINER	PERCENT	(X=NO)
	3/8"	100.0		
	#4	99.8		
	#10	98.2		
	#16	97.0		
	#30	.94.4		*
	#40	91.1		
	#50	79.0		
	#80	56.5		
	#100	52.8		
	#200	44.7		
	}			
.				
İ				

	Material Description	
Dark Gray Silty I	Fine to Medium Sand, L	ittle Clay
PL=	Atterberg Limits LL=	PI=
D ₉₀ = 0.4058 D ₅₀ = 0.1176 D ₁₀ = 0.0080	Coefficients D ₈₅ = 0.3464 D ₃₀ = 0.0370 C _u = 24.98	D ₆₀ = 0.1994 D ₁₅ = 0.0140 C _c = 0.86
USCS= SM	Classification AASHTC)=
	Remarks	
Organics Present		
Natural Moisture	= 87.3%	

* (no specification provided)

Sample Number: B6/S1

Date: 2/25/14

CGC,Inc.


Client: City of Madison

Project: Wingra Creek Phase 3

Project No: C13064-43

Figure

Tested By: JSG

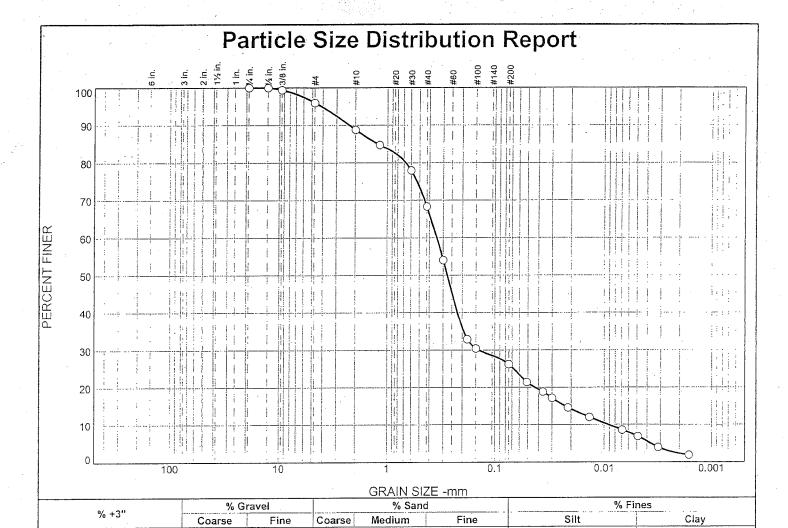

SIEVE	PERCENT	SPEC.*	PASS?
SIZE	FINER	PERCENT	(X=NO)
3/4 in.	100.0		
1/2 in.	100.0		·
3/8 in.	99.4		
#4	96.0		
#10	88.8		
#16	84.7		
#30	77.9		
#40	68.3		
#50	54.0		
#80	32.9		
#100	30.4		
#200	26.2		
	•		

Coarse

0.0

Fine

4.0

7.2

20.5

42.1

Dark Gray Fine to Gravel	Coarse Sand, Some S	ilt, Little Clay, Trace
PL=	Atterberg Limits LL=	PI=
D ₉₀ = 2.2908 D ₅₀ = 0.2757 D ₁₀ = 0.0092	Coefficients D85= 1.2368 D30= 0.1414 Cu= 37.21	D ₆₀ = 0.3429 D ₁₅ = 0.0228 C _c = 6.32
USCS= SM	Classification AASHT()=
Organics Present	Remarks	e e e e e e e e e e e e e e e e e e e
Natural Moisture =	· 43.2%	

19.2

(no specification provided)

Sample Number: B7/S1

0.0

Date: 2/25/14

7.0

CGC,Inc.


City of Madison

Project: Wingra Creek Phase 3

Project No: C13064-43

Figure

Tested By: JSG

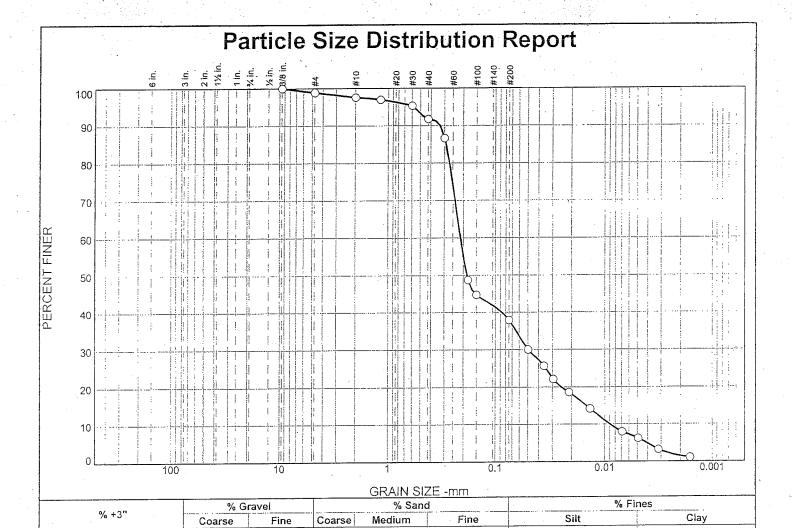

01515	DEDOCNE	CDEC *	PASS?
SIEVE	PERCENT	SPEC.*	PASS
SIZE	FINER	PERCENT	(X=NO)
3/8"	100.0		,
#4	98.9		
#10	97.6		
#16	97.0		
#30	95.4		
#40	91.8		
#50	86.7		
#80	48.7)	
#100	44.7	1	
#200	37.9		
	-		
		}	

0.0

1.1

1.3

5.8

53.9

<u></u>	Material Description	1					
Dark Gray Fine to	Dark Gray Fine to Medium Sand, Some Silt, Little Clay, Trace						
Gravel							
	Atterberg Limits						
PL=	LL=	PI=					
D ₉₀ = 0.3309 D ₅₀ = 0.1848 D ₁₀ = 0.0090	Coefficients D85= 0.2908 D30= 0.0495 Cu= 23.77	D ₆₀ = 0.2133 D ₁₅ = 0.0146 C _c = 1.28					
USCS= SM	Classification AASHTO)=					
	Remarks						
Organics Present							
Natūral Moisture =	= 34.2%						

31.6

(no specification provided)

Sample Number: B8/S1

0.0

Date: 2/25/14

6.3

CGC,Inc.


Client: City of Madison

Project: Wingra Creek Phase 3

Project No: C13064-43

Figure

Tested By: JSG

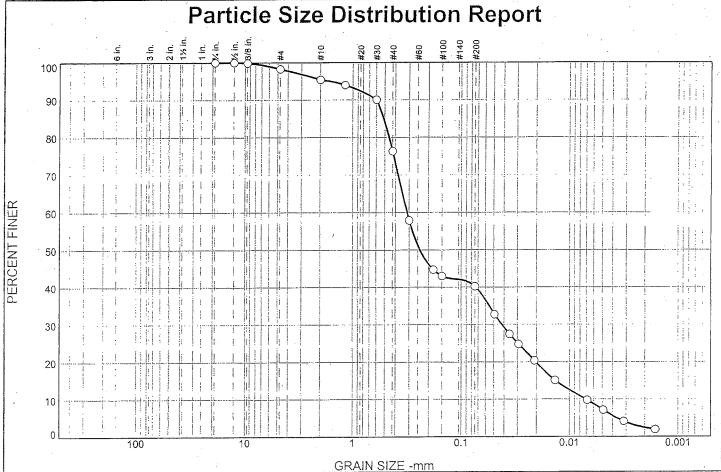

		% Gr	avel .		% Sand		% F	Ines
% +3	- •	Coarse	Fine	Coarse	Medium	Fine	Silt	Clay
0.0		0.0	1.7	2.9	19.1	36.1	32.9	7.3
SIEVE	PERCEN	JT SPEC	~ * p	ASS?		Mat	orial Description	

	SIEVE	PERCENT	SPEC.*	PASS?
	SIZE	FINER	PERCENT	(X=NO)
	3/4 in.	100.0	-	
	1/2 in.	100.0		
	3/8 in.	99.9		
	#4	98.3		
	#10	95.4		
	#16	94.0		
	#30	90.1		
	#40	76.3		
	#50	57.9		
	#80	44.7		
	#100	43.0		
	#200	40.2	*	·
-				
			-	.]
-			* '	

Gravel		
PL=	Atterberg Limits LL=	Pi=
D ₉₀ = 0.5988 D ₅₀ = 0.2397 D ₁₀ = 0.0071	Coefficients D ₈₅ = 0.5136 D ₃₀ = 0.0420 C _U = 44.36	D ₆₀ = 0.3137 D ₁₅ = 0.0134 C _c = 0.79
USCS= SM	Classification AASHTO	= ,
	Remarks	
Organics Present		
Natural Moisture =	= 67.8%	

(no specification provided)

Sample Number: B9/S1

Date: 2/25/14

CGC,Inc.


Client: City of Madison

Project: Wingra Creek Phase 3

Project No: C13064-43

Figure

Tested By: JSG

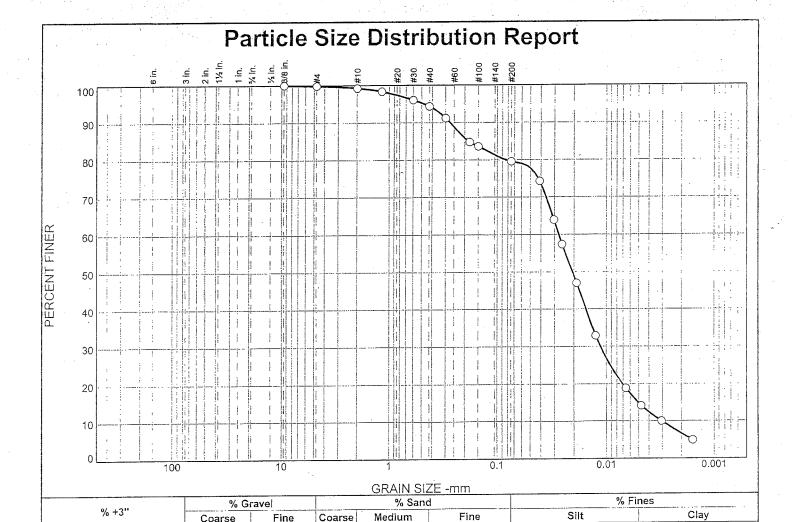

Medium

4.8

14.9

Coarse

0.6

Fine

0.2

SIEVE	PERCENT	SPEC.*	PASS?
SIZE	FINER	PERCENT	(X=NO)
3/8"	100.0		
#4	99.8		
#10	99.2		
#16	98.4		
#30	96.1		
#40	94.4		
#50	91.2		
#80	84.8		
#100	83.6		
#200	79.5		
	•		
	\$1ZE 3/8" #4 #10 #16 #30 #40 #50 #80 #100	SIZE FINER 3/8" 100.0 #4 99.8 #10 99.2 #16 98.4 #30 96.1 #40 94.4 #50 91.2 #80 84.8 #100 83.6	SIZE FINER PERCENT 3/8" 100.0 100

Coarse

0.0

	Material Description Dark Gray Silt, Some Sand and Clay						
	PL=	Atterberg Limits	PI=				
-	D ₉₀ = 0.2733 D ₅₀ = 0.0207 D ₁₀ = 0.0031	<u>Coefficients</u> D ₈₅ = 0.1850 D ₃₀ = 0.0114 C _u = 8.99	D ₆₀ = 0.0276 D ₁₅ = 0.0051 C _c = 1.53				
	USCS= ML	Classification AASHTO=					
	Organics Present Natural Moisture =	Remarks					

64.7

* (no specification provided)

Sample Number: B10/S1

0.0

Date: 2/25/14

14.8

CGC,Inc.

City of Madison Client:

Project: Wingra Creek Phase 3

Project No: C13064-43

Figure

Tested By: JSG





February 26, 2014

Dennis Iverson IVERTECH, LLC. 2880 Jonathan Circle Madison, WI 53711

RE: Project: C7799-WING III WINGRA

Pace Project No.: 4092070

Dear Dennis Iverson:

Enclosed are the analytical results for sample(s) received by the laboratory on February 13, 2014. The results relate only to the samples included in this report. Results reported herein conform to the most current TNI standards and the laboratory's Quality Assurance Manual, where applicable, unless otherwise noted in the body of the report.

If you have any questions concerning this report, please feel free to contact me.

Sincerely,

Dan Milewsky

dan.milewsky@pacelabs.com

Project Manager

Enclosures





Pace Analytical Services, Inc. 1241 Bellevue Street - Suite 9 : Green Bay, WI 54302 (920)469-2436

CERTIFICATIONS

C7799-WING III WINGRA

Pace Project No.:

4092070

Green Bay Certification IDs 1241 Bellevue Street, Green Bay, WI 54302 Florida/NELAP Certification #: E87948 Illinois Certification #: 200050 Kentucky Certification #: 82 Louisiana Certification #: 04168 Minnesota Certification #: 055-999-334

New York Certification #: 11888 North Dakota Certification #: R-150 South Carolina Certification #: 83006001 US Dept of Agriculture #: S-76505 Wisconsin Certification #: 405132750



SAMPLE SUMMARY

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Lab ID	Sample ID	Matrix	Date Collected	Date Received	
4092070001	B6-S1	Solid	02/11/14 07:30	02/13/14 08:40	
4092070002	B6-S2	Solid	02/11/14 07:45	02/13/14 08:40	
4092070003	B7-S1	Solid	02/11/14 08:15	02/13/14 08:40	
4092070004	B7-S2	Solid	02/11/14 08:30	02/13/14 08:40	
4092070005	B8-S1	Solid	02/11/14 09:00	02/13/14 08:40	
4092070006	B8-S2	Solid	02/11/14 09:15	02/13/14 08:40	
4092070007	B9-S1	Solid	02/11/14 09:45	02/13/14 08:40	
4092070008	B9-S2	Solid	02/11/14 10:00	02/13/14 08:40	
4092070009	B10-S1	Solid	02/11/14 10:30	02/13/14 08:40	
4092070010	B10-S2	Solid	02/11/14 10:45	02/13/14 08:40	



SAMPLE ANALYTE COUNT

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Lab ID	Sample ID	Method	Analysts	Analytes Reported	Laboratory
4092070001	B6-S1	EPA 8082	BLM	- 10	PASI-G
		EPA 6010	MMZ	9	PASI-G
		EPA 6010	MMZ	1	PASI-G
		EPA 7471	CMS	,1	PASI-G
		EPA 8270 by SIM	ARO	20	PASI-G
		ASTM D2974-87	skw	1	PASI-G
		EPA 9060 Modified	· TJJ	4	PASI-G
092070002	B6-S2	EPA 8082	BLM	10	PASI-G
		EPA 6010	MMZ	9	PASI-G
		EPA 6010	MMZ	1	PASI-G
		EPA 7471	CMS	1	PASI-G
		EPA 8270 by SIM	ARO	20	PASI-G
		ASTM D2974-87	SKW	1	PASI-G
		EPA 9060 Modified	TJJ	4	PASI-G
092070003	B7-S1	EPA 8082	BLM	10	PASI-G
		EPA 6010	MMZ	9	PASI-G
		EPA 6010	MMZ	1	PASI-G
		EPA 7471	CMS	. 1	PASI-G
	,	EPA 8270 by SIM	ARO	20	PASI-G
		ASTM D2974-87	SKW	1	PASI-G
		EPA 9060 Modified	TJJ	4	PASI-G
092070004	B7-S2	EPA 8082	BLM	10	PASI-G
		EPA 6010	MMZ	9	PASI-G
		EPA 6010	MMZ	. 1	PASI-G
		EPA 7471	CMS	1	PASI-G
		EPA 8270 by SIM	ARO	20	PASI-G
		ASTM D2974-87	SKW	1	PASI-G
		EPA 9060 Modified	TJJ	4	PASI-G
092070005	B8-S1	EPA 8082	BLM	. 10	PASI-G
		EPA 6010	MMZ	9	PASI-G
		EPA 6010	MMZ	1	PASI-G
		EPA 7471	CMS	1	PASI-G
		EPA 8270 by SIM	ARO	20	PASI-G
		ASTM D2974-87	skw	. 1	PASI-G
		EPA 9060 Modified	TJJ	4	PASI-G
092070006	B8-S2	- EPA 8082	BLM	10	PASI-G
		EPA 6010	MMZ	9	PASI-G



SAMPLE ANALYTE COUNT

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Lab ID	Sample ID		Method	Analysts	Analytes Reported	Laboratory
-			EPA 6010	MMZ	1	PASI-G
			EPA 7471	CMS	. 1	PASI-G
		· · · · · · · · · · · · · · · · · · ·	EPA 8270 by SIM	ARO	20	PASI-G
	•		ASTM D2974-87	SKW	. 1	PASI-G
			EPA 9060 Modified	TJJ	4	PASI-G
092070007	B9-S1		EPA 8082	BLM	10	PASI-G
			EPA 6010	MMZ	9	PASI-G
			EPA 6010	MMZ	1	PASI-G
			EPA 7471	CMS	1	PASI-G
			EPA 8270 by SIM	ARO	20	PASI-G
			ASTM D2974-87	SKW	. 1	PASI-G
			EPA 9060 Modified	TJJ	4	PASI-G
092070008	B9-S2		EPA 8082	BLM	10	PASI-G
			EPA 6010	MMZ	9	PASI-G
			EPA 6010	MMZ	. 1	PASI-G
			EPA 7471	CMS	1	PASI-G
			EPA 8270 by SIM	ARO	20	PASI-G
			ASTM D2974-87	SKW	1	PASI-G
			EPA 9060 Modified	TJJ	4	PASI-G
092070009	B10-S1		EPA 8082	BLM	10	PASI-G
		•	EPA 6010	MMZ	9	PASI-G
			EPA 6010	MMZ	. 1	PASI-G
	,		EPA 7471	CMS	1	PASI-G
			EPA 8270 by SIM	ARO	20	PASI-G
			ASTM D2974-87	SKW	1	PASI-G
			EPA 9060 Modified	TJJ	. 4	PASI-G
92070010	B10-S2		EPA 8082	BLM	10	PASI-G
			EPA 6010	MMZ	9	PASI-G
			EPA 6010	MMZ	1	PASI-G
			EPA 7471	CMS	1	PASI-G
			EPA 8270 by SIM	ARO	20	PASI-G
			ASTM D2974-87	skw	1	PASI-G
*			EPA 9060 Modified	TJJ	4	PASI-G



ANALYTICAL RESULTS

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B6-S1

Date: 02/26/2014 01:11 PM

Lab ID: 4092070001

Collected: 02/11/14 07:30

Received: 02/13/14 08:40

Matrix: Solid

viatrix. Solic

Results reported on a "dry-weight" basis

Parameters	Results L	Jnits LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8082 GCS PCB	Analytical Met	nod: EPA 8082 Pi	eparation Meth	hod: EP	A 3541		÷	
PCB-1016 (Aroclor 1016)	< 0.048 mg/kg	0.0	97 0.048	1	02/14/14 10:52	02/17/14 16:09	12674-11-2	•
PCB-1221 (Aroclor 1221)	<0.048 mg/kg	0.0	97 0.048	1	02/14/14 10:52	02/17/14 16:09	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.048 mg/kg		97 0.048	1	02/14/14 10:52	02/17/14 16:09	11141-16-5	
PCB-1242 (Aroclor 1242)	0.092J mg/kg	0.0	97 0.048	1	02/14/14 10:52	02/17/14 16:09	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.048 mg/kg		97 0.048	1	02/14/14 10:52	02/17/14 16:09	12672-29-6	
PCB-1254 (Aroclor 1254)	0.16 mg/kg		97 0.048	1	02/14/14 10:52	02/17/14 16:09	11097-69-1	
PCB-1260 (Aroclor 1260)	0.076J mg/kg		97 0.048	· 1	02/14/14 10:52	02/17/14 16:09	11096-82-5	
PCB, Total	0.33 mg/kg			1	02/14/14 10:52	02/17/14 16:09	1336-36-3	
Surrogates		-						
Tetrachloro-m-xylene (S)	72 %	40-1	30	1	02/14/14 10:52	02/17/14 16:09	877-09-8	
Decachlorobiphenyl (S)	79 %	48-1	30	. 1	02/14/14 10:52	02/17/14 16:09	2051-24-3	
010 MET ICP	Analytical Met	nod: EPA 6010 Pr	eparation Meth	nod: EP/	A 3050			
Arsenic	12.3 mg/kg	. 3	.6 0.98	1	02/14/14 08:57	02/14/14 18:24	7440-38-2	
Barium	76.0 mg/kg		91 0.16	1	02/14/14 08:57	02/14/14 18:24	7440-39-3	
Cadmium	1.4 mg/kg			1	02/14/14 08:57	02/14/14 18:24	7440-43-9	
Chromium	18.9 mg/kg			1	02/14/14 08:57	02/14/14 18:24	7440-47-3	
on	10200 mg/kg			1	02/14/14 08:57	02/14/14 18:24	7439-89-6	
ead	289 mg/kg	*	.8 0.53	1	02/14/14 08:57			
Manganese	243 mg/kg			1	02/14/14 08:57		7439-96-5	
Selenium	<1.1 mg/kg		.6 1.1	1	02/14/14 08:57	02/14/14 18:24		
Silver	<0.39 mg/kg		.8 0.39	1	02/14/14 08:57	02/14/14 18:24		
010 MET ICP, TCLP	Analytical Meth	nod: EPA 6010 Pr	eparation Meth	nod: EP/	A 3010		•	
	Leachate Meth	od/Date: EPA 131	1; 02/19/14 00	:00				
ead	0.30 mg/L	0.0	38 0.015	. 1	02/20/14 09:45	02/24/14 11:53	7439-92-1	
471 Mercury	Analytical Met	nod: EPA 7471 Pr	eparation Meth	nod: EP/	A 7471			
Mercury	0.13 mg/kg	0.0	10 0.0051	1	02/18/14 14:50	02/19/14 16:06	7439-97-6	
270 MSSV PAH by SIM	Analytical Meth	nod: EPA 8270 by	SIM Preparati	ion Meth	od: EPA 3546			
cenaphthene	0.078 mg/kg	0.06	35 0.032	1	02/19/14 09:27	02/20/14 11:29	83-32-9	
cenaphthylene	<0.029 mg/kg		35 0.029	1 -	02/19/14 09:27	02/20/14 11:29	208-96-8	
Inthracene	0.21 mg/kg		0.033	1	02/19/14 09:27	02/20/14 11:29	120-12-7	
Benzo(a)anthracene	0.60 mg/kg			1	02/19/14 09:27	02/20/14 11:29	56-55-3	
enzo(a)pyrene	0.67 mg/kg			1	02/19/14 09:27	02/20/14 11:29	50-32-8	
enzo(b)fluoranthene	0.74 mg/kg			- 1	02/19/14 09:27	02/20/14 11:29	205-99-2	
enzo(g,h,i)perylene	0.49 mg/kg			1	02/19/14 09:27			
Benzo(k)fluoranthene	0.55 mg/kg	*		1	02/19/14 09:27	02/20/14 11:29		
Chrysene	0.80 mg/kg			1	02/19/14 09:27			
Dibenz(a,h)anthracene	0.17 mg/kg			1	02/19/14 09:27	02/20/14 11:29		
	1.7 mg/kg			1	02/19/14 09:27	02/20/14 11:29		
morannene								
Fluoranthene Fluorene	0.083 mg/kg	0.06		1	02/19/14 09:27	02/20/14 11:29		



ANALYTICAL RESULTS

Project:

C7799-WING III WINGRA

Pace Project No.: 4092070

Sample: B6-S1

Lab ID: 4092070001

Collected: 02/11/14 07:30

Received: 02/13/14 08:40

Matrix: Solid

Results reported on a "dry-weight" basis

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical I	Method: EPA	8270 by SIM	Preparation	n Met	nod: EPA 3546			
1-Methylnaphthalene	<0.032 m	g/kg	0.065	0.032	1	02/19/14 09:27	02/20/14 11:29	90-12-0	
2-Methylnaphthalene	<0.032 m	g/kg	0.065	0.032	1	02/19/14 09:27	02/20/14 11:29	91-57-6	
Naphthalene	0.059J mg	g/kg	0.065	0.032	1	02/19/14 09:27	02/20/14 11:29	91-20-3	
Phenanthrene	0.80 mg	g/kg	0.065	0.032	1	02/19/14 09:27	02/20/14 11:29	85-01-8	
Pyrene Surrogates	1.3 mg	g/kg	0.065	0.032	1	02/19/14 09:27	02/20/14 11:29	129-00-0	
2-Fluorobiphenyl (S)	54 %		40-130	-	1	02/19/14 09:27	02/20/14 11:29	321-60-8	
Terphenyl-d14 (S)	53 %		40-130		1	02/19/14 09:27	02/20/14 11:29	1718-51-0	
Percent Moisture	Analytical I	Method: AST	M D2974-87						
Percent Moisture	48.4 %		0.10	0.10	1		02/13/14 14:24		
Total Organic Carbon	Analytical N	Method: EPA	N 9060 Modifie	d		٠.			
Surrogates									•
RPD%	18.5 %		0.10	0.10	1		02/20/14 10:44		
Total Organic Carbon	49400 mg	g/kg	20000	2490	1		02/20/14 10:39	7440-44-0	
Total Organic Carbon	59500 mg	-	16700	2070	1		02/20/14 10:44	7440-44-0	•
Mean Total Organic Carbon	54400 mg		18300	2280	1	•	02/20/14 10:44	7440-44-0	



ANALYTICAL RESULTS

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B6-S2

Date: 02/26/2014 01:11 PM

Lab ID: 4092070002

Collected: 02/11/14 07:45

Received: 02/13/14 08:40

Matrix: Solid

Results reported on a "dry-weight" basis

Parameters	Results Ur	nits LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual	
3082 GCS PCB	Analytical Metho	od: EPA 8082 Prepa	ration Meth	od: EP/	A 3541				
PCB-1016 (Aroclor 1016)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	12674-11-2		
PCB-1221 (Aroclor 1221)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	11104-28-2		
PCB-1232 (Aroclor 1232)	<0.031 mg/kg	0.062	0.031	· 1	02/14/14 10:52	02/17/14 16:26	11141-16-5		
PCB-1242 (Aroclor 1242)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	53469-21-9		
PCB-1248 (Aroclor 1248)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	12672-29-6		
PCB-1254 (Aroclor 1254)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	11097-69-1		
PCB-1260 (Aroclor 1260)	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52		11096-82-5		
PCB, Total	<0.031 mg/kg	0.062	0.031	1	02/14/14 10:52	02/17/14 16:26	1336-36-3		
Surrogates									
Tetrachloro-m-xylene (S)	72 %	40-130		1	02/14/14 10:52	02/17/14 16:26	877-09-8		
Decachlorobiphenyl (S)	83 %	48-130		1	02/14/14 10:52	02/17/14 16:26	2051-24-3		
6010 MET ICP	Analytical Metho	od: EPA 6010 Prepa	ration Meth	od: EP/	A 3050				
Arsenic	0.74J mg/kg	2.3	0.61	1	02/14/14 08:57	02/14/14 18:26	7440-38-2		
Barium	4.8 mg/kg	0.57	0.099	1	02/14/14 08:57	02/14/14 18:26			
Cadmium	0.22J mg/kg	0.57	0.058	1	02/14/14 08:57	02/14/14 18:26	*		
Chromium	3.5 mg/kg	0.57	0.14	1	02/14/14 08:57				
ron	1560 mg/kg	11.4	3.0	1	02/14/14 08:57				
_ead	19.6 mg/kg	1.1	0.33	1	02/14/14 08:57	02/14/14 18:26			
	70.0 mg/kg	0.57	0.035	1	02/14/14 08:57	02/14/14 18:26			
Manganese Selenium	<0.67 mg/kg	2.3	0.67	1	02/14/14 08:57	02/14/14 18:26			
· ·	<0.24 mg/kg	· 1.1	0.07	1	02/14/14 08:57	02/14/14 18:26			
Silver						02/14/14 10:20	7440-22-4		
6010 MET ICP, TCLP		od: EPA 6010 Prepa			A 3010				
3		d/Date: EPA 1311; 0			00/00/44 00:45	00/04/44 44440	7420 00 4		
_ead	0.083 mg/L	0.038	0.015	1	02/20/14 09:45	02/24/14 11:42	7439-92-1		
471 Mercury	Analytical Metho	od: EPA 7471 Prepa	ration Meth	od: EP/	A 7471				
Mercury	<0.0039 mg/kg	0.0077	0.0039	1	02/18/14 14:50	02/19/14 16:09	7439-97-6	2q	
3270 MSSV PAH by SIM	Analytical Metho	od: EPA 8270 by SIM	l Preparation	on Meth	od: EPA 3546				
Acenaphthene	<0.010 mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14: 4 8	83-32-9		
Acenaphthylene	<0.0093 mg/kg	0.021	0.0093	- 1	02/19/14 09:27	02/19/14 14:48	208-96-8		
Anthracene	<0.011 mg/kg	0.021	0.011	. 1	02/19/14 09:27	02/19/14 14:48	120-12-7		
Benzo(a)anthracene	0.0086J mg/kg	0.021	0.0072	1	02/19/14 09:27	02/19/14 14:48	56-55-3		
Benzo(a)pyrene	0.0084J mg/kg	0.021	0.0074	1	02/19/14 09:27	02/19/14 14:48	50-32-8		
Benzo(b)fluoranthene	<0.010 mg/kg	0.021	0.010	1 .	02/19/14 09:27	02/19/14 14:48	205-99-2		
Benzo(g,h,i)perylene	<0.0079 mg/kg	0.021	0.0079	1	02/19/14 09:27	02/19/14 14:48			
Benzo(k)fluoranthene	<0.011 mg/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 14:48			
Chrysene	0.010J mg/kg	0.021	0.0096	1	02/19/14 09:27	02/19/14 14:48			
Dibenz(a,h)anthracene	<0.0076 mg/kg	0.021	0.0076	1	02/19/14 09:27	02/19/14 14:48			
Fluoranthene	0.021 mg/kg	0.021	0.010	- 1	02/19/14 09:27	02/19/14 14:48			
Fluorene	<0.010 mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48			
				1	02/19/14 09:27	02/19/14 14:48			
ndeno(1,2,3-cd)pyrene	<0.0079 mg/kg	0.021	0.0079	1	02/19/14 09.2/	02/13/14 14.40	190-09-0		



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B6-S2

Lab ID: 4092070002

Collected: 02/11/14 07:45

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical Method:	EPA 8270 by SIM	1 Preparation	n Met	hod: EPA 3546			
1-Methylnaphthalene	<0.010 mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48	90-12-0	
2-Methylnaphthalene	<0.010 mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48	91-57-6	
Naphthalene	<0.010 mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48	91-20-3	
Phenanthrene	0.012J mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48	85-01-8	
Pyrene Surrogates	0.019 J mg/kg	0.021	0.010	1	02/19/14 09:27	02/19/14 14:48	129-00-0	
2-Fluorobiphenyl (S)	63 %	40-130		1	02/19/14 09:27	02/19/14 14:48	321-60-8	
Terphenyl-d14 (S)	63 %	40-130		1 .	02/19/14 09:27	02/19/14 14:48	1718-51-0	
Percent Moisture	Analytical Method:	ASTM D2974-87						
Percent Moisture	19.5 %	0.10	0.10	1	•	02/13/14 14:24		
Total Organic Carbon	Analytical Method:	EPA 9060 Modifie	∍d				•	
Surrogates					•			
RPD%	19.2 %	0.10	0.10	1		02/20/14 11:12		
Total Organic Carbon	935 mg/kg	375	46.6	1		02/20/14 11:08	7440-44-0	•
Total Organic Carbon	1130 mg/kg	382	47.5	1		02/20/14 11:12	7440-44-0	
Mean Total Organic Carbon	1030 mg/kg	378	47.0	1		02/20/14 11:12	7440-44-0	
						•		



Project:

C7799-WING III WINGRA

Pace Project No.:

Date: 02/26/2014 01:11 PM

4092070

Sample: B7-S1 Lab ID: 4092070003 Collected: 02/11/14 08:15 Received: 02/13/14 08:40

Matrix: Solid

Results reported on a "dry-weight" basis

ROB-S GCS PCB	Parameters	Results U	nits LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
PCB-1222 (Arodor 1221)	8082 GCS PCB	Analytical Meth	od: EPA 8082 Prepa	ration Meth	od: EP/	A 3541	•		
PCB-1232 ⟨Aroclor 1232⟩	PCB-1016 (Aroclor 1016)	<0.042 mg/kg	0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	12674-11-2	
PCB-1242 (Arocion 1242)	PCB-1221 (Aroclor 1221)	<0.042 mg/kg	0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	11104-28-2	•
PCB-1242 (Arocion 1242) PCB-1243 (Arocion 1242) PCB-1254 (Arocion 1243) PCB-1264 (Arocion 1254) PCB-1264 (Arocion 1254) PCB-1264 (Arocion 1260) PCB-1260 (Arocion 1260) PCB-1	PCB-1232 (Aroclor 1232)	<0.042 mg/kg	0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	11141-16-5	
PCB-1264 (Aroclor 1246)	The state of the s		0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	53469-21-9	
PCB-1264 (Aroclor 1264) PCB-1266 (Aroclor 1260)			0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	12672-29-6	
PCB-1260 (Anodor 1260) A.0.42 mg/kg 0.085 0.042 1 0.2144/14 10:52 0.2171/14 16:43 1308-82-5 PCB, Total N.0.65 mg/kg 0.085 0.042 1 0.2144/14 10:52 0.2171/14 16:43 1338-36-3 Surrogates N.0.65 mg/kg N.0.65 N.0.65 mg/kg N.0.65 N.0.65 mg/kg N.0.65 m			0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	11097-69-1	
PCB, Total		<0.042 mg/kg	0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	11096-82-5	
Surrogates Tetrachiror-maylene (S)	*		0.085	0.042	1	02/14/14 10:52	02/17/14 16:43	1336-36-3	
Decachiorobiphenyl (S) 85 % 48-130 1 02/14/14 10:52 02/17/14 16:43 0251-24-3	•								
Analytical Method: EPA 6010 Preparation Method: EPA 3050 Arsenic 7.0 mg/kg 3.2 0.86 1 02/14/14 08:57 02/14/14 18:28 7440-38-2 Barium 77.4 mg/kg 0.79 0.14 1 02/14/14 08:57 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7440-43-9 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-89-6 02/14/14 18:28 7439-92-1 02/14/14 08:57 02/14/14 18:28 7439-89-5 02/14/14 18:28 7439-92-1 02/14/14 08:57 02/14/14 18:28 7439-98-5 02/14/14 18:28 7439-92-1 02/14/14 08:57 02/14/14 18:28 7439-98-5 02/	Tetrachloro-m-xylene (S)	79 %	40-130		1	02/14/14 10:52	02/17/14 16:43	877-09-8	
Arsenic 7.0 mg/kg 3.2 0.86 1 02/14/14 08:57 02/14/14 18:28 7440-38-2 24 mg/kg 0.79 0.14 1 02/14/14 08:57 02/14/14 18:28 7440-38-3 02/14/14 18:28 7440-38-3 02/14/14 08:57 02/14/14 18:28 7440-38-3 02/14/14 08:57 02/14/14 18:28 7440-38-3 02/14/14 08:57 02/14/14 18:28 7440-38-3 02/14/14 08:57 02/14/14 18:28 7440-47-3 02/14/14 08:57 02/14/14 18:28 7440-47-3 02/14/14 08:57 02/14/14 18:28 7440-47-3 02/14/14 08:57 02/14/14 18:28 7439-38-6 02/14/14 08:57 02/14/14 18:28 7439-38-6 02/14/14 08:57 02/14/14 18:28 7439-39-1 02/14/14 08:57 02/14/14 18:28 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 08:57 02/14/14 18:28 02/14/14 18:28 02/14/14 18:28 02/14/	Decachlorobiphenyl (S)	85 %	48-130		. 1	02/14/14 10:52	02/17/14 16:43	2051-24-3	
Barium 77.4 mg/kg 0.79 0.14 1 02/14/14 08:57 02/14/14 18:28 7440-39-3 Cadmium 0.76 J mg/kg 0.79 0.081 1 02/14/14 08:57 02/14/14 18:28 7440-43-9 Chromium 14.9 mg/kg 0.79 0.20 1 02/14/14 08:57 02/14/14 18:28 7430-47-3 Iron 9180 mg/kg 15.9 4.3 1 02/14/14 08:57 02/14/14 18:28 7439-89-6 Lead 65.3 mg/kg 1.6 0.46 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-92-1 Silver 40.94 mg/kg 3.0 0.08 0.01 1 02/12/01/14 09:45 02/24/14 11:48 7439-92-1 <td>6010 MET ICP</td> <td>Analytical Meth</td> <td>od: EPA 6010 Prepa</td> <td>ration Meth</td> <td>od: EPA</td> <td>A 3050</td> <td></td> <td></td> <td></td>	6010 MET ICP	Analytical Meth	od: EPA 6010 Prepa	ration Meth	od: EPA	A 3050			
Barium 77.4 mg/kg 0.79 0.14 1 02/14/14 08:57 02/14/14 18:28 7440-39-3 Cadmium 0.76 J mg/kg 0.79 0.081 1 02/14/14 08:57 02/14/14 18:28 7440-43-9 Chromium 14.9 mg/kg 0.79 0.20 1 02/14/14 08:57 02/14/14 18:28 7430-47-3 Iron 9180 mg/kg 15.9 4.3 1 02/14/14 08:57 02/14/14 18:28 7439-89-6 Lead 65.3 mg/kg 1.6 0.46 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-98-5 Selenium 40.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-92-1 Silver 40.94 mg/kg 3.0 0.08 0.01 1 02/12/01/14 09:45 02/24/14 11:48 7439-92-1 <td>Arsenic</td> <td>7.0 ma/ka</td> <td>3.2</td> <td>0.86</td> <td>1</td> <td>02/14/14 08:57</td> <td>02/14/14 18:28</td> <td>7440-38-2</td> <td></td>	Arsenic	7.0 ma/ka	3.2	0.86	1	02/14/14 08:57	02/14/14 18:28	7440-38-2	
Cadmium		• •		0.14	1	02/14/14 08:57	02/14/14 18:28	7440-39-3	
Chromium					1	02/14/14 08:57	02/14/14 18:28	7440-43-9	
Iron									
Lead 66.3 mg/kg 1.6 0.46 1 02/14/14 08:57 02/14/14 18:28 7439-92-1 Manganese 257 mg/kg 0.79 0.049 1 02/14/14 08:57 02/14/14 18:28 7439-96-5 Selenium <0.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7439-92-1 Silver <0.94 mg/kg 1.6 0.34 1 02/14/14 08:57 02/14/14 18:28 7440-22-4 6010 MET ICP, TCLP Analytical Method: EPA 6010 Preparation Method: EPA 3010 Texas 3010 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>									
Manganese 257 mg/kg 0.79 0.049 1 02/14/14 08:57 02/14/14 18:28 7439-96-5 Selenium <0.94 mg/kg 3.2 0.94 1 02/14/14 08:57 02/14/14 18:28 7782-49-2 Silver <0.34 mg/kg 1.6 0.34 1 02/14/14 08:57 02/14/14 18:28 7439-96-5 6010 MET ICP, TCLP Analytical Method: EPA 6010 Preparation Method: EPA 1311; 02/19/14 00:00 EEA 3010 Call 14/14 08:57 02/14/14 18:28 7440-22-4 Lead 0.089 mg/L 0.038 0.015 1 02/20/14 09:45 02/24/14 11:44 7439-92-1 7471 Mercury Analytical Method: EPA 7471 Preparation Method: EPA 7471 Preparation Method: EPA 7471 Preparation Method: EPA 546 8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 EPA 3546 Acenaphthene 0.044.J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene <0.025 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 20-39-6-8 Anthracene					100				
Selenium									
Silver	•								
Analytical Method: EPA 6010 Preparation Method: EPA 3010 Leachate Method/Date: EPA 1311; 02/19/14 00:00 Lead						4.4			
Lead 0.089 mg/L 0.038 0.015 1 02/20/14 09:45 02/24/14 11:44 7439-92-1 7471 Mercury Analytical Method: EPA 7471 Preparation Method: EPA 7471 EPA 7471 Preparation Method: EPA 7471 Mercury 0.049 mg/kg 0.0086 0.0043 1 02/18/14 14:50 02/19/14 16:11 7439-97-6 8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 EPA 3546 Acenaphthene 0.044J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene 40.025 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Anthracene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(b)fluoranthene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>1 1 1 2 2 2 1</td><td></td></th<>								1 1 1 2 2 2 1	
Lead 0.089 mg/L 0.038 0.015 1 02/20/14 09:45 02/24/14 11:44 7439-92-1 7471 Mercury Analytical Method: EPA 7471 Preparation Method: EPA 7471 EPA 7471 Mercury 0.049 mg/kg 0.0086 0.0043 1 02/18/14 14:50 02/19/14 16:11 7439-97-6 8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 EPA 3546 Cenaphthene 0.044J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthene 0.024 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene 4.025 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Anthracene 0.13 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.05	6010 MET ICP, TCLP	·				4 3010		•	
7471 Mercury Analytical Method: EPA 7471 Preparation Method: EPA 7471 Mercury 0.049 mg/kg 0.0086 0.0043 1 02/18/14 14:50 02/19/14 16:11 7439-97-6 8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 Acenaphthene 0.044J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Acenaphthylene 40.025 mg/kg 0.057 0.025 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Anthracene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 120-12-7 Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0			•			00/00/44 00:45		7420 00 4	
Mercury 0.049 mg/kg 0.0086 0.0043 1 02/18/14 14:50 02/19/14 16:11 7439-97-6 8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 Acenaphthene 0.044J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene <0.025 mg/kg 0.057 0.025 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Anthracene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Benzo(a)anthracene 0.39 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.36 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 191-24-2	Lead	0.089 mg/L	0.038	0.015	. 1	02/20/14 09:45	02/24/14 11:44	/439-92-1	
8270 MSSV PAH by SIM Analytical Method: EPA 8270 by SIM Preparation Method: EPA 3546 Acenaphthene 0.044J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 83-32-9 Acenaphthylene <0.025 mg/kg	7471 Mercury	Analytical Meth	od: EPA 7471 Prepa	ration Meth	od: EPA	A 7471			
Acenaphthene	Mercury	0.049 mg/kg	0.0086	0.0043	1	02/18/14 14:50	02/19/14 16:11	7439-97-6	
Acenaphthylene <0.025 mg/kg 0.057 0.025 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Anthracene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 120-12-7 Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 191-24-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 50-32-8	8270 MSSV PAH by SIM	Analytical Meth	od: EPA 8270 by SIM	l Preparatio	on Meth	od: EPA 3546			
Acenaphthylene <0.025 mg/kg 0.057 0.025 g 2 02/19/14 09:27 02/20/14 10:55 208-96-8 Anthracene 0.13 mg/kg 0.057 0.029 g 2 02/19/14 09:27 02/20/14 10:55 120-12-7 Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 g 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 g 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 g 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 g 0.02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.021 g 0.021 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 g 0.02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.028 g 0.021 g 0.02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 g 0.021 12 02/19/14 09:27 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 10:55 02/20/14 02/20/20/20/20/20/20/20/20/20/20/20/20/2	Acenaphthene	0.044J mg/kg	0.057	0.028	2	02/19/14 09:27	02/20/14 10:55	83-32-9	•
Anthracene 0.13 mg/kg 0.057 0.029 2 02/19/14 09:27 02/20/14 10:55 120-12-7 Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7	•		0.057	0.025	2	02/19/14 09:27	02/20/14 10:55	208-96-8	
Benzo(a)anthracene 0.39 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 56-55-3 Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 191-24-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 36-73-7			0.057	0.029	2	02/19/14 09:27	02/20/14 10:55	120-12-7	
Benzo(a)pyrene 0.45 mg/kg 0.057 0.020 2 02/19/14 09:27 02/20/14 10:55 50-32-8 Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 191-24-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7						02/19/14 09:27	02/20/14 10:55	56-55-3	
Benzo(b)fluoranthene 0.47 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 205-99-2 Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 191-24-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7					•	02/19/14 09:27	02/20/14 10:55	50-32-8	
Benzo(g,h,i)perylene 0.36 mg/kg 0.057 0.022 2 02/19/14 09:27 02/20/14 10:55 191-24-2 Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7	_ i.i.i. i.			0.028	2	02/19/14 09:27	02/20/14 10:55	205-99-2	
Benzo(k)fluoranthene 0.43 mg/kg 0.057 0.031 2 02/19/14 09:27 02/20/14 10:55 207-08-9 Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7									
Chrysene 0.52 mg/kg 0.057 0.026 2 02/19/14 09:27 02/20/14 10:55 218-01-9 Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7							02/20/14 10:55	207-08-9	
Dibenz(a,h)anthracene 0.12 mg/kg 0.057 0.021 2 02/19/14 09:27 02/20/14 10:55 53-70-3 Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7	,								
Fluoranthene 1.1 mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 206-44-0 Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7			and the second s						
Fluorene 0.050J mg/kg 0.057 0.028 2 02/19/14 09:27 02/20/14 10:55 86-73-7		7 -						and the second s	
1.444.4.19.19									
	Indeno(1,2,3-cd)pyrene	0.32 mg/kg	0.057	0.021	2	02/19/14 09:27			



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B7-S1

Lab ID: 4092070003

Collected: 02/11/14 08:15

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical N	Method: EPA	A 8270 by SIM	Preparation	n Meth	nod: EPA 3546			
1-Methyinaphthalene	<0.028 mg	g/kg	0.057	0.028	2	02/19/14 09:27	02/20/14 10:55	90-12-0	
2-Methylnaphthalene	<0.028 mg	g/kg	0.057	0.028	2	02/19/14 09:27	02/20/14 10:55	91-57-6	
Naphthalene	0.052J mg	g/kg	0.057	0.028	2	02/19/14 09:27	02/20/14 10:55	91-20-3	
Phenanthrene	0.59 mg	g/kg	0.057	0.028	.2	02/19/14 09:27	02/20/14 10:55	85-01-8	
Pyrene Surrogates	0.86 mg	g/kg	0.057	0.028	2	02/19/14 09:27	02/20/14 10:55	129-00-0	
2-Fluorobiphenyl (S)	54 %		40-130		2	02/19/14 09:27	02/20/14 10:55	321-60-8	
Terphenyl-d14 (S)	47 %		40-130		2	02/19/14 09:27	02/20/14 10:55	1718-51-0	
Percent Moisture	Analytical N	Method: AS7	TM D2974-87						
Percent Moisture	41.1 %		0.10	0.10	1		02/13/14 14:25		
Total Organic Carbon	Analytical N	Method: EPA	A 9060 Modifie	d					
Surrogates									
RPD%	17.4 %		0.10	0.10	1		02/20/14 12:44		
Total Organic Carbon	34300 mg	g/kg	7690	956	1		02/20/14 12:40	7440-44-0	
Total Organic Carbon	28800 mg	g/kg	8330	1040	1		02/20/14 12:44	7440-44-0	
Mean Total Organic Carbon	31500 mg	g/kg	8010	996	1		02/20/14 12:44	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B7-S2

Lab ID: 4092070004

Collected: 02/11/14 08:30

Received: 02/13/14 08:40

Matrix: Solid

...

.....

.

Results	reported	on a	"dry-weight"	basis

Parameters	Results Ui	nits LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8082 GCS PCB	Analytical Meth	od: EPA 8082 Prepa	ration Meth	od: EP/	A 3541			
PCB-1016 (Aroclor 1016)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.039 mg/kg	0.078	0.039	. 1	02/14/14 10:52	02/17/14 17:01	12672-29-6	
PCB-1254 (Aroclor 1254)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	11097-69-1	
PCB-1260 (Aroclor 1260)	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	11096-82-5	
PCB, Total	<0.039 mg/kg	0.078	0.039	1	02/14/14 10:52	02/17/14 17:01	1336-36-3	
Surrogates								
Tetrachloro-m-xylene (S)	73 %	40-130		1	02/14/14 10:52	02/17/14 17:01	877-09-8	
Decachlorobiphenyl (S)	83 %	48-130		1	02/14/14 10:52	02/17/14 17:01	2051-24-3	
6010 MET ICP	Analytical Meth	od: EPA 6010 Prepa	ration Meth	od: EPA	A 3050			
Arsenic	4.4 mg/kg	2.7	0.74	1	02/14/14 08:57	02/14/14 18:30	7440-38-2	
Barium	38.0 mg/kg	0.68	0.12	1	02/14/14 08:57	02/14/14 18:30	7440-39-3	
Cadmium	0.33J mg/kg	0.68	0.070	1	02/14/14 08:57	02/14/14 18:30	7440-43-9	
Chromium	10.0 mg/kg	0.68	0.17	1	02/14/14 08:57	02/14/14 18:30	7440-47-3	
Iron	6680 mg/kg	13.7	3.7	1	02/14/14 08:57	02/14/14 18:30	7439-89-6	
Lead	13.5 mg/kg	1.4	0.40	1	02/14/14 08:57	02/14/14 18:30	7439-92-1	
Manganese	184 mg/kg	0.68	0.042	1	02/14/14 08:57	02/14/14 18:30	7439-96-5	
Selenium	<0.81 mg/kg	2.7	0.81	1	02/14/14 08:57	02/14/14 18:30	7782-49-2	,
Silver	<0.29 mg/kg	1.4	0.29	1	02/14/14 08:57	02/14/14 18:30	7440-22-4	
6010 MET ICP, TCLP	Analytical Metho	od: EPA 6010 Prepa	ration Metho	od: EPA	A 3010			
	Leachate Metho	od/Date: EPA 1311; 0	2/19/14 00:	00				
Lead	0.054 mg/L	0.038	0.015	1 ·	02/20/14 09:45	02/24/14 11:56	7439-92-1	1q
7471 Mercury	Analytical Metho	od: EPA 7471 Prepa	ration Metho	od: EPA	\ 7471			
Mercury	0.016 mg/kg	0.0084	0.0042	1	02/18/14 14:50	02/19/14 16:13	7439-97-6	2q
8270 MSSV PAH by SIM	Analytical Metho	od: EPA 8270 by SIM	l Preparatio	n Meth	od: EPA 3546			*
Acenaphthene	<0.013 mg/kg	0.026	0.013	. 1	02/19/14 09:27	02/19/14 15:05	83-32-9	
Acenaphthylene	<0.012 mg/kg	0.026	0.012	1	02/19/14 09:27	02/19/14 15:05	208-96-8	
Anthracene	<0.013 mg/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	120-12-7	
Benzo(a)anthracene	0.025J mg/kg	0.026	0.0090	1	02/19/14 09:27	02/19/14 15:05	56-55-3	
Benzo(a)pyrene	0.026J mg/kg	0.026	0.0093	1	02/19/14 09:27	02/19/14 15:05	50-32-8	
Benzo(b)fluoranthene	0.029 mg/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	205-99-2	
Benzo(g,h,i)perylene	0.018J mg/kg	0.026	0.0099	1	02/19/14 09:27	02/19/14 15:05		
Benzo(k)fluoranthene	0.024J mg/kg	0.026	0.014	1	02/19/14 09:27	02/19/14 15:05		
Chrysene	0.032 mg/kg	0.026	0.012	. 1	02/19/14 09:27	02/19/14 15:05		9
	<0.0095 mg/kg	0.026	0.0095	1	02/19/14 09:27	02/19/14 15:05		•
Dibenzia.maniniacene								
Dibenz(a,h)anthracene Fluoranthene	0.070 ma/ka	0 026	0.013	1	02/19/14 09:27	02/19/14 15:05	ZUO-44-U	
Dibenz(a,r)antifiacerie Fluoranthene Fluorene	0.070 mg/kg <0.013 mg/kg	0.026 0.026	0.013 0.013	1 1	02/19/14 09:27 02/19/14 09:27	02/19/14 15:05 02/19/14 15:05		



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B7-S2

Lab ID: 4092070004

Collected: 02/11/14 08:30

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical	Method: EPA	8270 by SIM	Preparatio	n Meth	od: EPA 3546			
1-Methylnaphthalene	< 0.013 m	g/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	90-12-0	
2-Methylnaphthalene	<0.013 m	g/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	91-57-6	
Naphthalene	<0.013 m	g/kg	0.026	0.013	1.	02/19/14 09:27	02/19/14 15:05	91-20-3	
Phenanthrene	0.037 m	g/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	85-01-8	
Pyrene Surrogates	0.059 m	g/kg	0.026	0.013	1	02/19/14 09:27	02/19/14 15:05	129-00-0	
2-Fluorobiphenyl (S)	58 %		40-130		1	02/19/14 09:27	02/19/14 15:05	321-60-8	
Terphenyl-d14 (S)	50 %		40-130		1	02/19/14 09:27	02/19/14 15:05	1718-51-0	
Percent Moisture	Analytical I	Method: AST	M D2974-87						
Percent Moisture	35.8 %		0.10	0.10	1		02/13/14 14:25		
Total Organic Carbon	Analytical I	Method: EPA	9060 Modifie	d		*,			
Surrogates								•	
RPD%	32.8 %		0.10	0.10	1		02/20/14 12:55		
Total Organic Carbon	20200 m	g/kg	9090	1130	1		02/20/14 12:47	7440-44-0	
Total Organic Carbon	28100 mg	g/kg	7140	888	1		02/20/14 12:55	7440-44-0	
Mean Total Organic Carbon	24200 m		8120	1010	1		02/20/14 12:55	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B8-S1

Lab ID: 4092070005

Collected: 02/11/14 09:00

Received: 02/13/14 08:40

Matrix: Solid

Results reported on a "dry-weight" basis

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qu
3082 GCS PCB	Analytical N	Method: EPA	8082 Prepa	ration Meth	od: EP/	A 3541	4.		
PCB-1016 (Aroclor 1016)	<0.035 mg	a/kg	0.071	0.035	1	02/14/14 10:52	02/17/14 17:18	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.035 mg	g/kg	0.071	0.035	1	02/14/14 10:52	02/17/14 17:18	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.035 mg		0.071	0.035	1	02/14/14 10:52	02/17/14 17:18	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.035 mg		0.071	0.035	1	02/14/14 10:52	02/17/14 17:18	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.035 mg		0.071	0.035	1	02/14/14 10:52	02/17/14 17:18	12672-29-6	
PCB-1254 (Aroclor 1254)	<0.035 mg		0.071	0.035	1	02/14/14 10:52		11097-69-1	
PCB-1260 (Aroclor 1260)	<0.035 mg	, ,	0.071	0.035	1			11096-82-5	
PCB, Total	<0.035 mg		0.071	0.035	1	02/14/14 10:52		1336-36-3	
Surrogates	10.000 1115	,,,,9	0.01	0.000	·				
etrachloro-m-xylene (S)	73 %	-	40-130	• .	1	02/14/14 10:52	02/17/14 17:18	877-09-8	
Decachlorobiphenyl (S)	82 %		48-130		1	02/14/14 10:52	02/17/14 17:18	2051-24-3	
010 MET ICP	Analytical N	Method: EPA	\ 6010 Prepai	ration Meth	od: EP/	A 3050			
rsenic	6.8 mg	ı/ka	2.6	0.71	1	02/14/14 08:57	02/14/14 18:33	7440-38-2	
Barium	57.4 mg		0.66	0.11	1 .	02/14/14 08:57	02/14/14 18:33		
Cadmium	0.35J mg	, ,	0.66	0.067	1	02/14/14 08:57			
Chromium	13.1 mg	-	0.66	0.16	1	02/14/14 08:57			
	9140 mg	-	13.1	3.5	1	02/14/14 08:57			
on			1.3	0.38	1	02/14/14 08:57	02/14/14 18:33		
ead 4	6.3 mg		0.66	0.040	1	02/14/14 08:57	02/14/14 18:33		
Manganese	220 mg				1		02/14/14 18:33	t	
elenium	<0.78 mg		2.6	0.78		02/14/14 08:57			
ilver	<0.28 mg	укд	1.3	0.28	1	02/14/14 08:57	02/14/14 18:33	1440-22-4	
010 MET ICP, TCLP			6010 Prepar			3010			
	Leachate M	lethod/Date:	: EPA 1311; 02	2/19/14 00:	00	~			
ead	<0.015 mg	J/L	0.038	0.015	1	02/20/14 09:45	02/24/14 11:46	7439-92-1	
471 Mercury	Analytical N	/lethod: EPA	7471 Prepar	ation Meth	od: EPA	A 7471		•	
Mercury	0.0089 mg	ı/kg	0.0073	0.0036	1	02/18/14 14:50	02/19/14 16:21	7439-97-6	2q
270 MSSV PAH by SIM	Analytical N	Method: EPA	8270 by S IM	Preparation	n Meth	od: EPA 3546			
cenaphthene	<0.012 mg	ı/kg	0,024	0.012	1	02/19/14 09:27	02/19/14 15:23	83-32-9	
cenaphthylene	<0.011 mg	ı/kg	0.024	0.011	1	02/19/14 09:27	02/19/14 15:23	208-96-8	
nthracene	<0.012 mg	/kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	120-12-7	
enzo(a)anthracene	<0.0082 mg	ı/kg	0.024	0.0082	1 1	02/19/14 09:27	02/19/14 15:23	56-55-3	
enzo(a)pyrene	-<0.0084 mg		0.024	0.0084	1	02/19/14 09:27	02/19/14 15:23	50-32-8	
enzo(b)fluoranthene	<0.012 mg	· . -	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	205-99-2	
enzo(g,h,i)perylene	<0.0090 mg		0.024	0.0090	1	02/19/14 09:27	02/19/14 15:23		
enzo(k)fluoranthene	<0.013 mg		0.024	0.013	-1	02/19/14 09:27	02/19/14 15:23		
chrysene	<0.011 mg		0.024	0.011	1	02/19/14 09:27			
Dibenz(a,h)anthracene	<0.0086 mg		0.024	0.0086	1	02/19/14 09:27	02/19/14 15:23		
luoranthene	<0.012 mg		0.024	0.0000	1	02/19/14 09:27	02/19/14 15:23		
		•	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23		
luorene	<0.012 mg <0.0089 mg		0.024	0.012	1	02/19/14 09:27	02/19/14 15:23		
ndeno(1,2,3-cd)pyrene	<0.0089 ma	UKA.	0.024	0.0089	-1	02/19/14 09:27	uz/19/14 15:23	130-03-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B8-S1

Lab ID: 4092070005

Collected: 02/11/14 09:00

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical Me	ethod: EPA 82	70 by SIM	Preparatio	n Meth	nod: EPA 3546			
1-Methylnaphthalene	<0.012 mg/l	kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	90-12-0	
2-Methylnaphthalene	<0.012 mg/l	kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	91-57-6	
Naphthalene	<0.012 mg/l	kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	91-20-3	
Phenanthrene	<0.012 mg/l	kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	85-01-8	
Pyrene Surrogates	<0.012 mg/l	kg	0.024	0.012	1	02/19/14 09:27	02/19/14 15:23	129-00-0	
2-Fluorobiphenyl (S)	60 .%		40-130		1	02/19/14 09:27	02/19/14 15:23	321-60-8	
Terphenyi-d14 (S)	58 %		40-130		1 .	02/19/14 09:27	02/19/14 15:23	1718-51-0	
Percent Moisture	Analytical Me	ethod: ASTM [2974-87						
Percent Moisture	29.2 %		0.10	0:10	1		02/13/14 14:25		
Total Organic Carbon	Analytical Me	ethod: EPA 90	30 Modifie	d			• .	•	
Surrogates									
RPD%	22.4 %		0.10	0.10	. 1		02/20/14 13:02		
Total Organic Carbon	8600 mg/l	kg	4760	592	1		02/20/14 12:58	7440-44-0	
Total Organic Carbon	10800 mg/l	kg	4350	541	1		02/20/14 13:02	7440-44-0	
Mean Total Organic Carbon	9690 mg/l	kg	4550	566	1		02/20/14 13:02	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B8-S2 Lab ID: 4092070006 Collected: 02/11/14 09:15 Received: 02/13/14 08:40 Matrix: Solid

Results reported on a "dry-weight" basis

Parameters	Results Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8082 GCS PCB	Analytical Method: EP	A 8082 Prepa	ration Meth	od: EP/	A 3541			
PCB-1016 (Aroclor 1016)	<0.032 mg/kg	0.064	0.032	1.	02/14/14 10:52	02/17/14 17:35	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	12672-29-6	
PCB-1254 (Arocior 1254)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	11097-69-1	
PCB-1260 (Aroclor 1260)	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	11096-82-5	
PCB, Total	<0.032 mg/kg	0.064	0.032	1	02/14/14 10:52	02/17/14 17:35	1336-36-3	
Surrogates			•					
Tetrachioro-m-xylene (S)	72 %	40-130		1	02/14/14 10:52	02/17/14 17:35	877-09-8	
Decachlorobiphenyl (S)	84 %	48-130		1	02/14/14 10:52	02/17/14 17:35	2051-24-3	
6010 MET ICP	Analytical Method: EPA	4 6010 Prepai	ration Metho	od: EP/	A 3050	i i		
Arsenic	5.8 mg/kg	2.2	0.59	1	02/14/14 08:57	02/14/14 18:35	7440-38-2	
Barium	10.1 mg/kg	0.55	0.095	1	02/14/14 08:57	02/14/14 18:35	7440-39-3	
Cadmium	0.076J mg/kg	0.55	0.056	. 1	02/14/14 08:57	02/14/14 18:35	7440-43-9	
Chromium	3.7 mg/kg	0.55	0.14	1	02/14/14 08:57	02/14/14 18:35	7440-47-3	
Iron	2890 mg/kg	11.0	2.9	1	02/14/14 08:57	02/14/14 18:35	7439-89-6	
Lead	1.4 mg/kg	. 1.1	0.32	1	02/14/14 08:57	02/14/14 18:35	7439-92-1	
Manganese	111 mg/kg	0.55	0.034	1	02/14/14 08:57	02/14/14 18:35	7439-96-5	
Selenium	<0.65 mg/kg	2.2	0.65	1	02/14/14 08:57	02/14/14 18:35	7782-49-2	
Silver	<0.23 mg/kg	1.1	0.23	1	02/14/14 08:57	02/14/14 18:35	7440-22-4	
6010 MET ICP, TCLP	Analytical Method: EPA	4 6010 Prepar	ration Metho	od: EPA	A 3010			
	Leachate Method/Date	:: EPA 1311; 02	2/19/14 00:0	00				
Lead	<0.015 mg/L	0.038	0.015	1	02/20/14 09:45	02/24/14 11:49	7439-92-1	
7471 Mercury	Analytical Method: EPA	A 7471 Prepar	ation Metho	od: EP/	A 7471			
Mercury	<0.0035 mg/kg	0.0071	0.0035	1.	02/18/14 14:50	02/19/14 16:23	7439-97-6	2q
8270 MSSV PAH by SIM	Analytical Method: EPA	3 8270 by S IM	Preparatio	n Meth	od: EPA 3546			
Acenaphthene	<0.011 mg/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	83-32-9	
Acenaphthylene	<0.0095 mg/kg	0.021	0.0095	1	02/19/14 09:27	02/19/14 15:40	208-96-8	
Anthracene	<0.011 mg/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	120-12-7	
Benzo(a)anthracene	<0.0074 mg/kg	0.021	0.0074	1	02/19/14 09:27	02/19/14 15:40		
Benzo(a)pyrene	<0.0076 mg/kg	0.021	0.0076	1	02/19/14 09:27	02/19/14 15:40	50-32-8	
Benzo(b)fluoranthene	<0.011 mg/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	205-99-2	
Benzo(g,h,i)perylene	<0.0081 mg/kg	0.021	0.0081	1	02/19/14 09:27	02/19/14 15:40		
Benzo(k)fluoranthene	<0.012 mg/kg	0.021	0.012	1	02/19/14 09:27	02/19/14 15:40	207-08-9	
• •	<0.0098 mg/kg	0.021	0.0098	1	02/19/14 09:27	02/19/14 15:40		
Chrysene	• •	0.021	0.0078	1	02/19/14 09:27	02/19/14 15:40		
· ·	<0.0078 ma/ka						_	
Dibenz(a,h)anthracene	<0.0078 mg/kg <0.011 ma/ka			1	02/19/14 09:27	02/19/14 15:40	206-44-0	
Chrysene Dibenz(a,h)anthracene Fluoranthene Fluorene	<0.011 mg/kg <0.011 mg/kg <0.011 mg/kg	0.021 0.021	0.011 0.011	1 1	02/19/14 09:27 02/19/14 09:27	02/19/14 15:40 02/19/14 15:40		



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B8-S2

Lab ID: 4092070006

Collected: 02/11/14 09:15

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
270 MSSV PAH by SIM	Analytical I	Method: EPA	A 8270 by SIM	Preparation	n Meth	nod: EPA 3546			•
-Methylnaphthalene	<0.011 mg	g/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	90-12-0	
-Methylnaphthalene	<0.011 mg	g/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	91-57-6	
laphthalene	<0.011 mg	g/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	91-20-3	
Phenanthrene	<0.011 mg	g/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	85-01-8	
Pyrene Surrogates	< 0.011 mg	g/kg	0.021	0.011	1	02/19/14 09:27	02/19/14 15:40	129-00-0	
-Fluorobiphenyl (S)	67 %		40-130		1.	02/19/14 09:27	02/19/14 15:40	321-60-8	
erphenyl-d14 (S)	70 %		40-130		1	02/19/14 09:27	02/19/14 15:40	1718-51-0	
ercent Moisture	Analytical I	Method: AS7	ГМ D2974-87			• •			
Percent Moisture	21.7 %		5 0,10	0.10	1	•	02/13/14 14:25		
otal Organic Carbon	Analytical N	Method: EPA	A 9060 Modifie	ed .				÷	
Surrogates									
RPD%	7.5 %		0.10	0.10	. 1		02/20/14 13:09	ν.	
otal Organic Carbon	863 mg	g/kg	345	42.9	1	•	02/20/14 13:07	7440-44-0	
otal Organic Carbon	800 mg		356	44.2	1		02/20/14 13:09	7440-44-0	
Mean Total Organic Carbon	832 mg	a/ka	350	43.6	1		02/20/14 13:09	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B9-S1

Lab ID: 4092070007

Collected: 02/11/14 09:45

Received: 02/13/14 08:40

Matrix: Solid

allix. Soliu

Results reported on a "dry-weight" basis

Parameters	Results Units	LOQ:	LOD	DF	Prepared	Analyzed	CAS No.	Qua
3082 GCS PCB	Analytical Method: El	PA 8082 Prepa	ration Meth	od: EP/	A 3541			
PCB-1016 (Aroclor 1016)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	12674-11-2	
PCB-1221 (Arocior 1221).	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	12672-29-6	
PCB-1254 (Aroclór 1254)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	11097-69-1	
PCB-1260 (Aroclor 1260)	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	11096-82-5	
PCB, Total Surrogates	<0.037 mg/kg	0.075	0.037	1	02/14/14 10:52	02/17/14 17:53	1336-36-3	
Tetrachloro-m-xylene (S) ⁻	72 %	40-130		1	02/14/14 10:52	02/17/14 17:53	877-09-8	
Decachlorobiphenyl (S)	78 %	48-130		1	02/14/14 10:52	02/17/14 17:53	2051-24-3	
010 MET ICP	Analytical Method: Ef	PA 6010 Prepa	ration Meth	od: EP/	A 3050			
Arsenic	7.3 mg/kg	2.5	0.68	1	02/14/14 08:57	02/14/14 18:37	7440-38-2	
Barium	72.6 mg/kg	0.63	0.11	1	02/14/14 08:57	02/14/14 18:37	7440-39-3	
Cadmium	0.51J mg/kg	0.63	0.064	1	02/14/14 08:57	02/14/14 18:37	7440-43-9	
Chromium	22.6 mg/kg	0.63	0.16	1	02/14/14 08:57	02/14/14 18:37	7440-47-3	
ron	16000 mg/kg	12.6	3.4	1	02/14/14 08:57	02/14/14 18:37	7439-89-6	
_ead	22.8 mg/kg	1.3	0.37	1	02/14/14 08:57	02/14/14 18:37	7439-92-1	
<i>M</i> anganese	527 mg/kg	0.63	0.039	1	02/14/14 08:57	02/14/14 18:37	7439-96-5	
Selenium	<0.75 mg/kg	2.5	0.75	1	02/14/14 08:57	02/14/14 18:37	7782-49-2	
Silver	<0.27 mg/kg	1.3	0.27	1	02/14/14 08:57	02/14/14 18:37	7440-22-4	
010 MET ICP, TCLP	Analytical Method: EF	PA 6010 Prepai	ration Metho	od: EPA	A 3010			
	Leachate Method/Dat	te: EPA 1311; 0	2/19/14 00:	00				
∟ead	0.038 mg/L	0.038	0.015	1	02/20/14 09:45	02/24/14 11:51	7439-92-1	
471 Mercury	Analytical Method: EF	PA 7471 Prepai	ation Metho	od: EPA	\ 7471			
Mercury	0.029 mg/kg	0.0080	0.0040	1	02/18/14 14:50	02/19/14 16:27	7439-97-6	2q
270 MSSV PAH by SIM	Analytical Method: EF	PA 8270 by SIM	Preparatio	n M eth	od: EPA 3546			
Acenaphthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	83-32-9	
Acenaphthylene	<0.011 mg/kg	0.025	0.011	1	02/19/14 09:27	02/19/14 15:57	208-96-8	
Anthracene	<0.013 mg/kg	0.025	0.013	-1	02/19/14 09:27	02/19/14 15:57	120-12-7	
Benzo(a)anthracene	0.039 mg/kg	0.025	0.0086	1	02/19/14 09:27	02/19/14 15:57	56-55-3	
Зепzo(a)pyrene	0.048 mg/kg	0.025	0.0089	1	02/19/14 09:27	02/19/14 15:57	50-32-8	
Benzo(b)fluoranthene	0.063 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57		
Benzo(g,h,i)perylene	0.039 mg/kg	0.025	0.0095	. 1	02/19/14 09:27	02/19/14 15:57	191-24-2	
Benzo(k)fluoranthene	0.050 mg/kg	0.025	0.014	1	02/19/14 09:27	02/19/14 15:57	207-08-9	
Chrysene	0.069 mg/kg	0.025	0.012	1 '	02/19/14 09:27	02/19/14 15:57		
Dibenz(a,h)anthracene	0.010J mg/kg	0.025	0.0091	1	02/19/14 09:27	Ph.		•
luoranthene	0.13 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57		
	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57		
Fluorene								



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B9-S1

Lab ID: 4092079007

Collected: 02/11/14 09:45

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical N	Method: EPA	8270 by SIM	Preparation	n Metļ	nod: EPA 3546			
1-Methylnaphthalene	<0.012 mg	g/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	90-12-0	
2-Methylnaphthalene	<0.012 mg	g/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	91-57-6	
Naphthalene	<0.012 mg	g/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	91-20-3	
Phenanthrene	0.051 mg	g/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	85-01-8	-
Pyrene Surrogates	0.11 mg	g/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 15:57	129-00-0	÷
2-Fluorobiphenyl (S)	63 %		40-130		1	02/19/14 09:27	02/19/14 15:57	321-60-8	
Terphenyl-d14 (S)	68 %		40-130.		1	02/19/14 09:27	02/19/14 15:57	1718-51-0	,
Percent Moisture	Analytical M	//lethod: AST	M D2974-87						
Percent Moisture	33.0 %		0.10	0.10	1		02/13/14 14:25		
Total Organic Carbon	Analytical M	/lethod: EPA	9060 Modifie	d					•
Surrogates									
RPD%	28.2 %		0.10	0.10	1		02/20/14 13:15		
Total Organic Carbon	18900 mg	j/kg	7140	888	1		02/20/14 13:12	7440-44-0	
Total Organic Carbon	. 25100 mg	/kg	6250	777	1 .		02/20/14 13:15	7440-44-0	
Mean Total Organic Carbon	22000 mg	J/kg	6700	833	1		02/20/14 13:15	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B9-S2

Lab ID: 4092070008

Collected: 02/11/14 10:00

Received: 02/13/14 08:40

Results reported on a "dry-weight" basis

Parameters	Results Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qua
3082 GCS PCB	Analytical Method: EP	A 8082 Prepa	ration Metho	od: EPA	3541			
PCB-1016 (Ároclor 1016)	<0.037 mg/kg	0.074	0.037	1 -	02/14/14 10:52	02/17/14 18:10	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	11104-28-2	
CB-1232 (Aroclor 1232)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.037 mg/kg	0.074	0.037	-1	02/14/14 10:52	02/17/14 18:10	12672-29-6	
PCB-1254 (Aroclor 1254)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	11097-69-1	
PCB-1260 (Aroclor 1260)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	11096-82-5	
CB, Total Surrogates	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:10	1336-36-3	-
etrachloro-m-xylene (S)	74 %	40-130		1	02/14/14 10:52	02/17/14 18:10	877-09-8	
ecachlorobiphenyl (S)	84 %	48-130		1	02/14/14 10:52	02/17/14 18:10	2051-24-3	
010 MET ICP	Analytical Method: EP	A 6010 Prepai	ration Metho	od: EPA	3050			
rsenic	9.4 mg/kg	2.8	0.75	1	02/14/14 08:57	02/14/14 18:39	7440-38-2	
arium	128 mg/kg	0.69	0.12	1	02/14/14 08:57	02/14/14 18:39	7440-39-3	
admium	0.50J mg/kg	0.69	0.070	1	02/14/14 08:57	02/14/14 18:39	7440-43-9	
chromium	18.1 mg/kg	0.69	0.17	1	02/14/14 08:57	02/14/14 18:39	7440-47-3	
on	14400 mg/kg	13.8	3.7	1	02/14/14 08:57		7439-89-6	
ead	9.1 mg/kg	1.4	0.41	1	02/14/14 08:57			
langanese	495 mg/kg	0.69	0.043	1		02/14/14 18:39		
elenium	<0.82 mg/kg	2.8	0.82	1	02/14/14 08:57			
ilver	<0.30 mg/kg	1.4	0.30	1	02/14/14 08:57			
010 MET ICP, TCLP	Analytical Method: EPA	4 6010 Prepar	ation Metho	od: EPA	3010			
	Leachate Method/Date	e: EPA 1311; 0	2/20/14 00:0	00				
ead	<0.015 mg/L	0.038	0.015	1	02/21/14 08:30	02/24/14 12:18	-7439-92-1	
471 Mercury	Analytical Method: EPA	A 7471 Prepar	ation Metho	od: EPA	7471			
lercury	0.019 mg/kg	0.0082	0.0041	1	02/18/14 14:50	02/19/14 16:29	7439-97-6	2q
270 MSSV PAH by SIM	Analytical Method: EPA	A 8270 by SIM	Preparatio	n Meth	od: EPA 3546			
cenaphthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	83-32-9	
cenaphthylene	<0.011 mg/kg	0.025	0.011	1	02/19/14 09:27	02/19/14 16:14	208-96-8	
nthracene	<0.013 mg/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:14	120-12-7	
enzo(a)anthracene	<0.0085 mg/kg	0.025	0.0085	1	02/19/14 09:27	02/19/14 16:14	56-55-3	
enzo(a)pyrene	<0.0088 mg/kg	0.025	0.0088	1	02/19/14 09:27	02/19/14 16:14	50-32-8	
enzo(b)fluoranthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	205-99-2	
enzo(g,h,i)perylene	<0.0094 mg/kg	0.025	0.0094	1	02/19/14 09:27	02/19/14 16:14	191-24-2	
enzo(k)fluoranthene	< 0.014 mg/kg	0.025	0.014	1	02/19/14 09:27	02/19/14 16:14	207-08-9	
hrysene	< 0.011 mg/kg	0.025	0.011	. 1	02/19/14 09:27	02/19/14 16:14	218-01-9	
ibenz(a,h)anthracene	<0.0090 mg/kg	0.025	0.0090	1	02/19/14 09:27	02/19/14 16:14		
luoranthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14		
	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14		
luorene	~0.012 ma/kg	0.02.0	0.012	1				



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B9-S2

Lab ID: 4092070008

Collected: 02/11/14 10:00

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results Units	LOQ	ĻOD	DF	Prepared	Analyzed .	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical Method:	EPA 8270 by SIM	Preparatio	n Metl	nod: EPA 3546			
1-Methylnaphthalene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	90-12-0	
2-Methylnaphthalene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	91-57-6	
Naphthalene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	91-20-3	
Phenanthrene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	85-01-8	
Pyrene Surrogates	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:14	129-00-0	
2-Fluorobiphenyl (S)	64 %	40-130		1	02/19/14 09:27	02/19/14 16:14	321-60-8	
Terphenyl-d14 (S)	69 %	40-130		1	02/19/14 09:27	02/19/14 16:14	1718-51-0	
Percent Moisture	Analytical Method:	ASTM D2974-87						
Percent Moisture	32.1 %	0.10	0.10	1		02/13/14 14:25		
Total Organic Carbon	Analytical Method:	EPA 9060 Modifie	ed					
Surrogates								
RPD%	2.1 %	0.10	0.10	1		02/20/14 13:22		
Total Organic Carbon	6600 mg/kg	2440	303	1		02/20/14 13:18	7440-44-0	
Total Organic Carbon	6730 mg/kg	2630	327	1		02/20/14 13:22	7440-44-0	
Mean Total Organic Carbon	6660 mg/kg	2540	315	1		02/20/14 13:22	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B10-S1

Lab ID: 4092070009

Collected: 02/11/14 10:30

Received: 02/13/14 08:40

Results reported on a "dry-weight" basis

Parameters	Results	Units LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8082 GCS PCB	Analytical Met	thod: EPA 8082 Prepa	ration Meth	od: EP	A 3541			
PCB-1016 (Aroclor 1016)	<0.037 mg/kg	g 0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.037 mg/kg		0.037	1	02/14/14 10:52	02/17/14 18:28	11104-28-2	
PCB-1232 (Aroclor 1232)	<0.037 mg/kg	g 0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.037 mg/kg	g 0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	12672-29-6	
PCB-1254 (Aroclor 1254)	<0.037 mg/kg	0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	11097-69-1	
PCB-1260 (Aroclor 1260)	<0.037 mg/kg		0.037	1	02/14/14 10:52	02/17/14 18:28	11096-82-5	
PCB, Total	<0.037 mg/kg	g 0.074	0.037	1	02/14/14 10:52	02/17/14 18:28	1336-36-3	
Surrogates								
Tetrachloro-m-xylene (S)	75 %	40-130		1	02/14/14 10:52	02/17/14 18:28	877-09-8	
Decachlorobiphenyl (S)	85 %	48-130		1	02/14/14 10:52	02/17/14 18:28	2051-24-3	
6010 MET ICP	Analytical Met	hod: EPA 6010 Prepa	ration Meth	od: EP/	A 3050			
Arsenic	7.7 mg/kg	2.9	0.78	1	02/14/14 08:57	02/14/14 18:42	7440-38-2	
Barium	101 mg/kg		0.13	1	02/14/14 08:57	02/14/14 18:42	7440-39-3	
Cadmium	0.50J mg/kg	0.72	0.074	1	02/14/14 08:57	02/14/14 18:42	7440-43-9	
Chromium	20.0 mg/kg		0.18	1	02/14/14 08:57	02/14/14 18:42	7440-47-3	
Iron	14000 mg/kg	14.5	3.9	1	02/14/14 08:57	02/14/14 18:42	7439-89-6	
Lead	15.3 mg/kg		0.42	1	02/14/14 08:57	02/14/14 18:42	7439-92-1	
Manganese	354 mg/kg		0.045	1	02/14/14 08:57	02/14/14 18:42	7439-96-5	
Selenium	<0.86 mg/kg	=	0.86	1	02/14/14 08:57	02/14/14 18:42	7782-49-2	
Silver	<0.31 mg/kg	1.4	0.31	1	02/14/14 08:57	02/14/14 18:42		
6010 MET ICP, TCLP	Analytical Met	hod: EPA 6010 Prepa	ration Metho	od: EP/	A 3010		entralise.	
	Leachate Met	nod/Date: EPA 1311; 0	2/20/14 00:	00				
Lead	0.015J mg/L	0.038	0.015	. 1	02/21/14 08:30	02/24/14 12:29	7439-92-1	
7471 Mercury	Analytical Met	hod: EPA 7471 Prepa	ration Metho	od: EPA	4 7471			
Mercury	0.018 mg/kg	0.0097	0.0049	1	02/18/14 14:50	02/19/14 16:31	7439-97-6	2q
8270 MSSV PAH by SIM	Analytical Met	hod: EPA 8270 by SIM	l Preparatio	n Meth	nod: EPA 3546			
Acenaphthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	83-32-9	
Acenaphthylene	<0.011 mg/kg	0.025	0.011	1	02/19/14 09:27	02/19/14 16:32	208-96-8	
Anthracene	<0.013 mg/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:32	120-12-7	
Benzo(a)anthracene	<0.0085 mg/kg	0.025	0.0085	1 -	02/19/14 09:27	02/19/14 16:32	56-55-3	
Benzo(a)pyrene	<0.0088 mg/kg	0.025	0.0088	1	02/19/14 09:27	02/19/14 16:32	50-32-8	
Benzo(b)fluoranthene	<0.012 mg/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	205-99-2	
Benzo(g,h,i)perylene	<0.0094 mg/kg		0.0094	1	02/19/14 09:27	02/19/14 16:32	191-24-2	
Benzo(k)fluoranthene	<0.014 mg/kg		0.014	1	02/19/14 09:27	02/19/14 16:32		
Chrysene	<0.011 mg/kg		0.011	1	02/19/14 09:27	02/19/14 16:32	218-01-9	
Dibenz(a,h)anthracene	<0.0090 mg/kg		0.0090	1	02/19/14 09:27	02/19/14 16:32	53-70-3	
Fluoranthene	0.019J mg/kg	•	0.012	1	02/19/14 09:27	02/19/14 16:32		
Fluorene	<0.012 mg/kg		0.012	. 1	02/19/14 09:27	02/19/14 16:32	86-73-7	
Indeno(1,2,3-cd)pyrene	<0.0094 mg/kg		0.0094	1	02/19/14 09:27			
AEX.		•						



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B10-S1

Lab ID: 4092070009

Collected: 02/11/14 10:30

Received: 02/13/14 08:40

Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical	Method: EPA	A 8270 by SIM	Preparation	on Meth	nod: EPA 3546			
1-Methylnaphthalene	<0.012 n	ng/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	90-12-0	
2-Methylnaphthalene	< 0.012 n	ng/kg	0.025	0.012	- 1	02/19/14 09:27	02/19/14 16:32	91-57-6	
Naphthalene	0.015J n	ng/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	91-20-3	
Phenanthrene	<0.012 n	ng/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	85-01-8	
Pyrene Surrogates	0.016J n	ng/kg	0.025	0.012	1	02/19/14 09:27	02/19/14 16:32	129-00-0	
2-Fluorobiphenyl (S)	. 61 %	6	40-130		1	02/19/14:09:27	02/19/14 16:32	321-60-8	
Terphenyl-d14 (S)	65 %	6	40-130		1	02/19/14 09:27	02/19/14 16:32	1718-51-0	
Percent Moisture	Analytical	Method: AS	TM D2974-87						
Percent Moisture	32.3 %	6	0.10	0.10	. 1		02/13/14 14:25		
Total Organic Carbon	Analytical	Method: EPA	4 9060 Modifie	ď				_	
Surrogates		•						_	
RPD%	24.3 %	6	0.10	0.10	1	4	02/20/14 13:28		
Total Organic Carbon	15100 n	ng/kg	2080	259	1		02/20/14 13:25	7440-44-0	
Total Organic Carbon	11800 n	ng/kg	2270	283	1		02/20/14 13:28	7440-44-0	
Mean Total Organic Carbon	13400 n	ng/kg	2180	271	1		02/20/14 13:28	7440-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B10-S2

Lab ID: 4092070010

Collected: 02/11/14 10:45 Received: 02/13/14 08:40

Results reported on a "dry-weight" basis

V.									
Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8082 GCS PCB	Analytical M	lethod: EPA 80	082 Prepa	ration Meth	od: EP/	A 3541			
PCB-1016 (Aroclor 1016)	<0.038 mg	/kg	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	12674-11-2	
PCB-1221 (Aroclor 1221)	<0.038 mg	-	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	11104-28-2	
PCB-1232 (Arocior 1232)	<0.038 mg	_	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	11141-16-5	
PCB-1242 (Aroclor 1242)	<0.038 mg	_	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	53469-21-9	
PCB-1248 (Aroclor 1248)	<0.038 mg	_	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	12672-29-6	
PCB-1254 (Aroclor 1254)	<0.038 mg	•	0.075	0.038	1		02/17/14 18:45		
PCB-1260 (Aroclor 1260)	<0.038 mg	_	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45		
PCB, Total	<0.038 mg	-	0.075	0.038	1	02/14/14 10:52	02/17/14 18:45	1336-36-3	
Surrogates									
Tetrachloro-m-xylene (S)	78 %		40-130		1	02/14/14 10:52	02/17/14 18:45	877-09-8	*
Decachlorobiphenyl (S)	90 %		48-130		1	02/14/14 10:52	02/17/14 18:45	2051-24-3	
6010 MET ICP	Analytical M	lethod: EPA 60	010 Prepa	ration Meth	od: EP/	A 3050			
Arsenic	7.7 mg	/ka	2.6	0.70	1	02/14/14 08:57	02/14/14 18:44	7440-38-2	
Barium	95.9 mg	-	0.64	0.11	1	02/14/14 08:57	02/14/14 18:44	7440-39-3	
Cadmium	0.47J mg	-	0.64	0.065	1	02/14/14 08:57	02/14/14 18:44		
Chromium	18.4 mg	_	0.64	0.16	1	02/14/14 08:57	02/14/14 18:44	7440-47-3	
Iron	14500 mg.		12.9	3.5	1	02/14/14 08:57	02/14/14 18:44	7439-89-6	
Lead	8.4 mg	_	1.3	0.38	1	02/14/14 08:57	02/14/14 18:44	7439-92-1	
Manganese	281 mg.	•	0.64	0.040	1	02/14/14 08:57	02/14/14 18:44	7439-96-5	
Selenium	< 0.76 mg.	•	2.6	0.76	1	02/14/14 08:57	02/14/14 18:44		
Silver	< 0.27 mg.	-	1.3	0.27	1	02/14/14 08:57	02/14/14 18:44		
6010 MET ICP, TCLP	Analytical M	ethod: EPA 60)10 Prepai	ration Metho	od: EP#	A 3010			-
	Leachate M	ethod/Date: E	PA 1311; 0:	2/20/14 00:	00		,		
Lead	<0.015 mg	/L	0.038	0.015	1	02/21/14 08:30	02/24/14 12:31	7439-92-1	
7471 Mercury	Analytical M	ethod: EPA 74	I71 Prepai	ration Metho	od: EP/	\ 7471			
Mercury	0.015 mg.	/kg	0.0094	0.0047	1	02/18/14 14:50	02/19/14 16:33	7439-97-6	2q
8270 MSSV PAH by SIM	Analytical M	ethod: EPA 82	270 by SIM	Preparation	n Meth	od: EPA 3546	e e		
Acenaphthene	<0.013 mg/	/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:49	83-32-9	
Acenaphthylene	< 0.011 mg/	/kg	0.025	0.011	1	02/19/14 09:27	02/19/14 16:49	208-96-8	
Anthracene	<0.013 mg/		0.025	0.013	1 .	02/19/14 09:27	02/19/14 16:49	120-12-7	
Велzo(a)anthracene	<0.0087 mg/		0.025	0.0087	1	02/19/14 09:27	02/19/14 16:49	56-55-3	
Benzo(a)pyrene	<0.0090 mg/	/kg	0.025	0.0090	1	02/19/14 09:27	02/19/14 16:49	50-32-8	
Benzo(b)fluoranthene	<0.013 mg/		0.025	0,013	1	02/19/14 09:27	02/19/14 16:49	205-99-2	
Benzo(g,h,i)perylene	<0.0095 mg/	-	0.025	0.0095	1.	02/19/14 09:27	02/19/14 16:49		
Benzo(k)fluoranthene	< 0.014 mg/	-	0.025	0.014	1	02/19/14 09:27	02/19/14 16:49	207-08-9	
	_	-	0.025	0.012	1	02/19/14 09:27	02/19/14 16:49		
	<0.012 mg/								
Chrysene	<0.012 mg/ <0.0092 mg/		0.025	0.0092	1.	02/19/14 09:27	02/19/14 16:49	53-70-3	
Chrysene Dibenz(a,h)anthracene	<0.0092 mg/	/kg	0.025 0.025	0.0092 0.013	1 [.] 1	02/19/14 09:27 02/19/14 09:27			
Chrysene Dibenz(a,h)anthracene Fluoranthene Fluorene		/kg /kg	0.025 0.025 0.025	0.0092 0.013 0.013			02/19/14 16:49 02/19/14 16:49 02/19/14 16:49	206-44-0	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Sample: B10-S2

Lab ID: 4092070010

Collected: 02/11/14 10:45

Received: 02/13/14 08:40 Matrix: Solid

Parameters	Results	Units	LOQ	LOD	DF	Prepared	Analyzed	CAS No.	Qual
8270 MSSV PAH by SIM	Analytical I	Method: EPA	8270 by SIM	Preparatio	n Metl	nod: EPA 3546			
1-Methylnaphthalene	<0.013 mg	g/kg	0.025	0.013	1 .	02/19/14 09:27	02/19/14 16:49	90-12-0	
2-Methylnaphthalene	<0.013 mg	g/kg	0.025	0.013	1.	02/19/14 09:27	02/19/14 16:49	91-57-6	
Naphthalene	<0.013 mg	g/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:49	91-20-3	
Phenanthrene	<0.013 mg	g/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:49	85-01-8	
Pyrene Surrogates	<0.013 mg	g/kg	0.025	0.013	1	02/19/14 09:27	02/19/14 16:49	129-00-0	
2-Fluorobiphenyl (S)	50 %		40-130		1	02/19/14 09:27	02/19/14 16:49	321-60-8	
Terphenyl-d14 (S)	50 %		40-130		1	02/19/14 09:27	02/19/14 16:49	1718-51-0	-
Percent Moisture	Analytical N	Method: AST	M D2974-87						
Percent Moisture	33.5 %		0.10	0.10	, 1		02/13/14 14:25		
Total Organic Carbon	Analytical N	Method: EPA	9060 Modifie	d		•			
Surrogates				~					
RPD%	5.9 %		0.10	0.10	1		02/20/14 13:36		
Total Organic Carbon	6770 mg	g/kg	3030	377	1		02/20/14 13:31	7440-44-0	
Total Organic Carbon	6380 mg	g/kg	3120	389	1		02/20/14 13:36	7440-44-0	
Mean Total Organic Carbon	6580 mg	g/kg	3080	383	1		02/20/14 13:36	7440-44-0	
			*						



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

MERP/4109

Analysis Method:

EPA 7471

QC Batch Method:

EPA 7471

Analysis Description:

7471 Mercury

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

METHOD BLANK: 932376

Matrix: Solid

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

Blank

Reporting

Parameter

Units

Units

4091982001

Result

0.016

Result

Limit Analyzed Qualifiers

Mercury

mg/kg

< 0.0033

0.0067 02/19/14 15:36

LABORATORY CONTROL SAMPLE:

Parameter

Parameter

932377

Spike

LCS Result

LCS % Rec % Rec Limits

Qualifiers

Mercury

mg/kg

Cónc. .17

0.17

932379

103

85-115

MATRIX SPIKE & MATRIX SPIKE DUPLICATE:

932378

MSD

Spike

MS

MSD

MS % Rec MSD

% Rec Max

Qual

Units

Conc.

Spike

Conc. Result Result

% Rec

Limits

RPD RPD

20

Mercury

mg/kg

.19

MS

.2 0.21

0.22

103

85-115 105

3



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

MPRP/9841

Analysis Method:

EPA 6010

QC Batch Method:

EPA 3050

Analysis Description:

6010 MET

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

METHOD BLANK: 931331 Associated Lab Samples:

Matrix: Solid

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

	•	Blank	Reporting		
Parameter	Units	Result	Limit	Analyzed	Qualifiers
Arsenic	mg/kg	<0.54	2.0	02/14/14 17:47	
Barium	mg/kg	<0.087	0.50	02/14/14 17:47	
Cadmium	mg/kg	< 0.051	0.50	02/14/14 17:47	
Chromium	mg/kg	<0.13	0.50	02/14/14 17:47	
Iron	mg/kg	<2.7	10.0	02/14/14 17:47	
Lead	mg/kg	<0.29	1.0	02/14/14 17:47	
Manganese	mg/kg	0.033J	0.50	02/14/14 17:47	
Selenium	mg/kg	< 0.59	2.0	02/14/14 17:47	
Silver	mg/kg	<0.21	1.0	02/14/14 17:47	

LABORATORY CONTROL SAM	IPLE: 931332					
		Spike	LCS	LCS	% Rec	
Parameter	Units	Conc.	Result	% Rec	Limits	Qualifiers
Arsenic	mg/kg		49.2	98	80-120	
3arium	mg/kg	50	49.9	100	80-120	
Cadmium	mg/kg	50	50.3	101	80-120	
Chromium	mg/kg	50	50.2	100	80-120	
ron .	mg/kg	500	479	96	80-120	
.ead	mg/kg	50	50.9	102	80-120	
/langanese	mg/kg	50	48.2	96	80-120	
Selenium	mg/kg	50	49.9	100	80-120	
Silver	mg/kg	25	25.1	100	80-120	

	41	092026001	MS Spike	MSD Spike	MS	MSD	MS	MSD	% Rec		Max
Parameter ·	Units	Result	Conc.	Conc.	Result	Result	% Rec	% Rec	Limits	RPD.	RPD Qua
Arsenic	mg/kg	12.4	55.3	55.5	70.0	65.4	104	95	75-125	7	20
Barium	mg/kg	139	55.3	55.5	203	244	114	189	75-125	19	20 M0
Cadmium	mg/kg	0.48J	55.3	55.5	56.2	55.4	101	99	75-125	1.	20
Chromium	mg/kg	37.5	55.3	55.5	77.1	84.4	72	84	75-125	9	20 M0
Iron	mg/kg	17900	553	555	23500	19300	1010	252	75-125	20	20 P6
Lead	mg/kg	38.8	55.3	55.5	86.0	85.5	86	. 84	75-125	1	20
Manganese	mg/kg	399	55.3	55.5	402	470	7	128	75-125	15	20 P6
Selenium	mg/kg	<0.66	55.3	55.5	54.0	52.3	98	94	75-125	3	20
Silver	mg/kg	< 0.24	27.7	27.8	28.3	28.0	102	100	75-125	1	20



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

MPRP/9859

Analysis Method:

EPA 6010

QC Batch Method:

EPA 3010

Analysis Description:

6010 MET TCLP

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007

METHOD BLANK: 933198

Matrix: Water

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007

Blank

Reporting

Parameter

Parameter

Units

Units

Result

Limit

Analyzed

Qualifiers

Lead

mg/L

<0.0030

0.0075

02/24/14 11:14

METHOD BLANK: 931972

Associated Lab Samples:

Matrix: Solid

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007

Blank Result

Reporting Limit

Analyzed

Qualifiers

Lead

mg/L

< 0.015

02/24/14 11:21 0.038

METHOD BLANK: 932739

Matrix: Solid

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007

Blank

Reporting

Qualifiers

Parameter

Units

Units

Units

Result

Limit

Analyzed

Lead

mg/L

< 0.015

0.038 02/24/14 11:17

METHOD BLANK: 932740

Associated Lab Samples:

Matrix: Solid

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007

Blank Result Reporting

Lead

Parameter

Limit

Analyzed

102

Qualifiers

mg/L

0.017J

0.038 02/24/14 11:19

LABORATORY CONTROL SAMPLE:

Parameter

Parameter

933199

Spike

LCS

LCS

% Rec

Qualifiers

Lead

Lead

mg/L

Conc. .5 Result 0.51 % Rec

Limits 80-120

MATRIX SPIKE SAMPLE:

933200

4092048001 Result

Spike

MS

Result

2.5

Units mg/L

< 0.015

Conc 2.5

% Rec

99

MS

% Rec Limits 75-125

Qualifiers

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full, without the written consent of Pace Analytical Services, Inc..





Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

MATRIX SPIKE SAMPLE:	933201	•		,			
Parameter	Units	4092225001 Result	Spike Conc.	MS Result	MS % Rec	% Rec: Limits	Qualifiers
i arameter	Onits .			1 (GSUIL	70 NGC	LITTIES -	Qualificis
Lead	mg/L	0.025J	2.5	2.5	99 ·	75-125	
						•	
MATRIX SPIKE SAMPLE:	933203						
		4092143001	Spike	MS	MS	% Rec	
Parameter	Units	Result	Conc.	Result	% Rec	Limits	Qualifiers
Lead	mg/L	<0.015	2.5	2.6	103	75-125	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

MPRP/9862

Analysis Method:

EPA 6010

QC Batch Method:

EPA 3010

Analysis Description:

6010 MET TCLP

Associated Lab Samples:

4092070008, 4092070009, 4092070010

METHOD BLANK: 933612

Matrix: Water

Associated Lab Samples:

Parameter

Parameter

4092070008, 4092070009, 4092070010

Units

Blank Result Reporting Limit

Analyzed

Qualifiers

Lead

mg/L

<0.0030

0.0075

02/24/14 12:09

METHOD BLANK: 933175

Associated Lab Samples:

Matrix: Solid

4092070008, 4092070009, 4092070010

Blank

Reporting Limit

Analyzed

Lead

mg/L

Result <0.015

0.038

02/24/14 12:11

Qualifiers

METHOD BLANK: 933176

Matrix: Solid

Associated Lab Samples:

4092070008, 4092070009, 4092070010

Units

Units

Blank

Reporting Limit

Analyzed

Qualifiers

Lead

Result

0.038

02/24/14 12:14

LABORATORY CONTROL SAMPLE:

Parameter

933613

mg/L

Units

< 0.015

LCS

LCS

% Rec

Qualifiers

Parameter

Result

% Rec

Limits

Lead

mg/L

Units

4092070008

Result

< 0.015

.5

0.51

103

80-120

933614

MS Spike

Conc.

Spike

Conc.

0.021J

MS

Result

2.5

MATRIX SPIKE & MATRIX SPIKE DUPLICATE:

Parameter

2.5

Spike

Conc.

MSD

933615

2.5

MSD Result

MS % Rec

MSD % Rec % Rec

Max

Lead

Lead

933616

Units

100

Limits 75-125 100

RPD RPD 0 20

mg/L

Spike

2.5

MS

MS

% Rec

Qual

MATRIX SPIKE SAMPLE:

Parameter

mg/L

4092267002 Result

Conc. 2.5 Result 2.6 % Rec 101 Limits 75-125 Qualifiers



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

OEXT/21331

Analysis Method:

EPA 8082

QC Batch Method:

EPA 3541

Analysis Description:

8082 GCS PCB

Associated Lab Samples:

4092070009, 4092070010

METHOD BLANK: 931395

Matrix: Solid

Associated Lab Samples:

 $4092070001,\,4092070002,\,4092070003,\,4092070004,\,4092070005,\,4092070006,\,4092070007,\,4092070008,$

4092070009, 4092070010

Parameter	Units	Blank Result	Reporting Limit	Analyzed	Qualifiers
PCB-1016 (Aroclor 1016)	 mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1221 (Aroclor 1221)	mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1232 (Aroclor 1232)	mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1242 (Aroclor 1242)	mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1248 (Aroclor 1248)	mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1254 (Aroclor 1254)	mg/kg	<0.025	0.050	02/17/14 14:25	
PCB-1260 (Aroclor 1260)	mg/kg	<0.025	0.050	02/17/14 14:25	
Decachlorobiphenyl (S)	%	96	48-130	02/17/14 14:25	
Tetrachloro-m-xylene (S)	%	76	40-130	02/17/14 14:25	

LABORATORY CONTROL SAMPLE:	931396					
		Spike	LCS	LCS	% Rec	•
Parameter	Units	Conc.	Result	% Rec	Limits	Qualifiers
PCB-1016 (Aroclor 1016)	mg/kg	-	<0.025			
PCB-1221 (Aroclor 1221)	mg/kg		<0.025			
PCB-1232 (Aroclor 1232)	mg/kg	-	<0.025			
PCB-1242 (Aroclor 1242)	mg/kg		<0.025			
PCB-1248 (Aroclor 1248)	mg/kg		< 0.025			
PCB-1254 (Aroclor 1254)	mg/kg		< 0.025			
PCB-1260 (Aroclor 1260)	mg/kg	.5	0.38	76	70-130	
Decachlorobiphenyl (S)	%			99	48-130	
Tetrachloro-m-xylene (S)	%			77	40-130	*

			MS	MSD				•	5"			
	40	092070002	Spike	Spike	MS	MSD	MS	MSD	% Rec		Max	
Parameter	Units	Result	Conc.	Conc.	Result	Result	% Rec	% Rec	Limits	RPD	RPD	Qual
PCB-1016 (Aroclor 1016)	mg/kg	<0.031			<0.031	<0.031					31	
PCB-1221 (Aroclor 1221)	mg/kg	< 0.031			< 0.031	<0.031					31	
PCB-1232 (Aroclor 1232)	mg/kg	<0.031			< 0.031	<0.031					31	
PCB-1242 (Aroclor 1242)	mg/kg	< 0.031			< 0.031	<0.031					31	
PCB-1248 (Aroclor 1248)	mg/kg	< 0.031			< 0.031	< 0.031					31	
PCB-1254 (Aroclor 1254)	mg/kg	< 0.031			<0.031	<0.031					31	
PCB-1260 (Aroclor 1260)	mg/kg	< 0.031	.62	.62	0.40	0.39	65	63	40-149	2	31	
Decachlorobiphenyl (S)	%						83	82	48-130			
etrachloro-m-xylene (S)	%						71	68	40-130			



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

OEXT/21381

Analysis Method:

EPA 8270 by SIM

QC Batch Method:

EPA 3546

Analysis Description:

8270/3546 MSSV PAH by SIM

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

METHOD BLANK: 932671

Matrix: Solid

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

Parameter	Units	Blank Result	Reporting Limit	Analyzed	Qualifiers
1-Methylnaphthalene	mg/kg	<0.0083	0.017	02/19/14 10:46	
2-Methylnaphthalene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Acenaphthene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Acenaphthylene	mg/kg	<0.0075	0.017	02/19/14 10:46	
Anthracene	mg/kg	<0.0086	0.017	02/19/14 10:46	
Benzo(a)anthracene	mg/kg	<0.0058	0.017	02/19/14 10:46	
Benzo(a)pyrene	mg/kg	<0.0060	0.017	02/19/14 10:46	
Benzo(b)fluoranthene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Benzo(g,h,i)perylene	mg/kg	<0.0063	0.017	02/19/14 10:46	
Benzo(k)fluoranthene	mg/kg	<0.0092	0.017	02/19/14 10:46	
Chrysene	mg/kg	<0.0077	0.017	02/19/14 10:46	
Dibenz(a,h)anthracene	mg/kg	<0.0061	0.017	02/19/14 10:46	
Fluoranthene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Fluorene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Indeno(1,2,3-cd)pyrene	mg/kg	<0.0063	0.017	02/19/14 10:46	
Naphthalene	mg/kg	<0:0083	0.017	02/19/14 10:46	
Phenanthrene	mg/kg	<0.0083	0.017	02/19/14 10:46	
Pyrene	mg/kg	<0.0083	0.017	02/19/14 10:46	
2-Fluorobiphenyl (S)	%	65	40-130	02/19/14 10:46	
Terphenyl-d14 (S)	%	74	40-130	02/19/14 10:46	

LABORATORY CONTROL SAM	IPLE: 932672	Spike	LCS	LCS	% Rec	
Parameter	Units	Conc.	Result	% Rec	Limits	Qualifiers
1-Methylnaphthalene	mg/kg		0.23	70	47-130	
2-Methylnaphthalene	mg/kg	.33	0.23	-69	48-130	
Acenaphthene	mg/kg	.33	0.22	65	55-130	•
Acenaphthylene	mg/kg	.33	0.21	64	55-130	
Anthracene	mg/kg	.33	0.24	71	66-130	
Benzo(a)anthracene	mg/kg	.33	0.23	69	55-130	
Benzo(a)pyrene	mg/kg	.33	0.24	71	56-130	
Benzo(b)fluoranthene	mg/kg	.33	0.26	77	53-130	
Benzo(g,h,i)perylene	mg/kg	.33	0.21	63	51-130	
Benzo(k)fluoranthene	mg/kg	.33	0.23	70	52-130	
Chrysene	mg/kg	.33	0.24	72	58-130	
Dibenz(a,h)anthracene	mg/kg	.33	0.18	55	55-130	
luoranthene	mg/kg	.33	0.24	72	62-130	
luorene	mg/kg	.33	0.22	67	58-130	
ndeno(1,2,3-cd)pyrene	mg/kg	.33	0.20	60	54-130	
Naphthalene	mg/kg	.33	0.22	65	41-130 ⁻	



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

LABORATORY CONTROL SAMPL	E: 932672	Spike	LCS	LCS	% Rec		
Parameter	Units	Conc.	Result	% Rec	Limits	Qualifiers	
Phenanthrene	mg/kg	.33	0.24	71	60-130		-
Pyrene	mg/kg	.33	0.25	74	51-130		•
2-Fluorobiphenyl (S)	%			58	40-130		
Terphenyl-d14 (S)	%			65	40-130		

MATRIX SPIKE & MATRIX S	SPIKE DUPLICAT	E: 93267	3 MS	MSD	932674							
Parameter	40 Units	092152003 Result	Spike Conc.	Spike Conc.	MS Result	MSD Result	MS % Rec	MSD % Rec	% Rec Limits	RPD	Max RPD	Qual
1-Methylnaphthalene	mg/kg	<9.6	.38	.38	0.27	0.29	71	75	42-130	6	32	
2-Methylnaphthalene	mg/kg	ug/kg <9.6 ug/kg	.38	.38	0.27	0.27	70	72	34-130	2	35	
Acenaphthene	mg/kg	<9.6 ug/kg	.38	.38	0.26	0.26	67	69	31-130	2	35	
Acenaphthylene	mg/kg	<8.6 ug/kg	.38	.38	0.26	0.26	68	69	32-130	1	25	
Anthracene	mg/kg	<9.9 ug/kg	.38	.38	0.28	0.28	72	74	39-131	2	38	
Benzo(a)anthracene	mg/kg	<6.6 ug/kg	.38	.38	0.26	0.27	69	70	29-130	2	30	
Benzo(a)pyrene	mg/kg	<6.8 ug/kg	.38	.38	0.28	0.28	73	74	35-130	1	33	
Benzo(b)fluoranthene	mg/kg	<9.6 ug/kg	.38	.38	0.28	0.29	72	77	21-142	6	44	
Benzo(g,h,i)perylene	mg/kg	<7.3 ug/kg	.38	.38	0.28	0.29	74	75	12-134	2	33	
Benzo(k)fluoranthene	mg/kg	<10.6 ug/kg	.38	.38	0.28	0.28	74	72	35-130	3	37	
Chrysene	mg/kg	<8.8 ug/kg	.38	.38	0.27	0.27	70	71	37-130	2	38	
Dibenz(a,h)anthracene	mg/kg	<7.0 ug/kg	.38	.38	0.27	0.27	71	71	23-130	1	27	
Fluoranthene	mg/kg	<9.6 ug/kg	.38	.38	0.28	0.28	73	74	29-137	2	50	
Fluorene	mg/kg	<9.6 ug/kg	.38	.38	0.26	0.27	68	70	32-130	2	32	
Indeno(1,2,3-cd)pyrene	mg/kg	<7.3 ug/kg	.38	.38	0.28	0.28	72	73	17-134	1	28	
Naphthalene	mg/kg	<9.6 ug/kg	.38	.38	0.26	0.27	68	70	24-130	_ 2	. 40	
Phenanthrene .	mg/kg	<9.6 ug/kg	.38	.38	0.28	0.28	72	73	27-135	2	46	
Pyrene	mg/kg	<9.6 ug/kg	.38	.38	0.28	0.29	74	75	24-130	1	49	
2-Fluorobiphenyl (S) Terphenyl-d14 (S)	% %	5 5					60 64	60 65	40-130 40-130			





Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

PMST/9432

Analysis Method:

ASTM D2974-87

QC Batch Method: ASTM D2974-87

Analysis Description:

Dry Weight/Percent Moisture

Associated Lab Samples:

 $4092070001,\,4092070002,\,4092070003,\,4092070004,\,4092070005,\,4092070006,\,4092070007,\,4092070008,$

4092070009, 4092070010

%

SAMPLE DUPLICATE: 931238

4092059001 Result

Dup Result

Max RPD **RPD**

10

Parameter

Percent Moisture

Units

7.6

7.5

Qualifiers

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full, without the written consent of Pace Analytical Services, Inc..



Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

QC Batch:

WETA/21935

Analysis Method:

EPA 9060 Modified

QC Batch Method:

EPA 9060 Modified

Analysis Description:

9060 TOC Average

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

METHOD BLANK:

Matrix: Solid

Associated Lab Samples:

4092070001, 4092070002, 4092070003, 4092070004, 4092070005, 4092070006, 4092070007, 4092070008,

4092070009, 4092070010

Blank

Reporting

Parameter

Units

Units

4092070001

Result

54400

Result

Limit

Analyzed

Qualifiers

Mean Total Organic Carbon

mg/kg

<31.1

250 02/20/14 09:27

LABORATORY CONTROL SAMPLE:

Parameter

933090

Spike

LCS Result

LCS % Rec % Rec

Mean Total Organic Carbon

Parameter

Mean Total Organic Carbon

mg/kg

Conc. 1000

Spike

Conc.

MS

45000

1040

104

Limits Qualifiers

MATRIX SPIKE & MATRIX SPIKE DUPLICATE:

933091

MS MSD 933092

MS

Result

101000

MSD

Result

95400

MS % Rec

MSD

% Rec

80-120

% Rec Limits

50-150

Max

6

RPD RPD. Qual 30

MATRIX SPIKE & MATRIX SPIKE DUPLICATE:

933093

Spike

Conc.

45000

933094

MSD

Spike

754

MSD Result

MS % Rec

104

MSD % Rec

Max

Parameter Mean Total Organic Carbon Units

mg/kg

Units

mg/kg

4092070002 Result 1030

Spike

Conc. Conc. 745

Result 1660

MS

1750

% Rec 84

Limits 50-150 95

RPD RPD

Quai 5 30

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full, without the written consent of Pace Analytical Services, Inc.





QUALIFIERS

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

DEFINITIONS

DF - Dilution Factor, if reported, represents the factor applied to the reported data due to changes in sample preparation, dilution of the sample aliquot, or moisture content.

ND - Not Detected at or above adjusted reporting limit.

J - Estimated concentration above the adjusted method detection limit and below the adjusted reporting limit.

MDL - Adjusted Method Detection Limit.

PRL - Pace Reporting Limit.

RL - Reporting Limit.

S - Surrogate

1,2-Diphenylhydrazine (8270 listed analyte) decomposes to Azobenzene.

Consistent with EPA guidelines, unrounded data are displayed and have been used to calculate % recovery and RPD values.

LCS(D) - Laboratory Control Sample (Duplicate)

MS(D) - Matrix Spike (Duplicate)

DUP - Sample Duplicate

RPD - Relative Percent Difference

NC - Not Calculable.

SG - Silica Gel - Clean-Up

U - Indicates the compound was analyzed for, but not detected.

N-Nitrosodiphenylamine decomposes and cannot be separated from Diphenylamine using Method 8270. The result reported for each analyte is a combined concentration.

Pace Analytical is TNI accredited. Contact your Pace PM for the current list of accredited analytes.

TNI - The NELAC Institute.

LABORATORIES

PASI-G

Pace Analytical Services - Green Bay

BATCH QUALIFIERS

Batch: WETA/21935

[WB] Results reported on dry weight basis per cited method.

Batch: WETA/21936

[WB] Results reported on dry weight basis per cited method.

ANALYTE QUALIFIERS

1q Analyte was detected in the associated leach blank at a concentration of 0.017 mg/L.

2q Negative detection value obtained for Method Blank (-0.0034 mg/kg).

M0 Matrix spike recovery and/or matrix spike duplicate recovery was outside laboratory control limits.

P6 Matrix spike recovery was outside laboratory control limits due to a parent sample concentration notably higher than the

spike level.



QUALITY CONTROL DATA CROSS REFERENCE TABLE

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Lab ID	Sample ID	QC Batch Method	QC Batch	Analytical Method	Analytical Batch	
4092070001	B6-S1	EPA 3541	OEXT/21331	EPA 8082	GCSV/1088	
4092070002	B6-S2	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
1092070003	B7-S1	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
1092070004	B7-S2	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
1092070005	B8-S1	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
1092070006	B8-S2	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
092070007	B9-S1	EPA 3541	OEXT/21331	EPA 8082	GCSV/1088	
092070008	B9-S2	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
092070009	B10-S1	EPA 3541	OEXT/21331	EPA 8082	GCSV/1088	
092070010	B10-S2	EPA 3541	OEXT/21331	EPA 8082	GCSV/10888	
092070001	B6-S1	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070002	B6-S2	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070003	B7-S1	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070004	B7-S2	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070005	B8-S1	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070006	B8-S2	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070007	B9-S1	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070008	B9-S2	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070009	B10-S1	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070010	B10-S2	EPA 3050	MPRP/9841	EPA 6010	ICP/8655	
092070001	B6-S1	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070002	B6-S2	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070003	B7-S1	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070004	B7-S2	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070005	B8-S1	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070006	B8-S2	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070007	B9-S1	EPA 3010	MPRP/9859	EPA 6010	ICP/8673	
092070008	B9-S2	EPA 3010	MPRP/9862	EPA 6010	ICP/8675	
092070009	B10-S1	EPA 3010	MPRP/9862	EPA 6010	ICP/8675	
092070010	B10-S2	EPA 3010	MPRP/9862	EPA 6010	ICP/8675	
092070001	B6-S1	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070002	B6-S2	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070003	B7-\$1	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070004	B7-S2	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070005	B8-S1	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070006	B8-S2	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070007	B9-S1	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070008	B9-S2	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070009	B10-S1	EPA 7471	MERP/4109	EPA 7471	MERC/5332	
092070010	B10-S2	EPA 747.1	MERP/4109	EPA 7471	MERC/5332	
092070001	B6-S1	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	
092070002	B6-S2	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	
092070003	B7-S1	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	
092070004	B7-S2	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	
092070005	B8-S1	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	
092070006	B8-S2	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV/6496	



QUALITY CONTROL DATA CROSS REFERENCE TABLE

Project:

C7799-WING III WINGRA

Pace Project No.:

4092070

Lab ID	Sample ID	QC Batch Method	QC Batch	Analytical Method	Analy Batch	
4092070007	B9-S1	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV	/6496
4092070008	B9-S2	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV	
4092070009	B10-S1	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV	
4092070010	B10-S2	EPA 3546	OEXT/21381	EPA 8270 by SIM	MSSV	/6496
4092070001	B6-S1	ASTM D2974-87	PMST/9432			
1092070002	B6-S2	ASTM D2974-87	PMST/9432			
1092070003	B7-S1	ASTM D2974-87	PMST/9432			
1092070004	B7-S2	ASTM D2974-87	PMST/9432			
4092070005	B8-S1	ASTM D2974-87	PMST/9432			
4092070006	B8-S2	ASTM D2974-87	PMST/9432			
1092070007	B9-S1 B9-S2	ASTM D2974-87 ASTM D2974-87	PMST/9432 PMST/9432			
4092070008 4092070009	B10-S1	ASTM D2974-87 ASTM D2974-87	PMST/9432			
4092070003 4092070010	B10-S2	ASTM D2974-87	PMST/9432			
4092070001	B6-S1	EPA 9060 Modified	WETA/21935			
1092070001	B6-S1	EPA 9060 Modified	WETA/21936	•		
092070002	B6-S2	EPA 9060 Modified	WETA/21935			
1092070002	B6-S2	EPA 9060 Modified	WETA/21936			
1092070003	B7-S1	EPA 9060 Modified	WETA/21935			
1092070003	B7-S1	EPA 9060 Modified	WETA/21936			
1092070004	B7-S2	EPA 9060 Modified	WETA/21935		*	
092070004	B7-S2	EPA 9060 Modified	WETA/21936			
1092070005	B8-S1	EPA 9060 Modified	WETA/21935	*		
1092070005	B8-S1	EPA 9060 Modified	WETA/21936			
1092070006	B8-S2	EPA 9060 Modified	WETA/21935			
1092070006	B8-S2	EPA 9060 Modified	WETA/21936			
1092070007	B9-S1	EPA 9060 Modified	WETA/21935			•
1092070007	B9-S1	EPA 9060 Modified	WETA/21936			
1092070008	B9-S2	EPA 9060 Modified	WETA/21935			
1092070008	B9-S2	EPA 9060 Modified	WETA/21936			
1092070009	B10-S1	EPA 9060 Modified	WETA/21935			
1092070009	B10-S1	EPA 9060 Modified	WETA/21936			
1092070010	B10-S2	EPA 9060 Modified	WETA/21935			
092070010	B10-S2	EPA 9060 Modified	WETA/21936			

Sample Condition Upon Receipt

Pace Analytical Services, Inc 1241 Bellevue Street, Suite Green Bay, WI 5430

Client Name:	e Other	\mathcal{U}	al	aco_	4000070	
racking #: 500131-1 sustody Seal on Cooler/Box Present: X yes	Ti no	Seals	intact	K yes ∏ no	4052070	
ustody Seal on Samples Present:	no	Seals	intact:	∏ yes ≣ no		
acking Material: Bubble Wrap Bub		ıs İ	Non	Other _		
hermometer Used N/A	Туре	of Ice		Blue Dry None		ice, cooling process has begun
ooler Temperature Uncorr: ROI /Corr.		<u>'</u>	Biolo	gical Tissue is Fro	F	
emp Blank Present: Tyes Tyno					□ no	Person examining content
emp should be above freezing to 6°C for all sample exc	ept Biota	ì.		Comments:		Initials:
ozen Biota Samples should be received ≤ 0°C.	War.	□ bin	□N/A			:
nain of Custody Present:	TY Yes			1		
nain of Custody Filled Out:	Ves N		□N/A			
nain of Custody Relinquished:	Yes		□N/A	<u> </u>		
impler Name & Signature on COC:	Ø¥¥es	□No	□N/A	4.		
imples Arrived within Hold Time:	Yes	□No	□n/A	5.		
- VOA Samples frozen upon receipt	□Yes	□No		Date/Time:		.`.
ort Hold Time Analysis (<72hr):	□Yes	ДМо	□n/a	6.		
sh Turn Around Time Requested:	□Yes	Ü₩o	□n/A	7.		
fficient Volume:	Yes	□No	□n/A	8.		
			□N/A	9		
rrect Containers Used:	V ØYes		□n/A			
-Pace Containers Used:	,					
-Pace IR Containers Used:	□Yes		□ TANA	40		
ntainers Intact:	Yes		□N/A			
tered volume received for Dissolved tests	□Yes	6	PN VA	005	O Match	mle_
mple Labels match COC:	□Yes	/No	□N/A	12.	0 ///20	,
-Includes date/time/ID/Analysis Matrix:	\sum_{i}					
containers needing preservation have been checked. on-Compliance noted in 13.)	∐Yes	□No	NIA	13. F. HNO:	B [H2SO4]	NaOH NaOH +ZnA
containers needing preservation are found to be in						
npliance with EPA recommendation. NO3, H2SO4 ≤2; NaOH+ZnAct ≥9, NaOH ≥12)	∐Yes	□Ио	AVN			
eptions: VOA, coliform, TOC, TOX, TOH,				Initial when	Lab Std #ID of preservative	Date/ Time:
3, WIDROW, Phenolics, OTHER:	□Yes			completed	preservante	
adspace in VOA Vials (>6mm):	□Yes		N/A	-		
p Blank Present	□Yes		Ø N/A	15.		
p Blank Custody Seals Present	.□Yes.	□No	MINIA.			•. • *
ce Trip Blank Lot # (if purchased):		 -		1.6	chacked see attach	ned form for additional comment
ent Notification/ Resolution:			Date/		CHECKED, SEE AUGU	· · · · · · · · · · · · · · · · · · ·
Person Contacted:Comments/ Resolution:						
Actification (Accordance)						

SECTION E: BIDDERS ACKNOWLEDGEMENT

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

Bidder must state a Unit Price and Total Bid for each item. The Total Bid for each item must be the product of quantity, by Unit Price. The Grand Total must be the sum of the Total Bids for the various items. In case of multiplication errors or addition errors, the Grand Total with corrected multiplication and/or addition shall determine the Grand Total bid for each contract. The Unit Price and Total Bid must be entered numerically in the spaces provided. All words and numbers shall be written in ink.

1.	The undersigned having familiarized himself/herself with the Contract documents, including Advertisement for Bids, Instructions to Bidders, Form of Proposal, City of Madison Standard
	Specifications for Public Works Construction - 2014 Edition thereto. Form of Agreement Form of
	Bond, and Addenda Issued and attached to the plans and specifications on file in the office of the
	City Engineer, nereby proposes to provide and furnish all the labor materials tools and
	expendable equipment necessary to perform and complete in a workmanlike manner the
	specified construction on this project for the City of Madison, all in accordance with the plant and
	specifications as prepared by the City Engineer, including Addenda to the Contract Nos
	through Issued thereto, at the prices for said work as contained in this proposal
	(Electronic bids submittals shall acknowledge addendum under Section F and shall not
<u> </u>	acknowledge nere)
2., .	If awarded the Contract, we will initiate action within seven (7) days after notification or in
	accordance with the date specified in the contract to begin work and will proceed with diligence to
	bring the project to full completion within the number of work days allowed in the Contract or by
	the calendar date stated in the Contract.
3.	The undersigned Bidder or Contractor certifies that he/she is not a party to any contract,
	combination in form of trust or otherwise, or conspiracy in restraint of trade or commerce or any
	other violation of the anti-trust laws of the State of Wisconsin or of the United States, with respect
at:	to this bid or contract or otherwise.
4.	I hereby certify that I have met the Bid Bond Requirements as specified in Section 102.5.
	(IF BID BOND IS USED, IT SHALL BE SUBMITTED ON THE FORMS PROVIDED BY THE
ë	CITY. FAILURE TO DO SO MAY RESULT IN REJECTION OF THE BID).
5.	hereby certify that all statements herein are made on behalf of
	Speedway Sand & Gravel Inc. (name of corporation, partnership, or person submitting bid)
	a corporation organized and existing under the laws of the State of Wisconsin
	a partnership consisting of; an individual trading as
	from the plans and specifications and have checked the same in detail before submitting this
	Proposal; that I have fully authority to make such statements and submit this Proposal in (its, their) behalf; and that the said statements are true and correct.
	and that the said statements are true and correct.
SIGNAT	TURF
	Vice President
TITLE, I	F ANY
Sworn	and subscribed to before me this
7th	
	Janian Vilon a E Partir E
13.16.2	WINCE THE STATE OF
(Notar	y Public or other officer authorized to administer oaths)
iviy Co	mmission Expires 10-22-17
blader	s shall not add any conditions or qualifying statements to this Proposal.
	(日本語画学の文本の文学教育等) ・ 「日本語の文学教育等)

Contract 6832 - Speedway Sand & Gravel, Inc.

Section F: Disclosure of Ownership and BVC

This section is a required document for the bid to be considered complete. There are two methods for completing the Disclosure of Ownership and BVC form. Method one: The form can be filled out online and submitted to this site to be included with your electronic bid. Method two: The form can be downloaded from the site and submitted by hand to the City of Madison.

Method of Submittal for Disclosure of Ownership and BVC (click in box below to choose) *

I will submit Bid Express fillable online form (Disclosure of Ownership and BVC).

Notice required under Section 15.04(1)(m), Wisconsin Statutes. The statutory authority for the use of this form is prescribed in Sections 66.0903(12)(d), Wisconsin Statutes. The use of this form is mandatory. The penalty for failing to complete this form is prescribed in Section 103.005(12). Personal information you provide may be used for secondary purposes.

- (1) On the date a contractor submits a bid to or completes negotiations with a state agency or local governmental unit, on a project subject to Section 66.0903 or 103.49, Wisconsin Statutes, the contractor shall disclose to such state agency or local governmental unit the name of any "other construction business", which the contractor, or a shareholder, officer or partner of the contractor, owns or has owned within the preceding three (3) years.
- (2) The term "other construction business" means any business engaged in the erection, construction, remodeling, repairing, demolition, altering or painting and decorating of buildings, structures or facilities. It also means any business engaged in supplying mineral aggregate, or hauling excavated material or spoil as provided by Sections 66.0903(3), 103.49(2) amd 103.50(2), Wisconsin Statues.
- (3) This form must ONLY be filed, with the state agency or local governmental unit that will be awarding the contract, if both (A) and (B) are met.
- (A) The contractor, or a shareholder, officer or partner of the contractor:
- 1. Owns at least a 25% interest in the "other construction business", indicated below,on the date the contractor submits a bid or completes negotiations.
- 2. Or has owned at least a 25% interest in the "other construction business" at any time within the preceding three (3) years.
- (B) The Wisconsin Department of Workforce Development (DWD) has determined that the "other construction business" has failed to pay the prevailing wage rate or time and one-half the required hourly basic rate of pay, for hours worked in excess of the prevailing hours of labor, to any employee at any time within the preceding three (3) years.

Other Construction Business

Not Applicable

Name of Business

Street Address or PO Box City, State and Zip Code

Best Value Contracting

- 1. The Contractor shall indicate the non-apprenticeable trades used on this contract.
- 2. Madison General Ordinance (M.G.O.), 33.07(7), does provide for some exemptions from the active apprentice requirement. Apprenticeable trades are those trades considered apprenticeable by the State of Wisconsin. Please check applicable box if you are seeking an exemption.
- Contractor has a total skilled workforce of four or less individuals in all apprenticeable trades combined.

 No available trade training program; The Contractor has been rejected by the only available trade training program, or there is no trade training program within 90 miles.

 Contractor is not using an apprentice due to having a journey worker on layoff status, provided the journey worker was employed by the contractor in the past six months.

 First time contractor on City of Madison Public Works contract requests a onetime exemption but intends to comply on all future contracts and is taking steps typical of a "good faith" effort.

 Contractor has been in business less than one year.

 Contractor doesn't have enough journeyman trade workers to qualify for a trade training program in that respective trade.
- 3. The Contractor shall indicate on the following section which apprenticeable trades are to be used on this contract. Compliance with active apprenticeship, to the extent required by M.G.O. 33.07(7), shall be satisfied by documentation from an applicable trade training body; an apprenticeship contract with the Wisconsin Department of Workforce Development or a similar agency in another state; or the U.S Department of Labor. This documentation is required prior to the Contractor beginning work on the project site.

	The Contractor has reviewed the list and shall not use any apprenticeable trades on this
-	project.
	LIST APPRENTICABLE TRADES (check all that apply to your work to be performed on this contract)
	PRICKI AVER
	BRICKLAYER CARPENTER
	CEMENT MASON / CONCRETE FINISHER
	CEMENT MASON / CONCRETE FINISHER CEMENT MASON (HEAVY HIGHWAY)
	CONSTRUCTION CRAFT LABORER
	DATA COMMUNICATION INSTALLER
	ELECTRICIAN
	ENVIRONMENTAL SYSTEMS TECHNICIAN / HVAC SERVICE TECH/HVAC
	INSTALL / SERVICE
	GLAZIER
	HEAVY EQUIPMENT OPERATOR / OPERATING ENGINEER
	INSULATION WORKER (HEAT and FROST)
	IRON WORKER
	IRON WORKER (ASSEMBLER, METAL BLDGS)
	PAINTER and DECORATOR
	PLASTERER
	PLUMBER
	RESIDENTIAL ELECTRICIAN
	ROOFER and WATER PROOFER
• -	SHEET METAL WORKER
	SPRINKLER FITTER
	T STEAMFITTER
	STEAMFITTER (REFRIGERATION)
	STEAMFITTER (SERVICE)
	TAPER and FINISHER
	TELECOMMUNICATIONS (VOICE, DATA and VIDEO) INSTALLER-TECHNICIAN
	TILE SETTER



WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

Small Business Enterprise Compliance Report

This information may be submitted electronically through Bid Express or submitted with bid in sealed envelope.

Cover Sheet

Prime Bidder Information	
Company: Speedway Sand & Gravel Inc.	
Address: 8500 Greenway Blvd Suite 202, Mi	ddleton, WI 53562
Telephone Number 608-836-1071	Fax Number: 608-836-7485
Contact Person/Title: John Czerepinski, Vice Presid	dent
Prime Bidder Certification	
John Czerepinski	Vice President of
Name	Title
Speedway Sand & Gravel, Inc.	certify that the information
Сотрапу	
contained in this SBE Compliance Report is true and correct	to the best of my knowledge and belief.
tonice lisa	
Witness' Signature B	idder Signature
November 7, 2014	,
Date	

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

Small Business Enterprise Compliance Report

Summary Sheet

SBE Subcontractors Who Are NOT Suppliers

Name(s) of SBEs Utilized	Type of Work	14 % of Total Bid Amount
		%
Here Brumm Mucking	Hauling.	3,40 %
		%
Burse Surveying	Stakina	0.65 %
		%
		%
		%
		%
		%
		%
		%
		%
		%
Subtotal SBE who are NOT suppliers:		4.05 %
SBE Subcontractors Who Are Suppliers		
Name(s) of SBEs Utilized	Type of Work	% of Total Bid Amount
· · · · · · · · · · · · · · · · · · ·		%
	11.7 · · · · · · · · · · · · · · · · · · ·	%
		<u>%</u>
		%
		%
<u> </u>		%
Subtotal Contractors who are suppliers:	% x 0.6 =	% (discounted to 60%)
Total Percentage of SBE Utilization:	4.05 %.	

NAME: WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

BID OPEN DATE: 11/7/14

Speedway Sand & Gravel, inc.

	item#	Quantity	Price	Extension
CUNDISTRIBUTED) - L.F. \$5.00 \$5.00 \$5.00 \$5.00 \$5.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$143,000.00 \$1,000.00 \$1,000.00 \$1,000.00 \$1,000.00 \$1,000.00 \$1,000.00 \$3,675.00 \$20,000.00 \$1,755.00 \$3,675.00 \$20,000.00 \$1,755.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,675.00 \$20,000.00 \$3,670.00 \$3,670.00 \$3,670.00 \$3,670.00 \$3,600.00 \$3,	10701.0 - TRAFFIC CONTROL - LUMP SUM	1.00	\$5,000.00	\$5,000.00
10911.0 - MOBILIZATION - LUMP SUM		50.00	\$5.00	\$250.00
20101.0 - EXCAVATION CUT - C.Y. 1700.00 \$48.00 \$81,600.00 20140.0 - GEOTEXTILE FABRIC TYPE SAS NON WOVEN - 6 OZ - S.Y. 11110.00 \$3.11 \$34,552.10 20217.0 - CILEAR STONE - TON 245.00 \$1.50 \$3.575.00 20221.0 - TONSOIL - S.Y. 20400.00 \$1.75 \$35,700.00 20210.1 - TONSOIL - S.Y. 20400.00 \$1.75 \$35,700.00 20210.1 - TONSOIL - S.Y. 20400.00 \$1.70 \$3.075.00 20210.1 - TONSOIL - S.Y. 20400.00 \$1.70 \$35,700.00 20314.0 - REMOVE PIEP - L.F. 39.00 \$20.00 \$700.00 20326.0 - REMOVE PIEP - L.F. 39.00 \$20.00 \$700.00 20326.0 - REMOVE PIEP - L.F. 40.00 \$40.00 \$1.600.00 20401.0 - CILEARING - I.D. 1500.00 \$7.00 \$1.000.00 20401.0 - CILEARING - I.D. 1500.00 \$7.00 \$1.000.00 20401.0 - CILEARING - I.D. 1500.00 \$7.00 \$1.000.00 20401.0 - CILEARING - I.D. 1600.00 \$7.00 \$1.000.00 20401.0 - CILEARING - I.D. 1600.00 \$7.00 \$1.000.00 20401.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$4.400.00 \$4.40			,	
20217.0 - CLEAR STONE - TON 245.00 \$16.500 \$36,875.00 20221.0 - TOPSOIL - \$Y.				\$81,600.00
20221.0 - TOPSOIL - S Y 20400.00 \$1.75 \$35,700.00 20311.0 - REMOVE SEWER ACCESS STRUCTURE - EACH 1.00 \$700.00 \$700.00 20311.0 - REMOVE PIPE - L.F. 39.00 \$20.00 \$700.00 20326.0 - REMOVE FENCE - L.F. 68.00 \$1.00 \$88.00 20336.0 - PIDE PLUG - EACH 4.00 \$40.00 \$1,600.00 20401.0 - CLEARING - I.D. 1500.00 \$7.00 \$1,600.00 20401.0 - CLEARING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - SRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$6.00 \$7.00 \$1,200.00 \$1				
20311.0 - REMOVE SEWER ACCESS STRUCTURE - EACH				
20314.0 - REMOVE PIPE - L.F. 39.00 \$20.00 \$780.00 20326.0 - REMOVE FENCE - L.F. 68.00 \$1.00 \$400.00 \$1,600.00 20326.0 - PIPE PLUG - EACH 4.00 \$400.00 \$1,600.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$1,600.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$1,600.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$1,000.00 20403.0 - TALL GRASS PRAIRIE SEEDING - S.Y. 16309.00 \$0.88 \$14,351.92 21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$1,200.00 \$1,200.00 21010.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00			*	·
20326.0 - REMOVE FENCE - L.F. 68.00 \$1.00 \$88.00 20336.0 - PIPE PLUG - EACH 4.00 \$400.00 \$1,600.00 20401.0 - CLEARING - L.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20405.0 - BRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$4,400.00 20706.0 - TALL GRASS PRAIRIE SEEDING - S.Y. 16309.00 \$350.00 \$7,000.00 21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$1,200.00 \$7,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 20.00 \$350.00 \$7,000.00 21011.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2,000.00 21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$4.74 \$5,688.00 21019.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F. 1200.00 \$4.74 \$5,688.00 21012.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F. 1200.00 \$4.74 \$5,688.00 21018.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F. 1200.00 \$2.00 \$2,00 2102.0 - SILT FENCE				
20336.0 - PIPE PLIG - EACH 4.00 \$400.00 \$1,600.00 20401.0 - CLEARING - I.D. 1500.00 \$7.00 \$10,500.00 20402.0 - GRUBBING - I.D. 1500.00 \$7.00 \$10,500.00 20405.0 - BRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$4,400.00 20706.0 - TALL GRASS PRAIRIE SEEDING - S.Y. 18309.00 \$1,200.00 \$1,200.00 21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$1,200.00 \$1,200.00 21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$250.00 \$7,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 4.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00 \$2,000.00 21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$4.74 \$5,688.00 21019.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,400.00 21023.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$1.85 \$2,220.00 21032.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - EACH 30.00 \$6.50 \$564.00				
20401.0 - CLEARING - I.D. 1500.00 \$7.00 \$10,500.00 20403.0 - GRUBBING - I.D. 1500.00 \$10,500.00 20405.0 - BRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$6,000 \$10,500.00 20002.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$1,200.00 \$1,200.00 21002.0 - EROSION CONTROL INSPECTION - EACH 20.00 \$350.00 \$7,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 4.00 \$250.00 \$7,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 4.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00 \$2,000.00 21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,000.00 21022.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,000.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,000.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21023.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21023.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21023.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 21023.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$2,200.00 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$0.10 \$1.00 \$1.00 \$0.10 \$1.00 \$1.00 \$1.00 \$0.10 \$1.00 \$1.00 \$1.00 \$1.00 \$1.00 \$1.00 \$1.00				•
20405.0 - GRUBBING - I.D. 1500.00 \$7.00 \$4,400.00 \$20405.0 - BRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$4,400.00 \$1,200.0				
20405.0 - BRUSH CLEARING - LUMP SUM 1.00 \$4,400.00 \$0.80 \$14,301.02 20706.0 - TALL GRASS PRAIRIE SEEDING - S.Y. 16309.00 \$0.88 \$14,351.92 21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM 1.00 \$1,200.00 \$350.00 \$7,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 4.00 \$350.00 \$7,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00 \$2,000.00 21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$4.74 \$5,688.00 21019.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,400.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$0.45 \$540.00 21022.0 - SILT FENCE - REMOVE & RESTORE - L.F. 1200.00 \$0.45 \$540.00 21052.0 - POLYMER STABILIZATION - S.Y. 1000.00 \$0.22 \$2,200.00 21052.0 - POLYMER STABILIZATION - TYPE D HYBRID - PROVIDE & INSTALL 6.00 \$95.00 \$570.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 8.00 \$50.00 \$5750.00 21057.0 - INLET PROTECTION, TYPE D			•	
20706.0 - TALL GRASS PRAIRIE SEEDING - S.Y. 16309.00 \$0.88 \$14,351.92				
21001.0 - EROSION CONTROL PLAN & IMPLEMENTATION - LUMP SUM				•
21002.0 - EROSION CONTROL INSPECTION - EACH 20.00 \$350.00 \$1,000.00 21011.0 - CONSTRUCTION ENTRANCE - EACH 4.00 \$250.00 \$1,000.00 21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00 21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$4.74 \$5,688.00 21019.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$2.00 \$2,400.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$1.85 \$2,220.00 21023.0 - SILT FENCE - REMOVE & RESTORE - L.F. 1200.00 \$0.45 \$540.00 21052.0 - POLYMER STABILIZATION - S.Y. 1000.00 \$0.22 \$2,200.00 21056.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL - EACH 6.00 \$95.00 \$570.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 6.00 \$95.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21073.0 - SEROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 922.00 \$4.18 \$38,59.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$46.00 \$45.00 \$9,632.00 50433.0 - 18 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 7.00 \$0.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 7.00 \$0.00 \$1,000.00 50499.0 - CONORTETE COLLAR - EACH 7.00 \$0.00 \$1,000.00 50499.0 - CONORTETE COLLAR - EACH 7.00 \$0.00 \$1,000.00 50003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$47,000.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$47,000.00 \$47,000.00 50006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 2122.00 \$1.00 \$1,000.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$1,000.00 9003.0 - STORM/STREAM CO	20706.0 - TALL GRASS PRAIRIE SEEDING - S.Y.	16309.00	\$0.88	\$14,351.92
21011.0 - CONSTRUCTION ENTRANCE - EACH 2.00 \$250.00 \$1,000.00 \$21013.0 - STREET SWEEPING - LUMP SUM 1.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000.00 \$2,000 \$2,000.00 \$2,000 \$2,000.00 \$2,000 \$2,000 \$2,000.00 \$2,000 \$2,000 \$2,000.00 \$2,000 \$2,000.00 \$2,000 \$2,000.00 \$2,000 \$2,000.00 \$2,000 \$2,000.00 \$				
21013.0 - STREET SWEEPING - LUMP SUM				
21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$4.74 \$5,688.00 21019.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F. 1200.00 \$2.00 \$2,400.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$1.85 \$2,220.00 21023.0 - SILT FENCE - REMOVE & RESTORE - L.F. 1200.00 \$0.45 \$540.00 21052.0 - POLYMER STABILIZATION - S.Y. 10000.00 \$0.22 \$2,200.00 21056.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL - EACH 6.00 \$95.00 \$570.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 30.00 \$25.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21051.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 18000.00 \$1.68 \$30,240.00 21051.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$33,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31,70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50451.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$9,632.00 50451.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$3,500.00 50463.0 - 18 INCH RCP AE - EACH 4.00 \$1,000.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,650.00 \$0000.00 50000.00 - TEMPORARY FENCING - L.F. 1500.00 \$4,000.00 \$3,500.00 50000.00 - TEMPORARY FENCING - L.F. 68.00 \$1.00 \$6,000.00 \$0000.00 - TEMPORARY FENCING - L.F. 68.00 \$1.00 \$6,000.00 \$0000.00 - TEMPORARY FENCING - L.F. 68.00 \$1.00 \$6,000.00 \$0000.00 - TEMPORARY FENCING - L.F. 68.00 \$1.00 \$6,000.00 \$0000.00 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 400.00 \$46.60 \$10,000.00 \$10,000.00				
21019.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F. 1200.00 \$2.00 \$2.400.00 21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F. 1200.00 \$1.855 \$2.220.00 21023.0 - SILT FENCE - REMOVE & RESTORE - L.F. 1200.00 \$0.45 \$540.00 21052.0 - POLYMER STABILIZATION - S.Y. 10000.00 \$0.22 \$2.200.00 21056.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL - EACH 30.00 \$25.00 \$750.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 30.00 \$25.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 18000.00 \$1.68 \$30,240.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,640.00 50463.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.0	21013.0 - STREET SWEEPING - LUMP SUM	1.00	\$2,000.00	\$2,000.00
21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F.	21018.0 - SILT SOCK (8 INCH) - PROVIDE, INSTALL, & MAINTAIN - L.F.	1200.00	\$4.74	\$5,688.00
21023.0 - SILT FENCE - REMOVE & RESTORE - L.F. 1200.00 \$0.45 \$540.00 21052.0 - POLYMER STABILIZATION - S.Y. 10000.00 \$0.22 \$2,200.00 21056.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL - EACH 6.00 \$95.00 \$570.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 30.00 \$25.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 18000.00 \$1.68 \$30,240.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 7.00 \$500.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 \$0001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4,000.00 \$6,000.00 \$0001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4,000.00 \$6,000.00 \$0001.0 - TEMPORARY FENCING - L.F. 160.00 \$47,000.00 \$40.00 \$68.00 \$1,000.00 \$40.00 \$68.00 \$1.00 \$68.00	21019.0 - SILT SOCK (8 INCH) - REMOVE & RESTORE - L.F.	1200.00	\$2.00	\$2,400.00
21052.0 - POLYMER STABILIZATION - S.Y. 10000.00 \$0.22 \$2,200.00 21055.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL - EACH 6.00 \$95.00 \$570.00 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 30.00 \$25.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 18000.00 \$1.68 \$30,240.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 220.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$3,390.00 50463.0 - 18 INCH RCP AE - EACH 4.00 \$1,100.00 \$3,390.00 50463.0 - 18 INCH RCP AE - EACH 7.00 \$500.00 \$3,390.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4,000.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 \$7,500.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$47,000.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - WETLAND EMERGENT - S.Y. 400.00 \$46.50 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000.00 \$10,000	21022.0 - SILT FENCE - PROVIDE, INSTALL, & MAINTAIN - L.F.	1200.00	\$1.85	\$2,220.00
21056.0 - INLET PROTECTION, TYPE D HYBRID - PROVIDE & INSTALL-EACH	21023.0 - SILT FENCE - REMOVE & RESTORE - L.F.	1200.00	\$0.45	\$540.00
EACH 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 21073.0 - SEEDING - WETLAND EMERGENT - S.Y. 21073.0 - SEEDING - WETLAND EMERGENT - S.Y. 21073.0 - SEEDING - FLOOD PLAIN - S.Y. 21073.0 - SEEDING - FLOOD PLAIN - S.Y. 21073.0 - SEEDING - FLOOD PLAIN - S.Y. 21073.0 - SEEDING - SEEDING - LUMP SUM 21074.0 - SEEDING - SEEDING - LUMP SUM 21074.0 - SEEDING -	21052.0 - POLYMER STABILIZATION - S.Y.	10000.00	\$0.22	\$2,200.00
21057.0 - INLET PROTECTION, TYPE D HYBRID - MAINTAIN - EACH 30.00 \$25.00 \$750.00 21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVE - EACH 6.00 \$20.00 \$120.00 21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 18000.00 \$1.68 \$30,240.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER PIPE - L.F. 9220.00 \$41.00 \$1.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,390.00 50601.0 - 12 INCH RCP AE GATE - EACH 7.00 \$500.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00				
21058.0 - INLET PROTECTION, TYPE D HYBRID - REMOVÉ - EACH 21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 18000.00 \$1.68 \$30,240.00 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 2200.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,390.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 1500.00 \$4.00 \$6,000.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$7,500.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.00 \$46.50 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00	· ·			
21061.0 - EROSION MATTING, CLASS I, URBAN TYPE A - S.Y. 21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$38,539.60 \$50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 \$31.70 \$0411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 \$043.0 \$9,632.00 \$44.60.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$4,000.00 \$1,000.00 \$4,000.00 \$3,390.00 \$0463.0 - 18 INCH RCP AE - EACH \$0.00 \$1,100.00 \$3,390.00 \$0499.0 - CONCRETE COLLAR - EACH \$0.00 \$1,000.00 \$3,500.00 \$0601.0 - 12 INCH RCP AE GATE - EACH \$0.00 \$450.00 \$1,800.00 \$1,800.00 \$0603.0 - 18 INCH RCP AE GATE - EACH \$0.00 \$450.00 \$1,800.00 \$1,650.00 \$1,650.00 \$1,000.			•	•
21073.0 - EROSION MATTING, CLASS II, TYPE C - ORGANIC - S.Y. 9220.00 \$4.18 \$38,539.60 50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH.RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH.RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 9006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$10,000.00 \$46.50 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$46.50 \$18,600.00 9003.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00				
50211.0 - SELECT BACKFILL FOR STORM SEWER - T.F. 317.00 \$0.10 \$31.70 50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42				
50411.0 - 12 INCH RCP STORM SEWER PIPE - L.F. 224.00 \$43.00 \$9,632.00 50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 9004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$68.00 9005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 400.00 \$46.50 \$18,600.00 900				
50413.0 - 18 INCH RCP STORM SEWER PIPE - L.F. 93.00 \$48.00 \$4,464.00 50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$47,000.00 \$47,000.00 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00				
50461.0 - 12 INCH RCP AE - EACH 4.00 \$1,000.00 \$4,000.00 50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 9005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 9008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	·			
50463.0 - 18 INCH RCP AE - EACH 3.00 \$1,130.00 \$3,390.00 50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00			'	
50499.0 - CONCRETE COLLAR - EACH 7.00 \$500.00 \$3,500.00 50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00				
50601.0 - 12 INCH RCP AE GATE - EACH 4.00 \$450.00 \$1,800.00 50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00			100	•
50603.0 - 18 INCH RCP AE GATE - EACH 3.00 \$550.00 \$1,650.00 90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00				
90001.0 - TEMPORARY FENCING - L.F. 1500.00 \$4.00 \$6,000.00 90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00			·	
90002.0 - CONSTRUCTION SURVEYING - LUMP SUM 1.00 \$7,500.00 \$7,500.00 90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00				
90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F. 101.00 \$13.55 \$1,368.55 \$90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00	· · · · · · · · · · · · · · · · · · ·			
90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM 1.00 \$47,000.00 \$47,000.00 90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00	90002.0 - CONSTRUCTION SURVEYING - LUMP SUM	1.00	\$7,500.00	\$7,500.00
90005.0 - CHAIN LINK FENCE - L.F. 68.00 \$1.00 \$68.00 90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	90003.0 - REMOVE AND REPLACE STEEL PLATE BEAM GUARD - L.F.	101.00	\$13.55	\$1,368.55
90006.0 - SEEDING - WETLAND EMERGENT - S.Y. 2122.00 \$1.11 \$2,355.42 90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	90004.0 - QUANN SOCCER FIELD TOPSOIL AND SEEDING - LUMP SUM	1.00	\$47,000.00	\$47,000.00
90007.0 - SEEDING - FLOOD PLAIN - S.Y. 1969.00 \$1.02 \$2,008.38 90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	90005.0 - CHAIN LINK FENCE - L.F.	68.00		· ·
90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y. 400.00 \$46.50 \$18,600.00 90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	90006.0 - SEEDING - WETLAND EMERGENT - S.Y.	2122.00	\$1.11	\$2,355.42
90030.0 - STORM/STREAM CONTROL - LUMP SUM 1.00 \$10,000.00 \$10,000.00	90007.0 - SEEDING - FLOOD PLAIN - S.Y.	1969:00	\$1.02	\$2,008.38
	90008.0 - ASPHALT PATH REPAIR (PARK) - S.Y.	400.00	\$46.50	
90031.0 - SILT CURTAIN - L.F. 400.00 \$33.30 \$13,320.00	90030.0 - STORM/STREAM CONTROL - LUMP SUM	1.00	\$10,000.00	\$10,000.00
	90031.0 - SILT CURTAIN - L.F.	400.00	\$33.30	\$13,320.00

NAME: WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

BID OPEN DATE: 11/7/14

Speedway Sand & Gravel, Inc.

ltem	Quantity	Price	Extension
90032.0 - LIGHT RIPRAP - GLÁCIAL FIELD STONE - TON	4270.00	\$20.00	\$85,400.00
90033:0 - DREDGING - C.Y.	5500.00	\$33.00	\$181,500.00
90034.0 - DEWATERING (DREDGED MATERIAL) - LUMP SUM	1.00	\$25,000.00	\$25,000.00
90035.0 - STEPPED STONE REVETMENT (STATION 1+25) - L.F.	10.00	\$1,010.00	\$10,100.00
90036.0 - STEPPED STONE REVETMENT			•
(STATION 6+50) - L.F.	25.00	\$1,360.00	\$34,000.00
90037.0 - LITTORAL SHELF CONSTRUCTION - S.F.	36820.00	\$1.50	\$55,230.00
90038.0 - WOODY DEBRIS FISH HABITAT - EACH	4.00	\$1,500.00	\$6,000.00
90039.0 - GEOWEB CREEK ACCESS - S.F.	650.00	\$12.32	\$8,008.00
40201.0 - HMA PAVEMENT TYPE E-0.3 - TON	436.00	\$87.00	\$37,932.00
40311.0 - PULVERIZE AND SHAPE - S.Y.	2425.00	\$3.75	\$9,093.75
40321.0 - UNDERCUT			
(UNDISTRIBUTED) - C.Y.	50.00	\$15.00	\$750.00
TOTALS			\$1,030,846.42



Department of Public Works City Engineering Division

608 266 4751

Robert F. Phillips, P.E. City Engineer

City-County Building, Room 115 210 Martin Luther King, Jr. Boulevard Madison, Wisconsin 53703 508 264 9275 FAX 1 866 704 2315 Yextnet Principal Engineers Michael R. Dalley, P.E. Christina M. Bachmann, P.E. John S. Fahmey, P.E. Gregory T. Fries, P.E.

Facilities & Sustainability Jeanne E. Hoffman, Manager James C. Whitney, A.LA.

> Operations Manager Kathleen M. Cryan GIS Manager David A. Davis, R.L.S.

Financial Officer Steven B. Denner-Rivers Hydrogeologist Bryon Bemis

BIEWNAL BID EOND

Speedway Sand & Gravel, Inc.

(a corporation of the State of Wisconsin

(individual), (partnership), (hereinafter referred to as the "Principal") and Fidelity and Deposit Company of Maryland

a corporation of the State of Maryland (hereinafter referred to as the "Surety") and licensed to do business in the State of Wisconsin, are held and firmly bound unto the City of Madison, Wisconsin (hereinafter referred to as the "City"), in the sum equal to the individual proposal guaranty amounts of the total bid or bids of the Principal herein accepted by the City, for the payment of which the Principal and the Surety hereby jointly and severally bind ourselves, our heirs, executors, administrators, successors and assigns.

The condition of this obligation is that the Principal has submitted to the City certain bids for projects from the time period of February 1, 2014 through January 31, 2016

If the Principal is awarded the contract(s) by the City and, within the time and manner required by law after the prescribed forms are presented for its signature, the Principal enters into (a) written contract(s) in accordance with the bid(s), and files with the City its bond(s) guaranteeing faithful performance and payment for all labor and materials, as required by law, or if the City rejects all bids for the work described, then this obligation shall be null and void; otherwise, it shall remain in full force and effect

In the event the Principal shall fail to execute and deliver the contract(s) or the performance and payment bond(s), all within the time specified or any extension thereof, the Principal and Surety agree jointly and severally to pay to the City within ten (10) calendar days of written demand a total equal to the sum of the individual proposal guaranty amounts of the total bid(s) as liquidated damages.

The Surety, for value received, hereby agrees that the obligations of it and its bond shall be in no way impaired or affected by any extension of time within which the City may accept a bid, and the Surety does hereby waive notice of any such extension.

This bond may be terminated by the Surety upon giving thirty (30) days written notice to the City of its intent to terminate this bond and to be released and discharged therefrom, but such termination shall not operate to relieve or discharge the Surety from any liability already accrued or which shall accrue before the expiration of such thirty (30) day period.

IN WITNESS WHEREOF, the Principal and the Surety have bereunto set their hands and seals, and such of them as are corporations have caused their corporate seals to be hereto affixed and these presents to be signed by their proper officers, on the day and year set forth below.

PRINCIPAL	
Speedway Sand & Gravel, Inc.	11-20-2013
By: SIGNATURE AND TITLE John CZECEO	omski, VP.
SURETY	
Sh. M.	
By: EhMeen	DATE
This certifies that I have been duty licensed as an 2530156 for the year 20 fact with authority to execute this bid bond, which	
11-18-13	Elizabeth Mosca
DATE	AGENT
	6609 University Ave
	Middleton, WI 53562 CITY, STATE AND ZIP CODE
	608-644-8668 TELEPHONE NUMBER

Note to Surety and Principal: Any bid submitted which this bond guarantees may be rejected if the Power of Attorney form showing that the Agent of Surety is currently authorized to execute bonds on behalf of Surety is not attached to this bond.

CERTIFICATE OF BIENNIAL BID BOND

February 1, 2014 through January 31, 2016

NAME OF SURETY

Fidelity and Deposit Company of Maryland

NAME OF CONTRACTOR

Speedway Sand & Gravei, Inc.

CERTIFICATE HOLDER

City of Madison, Wisconsin

This is to certify that a biennial bid bond issued by the above-named Surety is currently on file with the City of Madison.

This certificate is issued as a matter of information and conveys no rights upon the certificate holder and does not amend, extend or alter the coverage of the biennial bid bond.

Cancellation: Should the above policy be cancelled before the expiration date, the issuing Surety will give thirty (30) days written notice to the certificate holder indicated above.

SIGNATURE OF AUTHORIZED CONTRACTOR REPRESENTATIVE

11-20-2013

DATE

ZURICH AMERICAN INSURANCE COMPANY COLONIAL AMERICAN CASUALTY AND SURETY COMPANY FIDELITY AND DEPOSIT COMPANY OF MARYLAND POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That the ZURICH AMERICAN INSURANCE COMPANY, a corporation of the State of New York, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, a corporation of the State of Maryland, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND a corporation of the State of Maryland (herein collectively called the "Companies"), by THOMAS O. MCCLELLAN, Vice President, in pursuance of authority granted by Article V, Section 8, of the By-Laws of said Companies, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, do hereby nominate, constitute, and appoint Ann MAY, Rana R. HUGHEY, Janice CLOOTEN, Michele A. HOLZ and Elizabeth MOSCA, all of Middleton, Wisconsin, EACH its true and lawful agent and Attorney-in-Fact, to make, execute, seal and deliver, for, and on its behalf as surety, and as its act and deed: any and all bonds and undertakings, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Companies, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the ZURICH AMERICAN INSURANCE COMPANY at its office in New York, New York, the regularly elected officers of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at its office in Owings Mills, Maryland, and the regularly elected officers of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at its office in Owings Mills, Maryland, in their own proper persons.

The said Vice President does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article V, Section 8, of the By-Laws of said Companies, and is now in force.

IN WITNESS WHEREOF, the said Vice-President has hereunto subscribed his/her names and affixed the Corporate Seals of the said ZURICH AMERICAN INSURANCE COMPANY, COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 14th day of May, A.D. 2013.

ATTEST:

ZURICH AMERICAN INSURANCE COMPANY COLONIAL AMERICAN CASUALTY AND SURETY COMPANY FIDELITY AND DEPOSIT COMPANY OF MARYLAND







Ву:

Assistant Secretary Eric D. Barnes Vice President Thomas O. McCleilan

State of Maryland

City of Baltimore

On this 14th day of May, A.D. 2013, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, THOMAS O. MCCLELLAN, Vice President, and ERIC D. BARNES, Assistant Secretary, of the Companies, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and acknowledged the execution of same, and being by me duly sworn, deposeth and saith, that he/she is the said officer of the Company aforesaid, and that the seals affixed to the preceding instrument are the Corporate Seals of said Companies, and that the said Corporate Seals and the signature as such officer were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporations.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.

Constance a. Durn

Constance A. Dunn, Notary Public My Commission Expires: July 14, 2015

EXTRACT FROM BY-LAWS OF THE COMPANIES

"Article V, Section 8, Attorneys-in-Fact. The Chief Executive Officer, the President, or any Executive Vice President or Vice President may, by written instrument under the attested corporate seal, appoint attorneys-in-fact with authority to execute bonds, policies, recognizances, stipulations, undertakings, or other like instruments on behalf of the Company, and may authorize any officer or any such attorney-in-fact to affix the corporate seal, thereto; and may with or without cause modify of revoke any such appointment or authority at any time."

CERTIFICATE

I, the undersigned, Vice President of the ZURICH AMERICAN INSURANCE COMPANY, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, do hereby certify that the foregoing Power of Attorney is still in full force and effect on the date of this certificate; and I do further certify that Article V, Section 8, of the By-Laws of the Companies is still in force.

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the TUTION AMERICAN INSTRANCE COMPANY of streeting duly called and held on the 15th day of December 1988.

RESOLVED: "That the signature of the President or a Vice President and the attesting signature of a Secretary or an Assistant Secretary and the Seal of the Company may be affixed by facsimile on any Power of Attorney...Any such Power or any certificate thereof bearing such facsimile signature and seal shall be valid and binding on the Company."

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at a meeting duly called and held on the 5th day of May, 1994, and the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the 5th day of May, 1994, and the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the L0th day of May, 1990, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND AT A MARYLAN

RESOLVED: "That the facsimile or mechanically reproduced seal of the company and facsimile or mechanically reproduced signature of any Vice-President, Secretary, or Assistant Secretary of the Company, whether made heretofore or hereafter, wherever appearing upon a certified copy of any power of attorney issued by the Company, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

IN TESTIMONY WHEREOF, I have hereunto subscribed my name and affixed the corporate seals of the said Companies, this /8 day of //8/. 20/3.







Geoffrey Delisio, Vice President

			•						
				,					
	*								
·									
				. •			ŧ		
				د					,
				* -			N		
				,					
		•							
5								·	
							\mathcal{F}_{i}		
		•							
					w	-			
			. · · · · · .						

SECTION H: AGREEMENT

THIS AGREEMENT made this 3d day of December in the year Two Thousand and Fourteen between SPEEDWAY SAND & GRAVEL, INC. hereinafter called the Contractor, and the City of Madison, Wisconsin, hereinafter called the City.

WHEREAS, the Common Council of the said City of Madison under the provisions of a resolution adopted <u>DECEMBER 2, 2014</u>, and by virtue of authority vested in the said Council, has awarded to the Contractor the work of performing certain construction.

NOW, THEREFORE, the Contractor and the City, for the consideration hereinafter named, agree as follows:

Scope of Work. The Contractor shall, perform the construction, execution and completion of the following listed complete work or improvement in full compliance with the Plans, Specifications, Standard Specifications, Supplemental Specifications, Special Provisions and contract; perform all items of work covered or stipulated in the proposal; perform all altered or extra work; and shall furnish, unless otherwise provided in the contract, all materials, implements, machinery, equipment, tools, supplies, transportation, and labor necessary to the prosecution and completion of the work or improvements:

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

- 2. Completion Date/Contract Time. Construction work must begin within seven (7) calendar days after the date appearing on mailed written notice to do so shall have been sent to the Contractor and shall be carried on at a rate so as to secure full completion <u>SEE SPECIAL PROVISIONS</u>, the rate of progress and the time of completion being essential conditions of this Agreement.
- Contract Price. The City shall pay to the Contractor at the times, in the manner and on the conditions set forth in said specifications, the sum of ONE MILLION THIRTY THOUSAND EIGHT HUNDRED FORTY-SIX AND 42/100 (\$1,030,846.42) Dollars being the amount bid by such Contractor and which was awarded to him/her as provided by law.
- 4. Wage Rates for Employees of Public Works Contractors

General and Authorization. The Contractor shall compensate its employees at the prevailing wage rate in accordance with section 66.0903, Wis. Stats., DWD 290 of the Wisconsin Administrative Code and as hereinafter provided unless otherwise noted in Section D: Special Provisions, Subsection 102.10 – Minimum Rate of Wage Scale.

"Public Works" shall include building or work involving the erection, construction, remodeling, repairing or demolition of buildings, parking lots, highways, streets, bridges, sidewalks, street lighting, traffic signals, sanitary sewers, water mains and appurtenances, storm sewers, and the grading and landscaping of public lands.

"Building or work" includes construction activity as distinguished from manufacturing, furnishing of materials, or servicing and maintenance work, except for the delivery of mineral aggregate such as sand, gravel, bituminous asphaltic concrete or stone which is incorporated into the work under contract with the City by depositing the material directly in final place from transporting vehicle.

"Erection, construction, remodeling, repairing" means all types of work done on a particular building or work at the site thereof in the construction or development of the project, including without limitation, erecting, construction, remodeling, repairing, altering, painting, and decorating, the transporting of materials and supplies to or from the building or work done by the employees of the Contractor, Subcontractor, or Agent thereof, and the manufacturing or furnishing of

H-1

materials, articles, supplies or equipment on the site of the building or work, by persons employed by the Contractor, Subcontractor, or Agent thereof.

"Employees working on the project" means laborers, workers, and mechanics employed directly upon the site of work.

"Laborers, Workers, and Mechanics" include pre-apprentices, helpers, trainees, learners and properly registered and indentured apprentices but exclude clerical, supervisory, and other personnel not performing manual labor.

Establishment of Wage Rates. The Department of Public Works shall periodically obtain a current schedule of prevailing wage rates from DWD. The schedule shall be used to establish the City of Madison Prevailing Wage Rate Schedule for Public Works Construction (prevailing wage rate). The Department of Public Works may include known increases to the prevailing wage rate which can be documented and are to occur on a future specific date. The prevailing wage rate shall be included in public works contracts subsequently negotiated or solicited by the City. Except for known increases contained within the schedule, the prevailing wage rate shall not change during the contract. The approved wage rate is attached hereto.

Workforce Profile. The Contractor shall, at the time of signature of the contract, notify the City Engineer in writing of the names and classifications of all the employees of the Contractor, Subcontractors, and Agents proposed for the work. In the alternative, the Contractor shall submit in writing the classifications of all the employees of the Contractor, Subcontractors and Agents and the total number of hours estimated in each classification for the work. This workforce profile(s) shall be reviewed by the City Engineer who may, within ten (10) days, object to the workforce profile(s) as not being reflective of that which would be required for the work. The Contractor may request that the workforce profile, or a portion of the workforce profile, be submitted after the signature of the contract but at least ten (10) days prior to the work commencing. Any costs or time loss resulting from modifications to the workforce profile as a result of the City Engineer's objections shall be the responsibility of the Contractor.

Payrolls and Records. The Contractor shall keep weekly payroll records setting forth the name, address, telephone number, classification, wage rate and fringe benefit package of all the employees who work on the contract, including the employees of the Contractor's subcontractors and agents. Such weekly payroll records must include the required information for all City contracts and all other contracts on which the employee worked during the week in which the employee worked on the contract. The Contractor shall also keep records of the individual time each employee worked on the project and for each day of the project. Such records shall also set forth the total number of hours of overtime credited to each such employee for each day and week and the amount of overtime pay received in that week. The records shall set forth the full weekly wages earned by each employee and the actual hourly wage paid to the employee.

The Contractor shall submit the weekly payroll records, including the records of the Contractor's subcontractors and agents, to the City Engineer for every week that work is being done on the contract. The submittal shall be within twenty-one (21) calendar days of the end of the Contractor's weekly pay period.

Employees shall receive the full amounts accrued at the time of the payment, computed at rates not less than those stated in the prevailing wage rate and each employee's rate shall be determined by the work that is done within the trade or occupation classification which should be properly assigned to the employee.

An employee's classification shall not be changed to a classification of a lesser rate during the contract. If, during the term of the contract, an employee works in a higher pay classification than the one which was previously properly assigned to the employee, then that employee shall be considered to be in the higher pay classification for the balance of the contract, receive the appropriate higher rate of pay, and she/he shall not receive a lesser rate during the balance of the

Rev. 07/11/2014-6832specs.doc

contract. For purposes of clarification, it is noted that there is a distinct difference between working in a different classification with higher pay and doing work within a classification that has varying rates of pay which are determined by the type of work that is done within the classification. For example, the classification "Operating Engineer" provides for different rates of pay for various classes of work and the Employer shall compensate an employee classified as an "Operating Engineer" based on the highest class of work that is done in one day. Therefore, an "Operating Engineer's" rate may vary on a day to day basis depending on the type of work that is done, but it will never be less than the base rate of an "Operating Engineer". Also, as a matter of clarification, it is recognized that an employee may work in a higher paying classification merely by chance and without prior intention, calculation or design. If such is the case and the performance of the work is truly incidental and the occurrence is infrequent, inconsequential and does not serve to undermine the single classification principle herein, then it may not be required that the employee be considered to be in the higher pay classification and receive the higher rate of pay for the duration of the contract. However, the Contractor is not precluded or prevented from paying the higher rate for the limited time that an employee performs work that is outside of the employee's proper classification.

Questions regarding an employee's classification, rate of pay or rate of pay within a classification, shall be resolved by reference to the established practice that predominates in the industry and on which the trade or occupation rate/classification is based. Rate of pay and classification disputes shall be resolved by relying upon practices established by collective bargaining agreements and guidelines used in such determination by appropriate recognized trade unions operating within the City of Madison.

The Contractor, its Subcontractors and Agents shall submit to interrogation regarding compliance with the provisions of this ordinance.

Mulcting of the employees by the Contractor, Subcontractor, and Agents on Public Works contracts, such as by kickbacks or other devices, is prohibited. The normal rate of wage of the employees of the Contractor, Subcontractor, and Agents shall not be reduced or otherwise diminished as a result of payment of the prevailing wage rate on a public works contract.

Hourly contributions. Hourly contributions shall be determined in accordance with the prevailing wage rate and with DWD. 290.01(10), Wis. Admin. Code.

Apprentices and Subjourney persons. Apprentices and sub journeypersons performing work on the project shall be compensated in accordance with the prevailing wage rate and with DWD 290.02, and 290.025, respectively, Wis. Admin. Code.

Straight Time Wages. The Contractor may pay straight time wages as determined by the prevailing wage rate and DWD 290.04, Wis. Admin. Code.

Overtime Wages. The Contractor shall pay overtime wages as required by the prevailing wage rate and DWD 290.05, Wis. Admin. Code.

Posting of Wage Rates and Hours. A clearly legible copy of the prevailing wage rate, together with the provisions of Sec. 66.0903(10)(a) and (11)(a), Wis. Stats., shall be kept posted in at least one conspicuous and easily accessible place at the project site by the Contractor and such notice shall remain posted during the full time any laborers, workers or mechanics are employed on the contract.

Evidence of Compliance by Contractor. Upon completion of the contract, the Contractor shall file with the Department of Public Works an affidavit stating:

a. That the Contractor has complied fully with the provisions and requirements of Sec. 66.0903(3), Wis. Stats., and Chapter DWD 290, Wis. Admin. Code; the Contractor has received evidence of compliance from each of the agents and subcontractors; and the

names and addresses of all of the subcontractors and agents who worked on the contract.

b. That full and accurate records have been kept, which clearly indicate the name and trade or occupation of every laborer, worker or mechanic employed by the Contractor in connection with work on the project. The records shall show the number of hours worked by each employee and the actual wages paid therefore; where these records will be kept and the name, address and telephone number of the person who will be responsible for keeping them. The records shall be retained and made available for a period of at least three (3) years following the completion of the project of public works and shall not be removed without prior notification to the municipality.

Evidence of Compliance by Agent and Subcontractor. Each agent and subcontractor shall file with the Contractor, upon completion of their portion of the work on the contract an affidavit stating that all the provisions of Sec. 66.0903(3), Wis. Stats., have been fully complied with and that full and accurate records have been kept, which clearly indicate the name and trade or occupation of every laborer, worker or mechanic employed by the Contractor in connection with work on the project. The records shall show the number of hours worked by each employee and the actual wages paid therefore; where these records shall be kept and the name, address and telephone number of the person who shall be responsible for keeping them. The records shall be retained and made available for a period of at least three (3) years following the completion of the project of public works and shall not be removed without prior notification to the municipality.

Failure to Comply with the Prevailing Wage Rate. If the Contractor fails to comply with the prevailing wage rate, she/he shall be in default on the contract.

Affirmative Action. In the performance of the services under this Agreement the Contractor agrees not to discriminate against any employee or applicant because of race, religion, marital status, age, color, sex, disability, national origin or ancestry, income level or source of income, arrest record or conviction record, less than honorable discharge, physical appearance, sexual orientation, gender identity, political beliefs, or student status. The Contractor further agrees not to discriminate against any subcontractor or person who offers to subcontract on this contract because of race, religion, color, age, disability, sex, sexual orientation, gender identity or national origin.

The Contractor agrees that within thirty (30) days after the effective date of this agreement, the Contractor will provide to the City Affirmative Action Division certain workforce utilization statistics, using a form to be furnished by the City.

If the contract is still in effect, or if the City enters into a new agreement with the Contractor, within one year after the date on which the form was required to be provided, the Contractor will provide updated workforce information using a second form, also to be furnished by the City. The second form will be submitted to the City Affirmative Action Division no later than one year after the date on which the first form was required to be provided.

The Contractor further agrees that, for at least twelve (12) months after the effective date of this contract, it will notify the City Affirmative Action Division of each of its job openings at facilities in Dane County for which applicants not already employees of the Contractor are to be considered. The notice will include a job description, classification, qualifications and application procedures and deadlines. The Contractor agrees to interview and consider candidates referred by the Affirmative Action Division if the candidate meets the minimum qualification standards established by the Contractor, and if the referral is timely. A referral is timely if it is received by the Contractor on or before the date started in the notice.

Articles of Agreement Article I

The Contractor shall take affirmative action in accordance with the provisions of this contract to insure that applicants are employed, and that employees are treated during employment without regard to race, religion, color, age, marital status, disability, sex, sexual orientation, gender identity or national original and that the employer shall provide harassment free work environment for the realization of the potential of each employee. Such action shall include, but not be limited to, the following: employment, upgrading, demotion or transfer, recruitment or recruitment advertising, layoff or termination, rates of pay or other forms of compensation and selection for training including apprenticeship insofar as it is within the control of the Contractor. The Contractor agrees to post in conspicuous places available to employees and applicants notices to be provided by the City setting out the provisions of the nondiscrimination clauses in this contract.

Article II

The Contractor shall in all solicitations or advertisements for employees placed by or on behalf of the Contractors state that all qualified or qualifiable applicants will be employed without regard to race, religion, color, age, marital status, disability, sex, sexual orientation, gender identity or national origin.

Article III

The Contractor shall send to each labor union or representative of workers with which it has a collective bargaining agreement or other contract or understanding a notice to be provided by the City advising the labor union or worker's representative of the Contractor's equal employment opportunity and affirmative action commitments. Such notices shall be posted in conspicuous places available to employees and applicants for employment.

Article V

The Contractor agrees that it will comply with all provisions of the Affirmative Action Ordinance of the City of Madison, including the contract compliance requirements. The Contractor agrees to submit the model affirmative action plan for public works contractors in a form approved by the Affirmative Action Division Manager.

Article VI

The Contractor will maintain records as required by Section 39.02(9)(f) of the Madison General Ordinances and will provide the City Affirmative Action Division with access to such records and to persons who have relevant and necessary information, as provided in Section 39.02(9)(f). The City agrees to keep all such records confidential, except to the extent that public inspection is required by law.

Article VII

In the event of the Contractor's or subcontractor's failure to comply with the Equal Employment Opportunity and Affirmative Action Provisions of this contract or Section 39.03 and 39.02 of the Madison General Ordinances, it is agreed that the City at its option may do any or all of the following:

- 1. Cancel, terminate or suspend this Contract in whole or in part.
- 2. Declare the Contractor ineligible for further City contracts until the Affirmative Action requirements are met.

3. Recover on behalf of the City from the prime Contractor 0.5 percent of the contract award price for each week that such party fails or refuses to comply, in the nature of liquidated damages, but not to exceed a total of five percent (5%) of the contract price, or five thousand dollars (\$5,000), whichever is less. Under public works contracts, if a subcontractor is in noncompliance, the City may recover liquidated damages from the prime Contractor in the manner described above. The preceding sentence shall not be construed to prohibit a prime Contractor from recovering the amount of such damage from the non-complying subcontractor.

Article VIII

The Contractor shall include the above provisions of this contract in every subcontract so that such provisions will be binding upon each subcontractor. The Contractor shall take such action with respect to any subcontractor as necessary to enforce such provisions, including sanctions provided for noncompliance.

Article IX

The Contractor shall allow the maximum feasible opportunity to small business enterprises to compete for any subcontracts entered into pursuant to this contract. (In federally funded contracts the terms "DBE, MBE and WBE" shall be substituted for the term "small business" in this Article.)

WINGRA CREEK PARKWAY, PHASE 3 CONTRACT NO. 6832

IN WITNESS WHEREOF, the Contractor has hereunto set his/her hand and seal and the City has caused these presents to be sealed with its corporate seal and to be subscribed by its Mayor and City Clerk the day and year first above written.

Countersigned:	SPEEDWAY SAND & GRAVEL, INC.
	Company: Name
Jode McKewn 12314	12/3/14
Witness Date	V. President Date
Dust Bith 12/3/14	January 12/3/14
Withess Date	"Secretary Date
CITY OF MADISON, WISCONSIN	
Provisions have been made to pay the liability	Approved as to form:
that will accrue under this contract.	1112
And bromedule	/ WM 4.7 VM
Finance Director	City Attorney
Signed this day of day of day	nbes 20 14
TOO	Mars 12/18/14
Witness	Mayor Date
Witness K. Phelps	Trie a. Christian FOR 12-5-14
\Mitnede	City Clark

SECTION I: PAYMENT AND PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS, that we and Fidelity and Deposit Company of Maryland	SPEEDWAY SAND & GRAVEL, INC. as principal,
	f the United States, for the payment of which sum to
these presents.	an respective executive and darrantematics minny by
The condition of this Bond is such that if the above perform all of the terms of the Contract entered into be construction of:	
WINGRA CREEK PA CONTRACT	
in Madison, Wisconsin, and shall pay all claims for prosecution of said work, and save the City harmless in the prosecution of said work, and shall save harm (under Chapter 102, Wisconsin Statutes) of employees to be vold, otherwise of full force, virtue and effect.	from all claims for damages because of negligence less the said City from all claims for compensation
Signed and sealed this 3rdday o	f December, 2014
Countersigned:	SPEEDWAY SAND & GRAVEL, INC. Company Name (Principal)
Dust 3th	1
Witness (Chan)	President Seat
Secretary	
Approved as to form:	Fidelity and Deposit Company of Maryland
Nout P. My	Surety Seal Salary Employee Commission By
City Attorney	Attorney-in-Fact , Elizabeth Mosca
This certifies that I have been duly licensed as an a License No. 2530156 for the year 20 authority to execute this payment and performance bor	14, and appointed as attorney-in-fact with
December 3, 2014	- Ehil henen
Date Control of the C	Agent Signature

ZURICH AMERICAN INSURANCE COMPANY COLONIAL AMERICAN CASUALTY AND SURETY COMPANY FIDELITY AND DEPOSIT COMPANY OF MARYLAND POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That the ZURICH AMERICAN INSURANCE COMPANY, a corporation of the State of New York, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, a corporation of the State of Maryland, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND a corporation of the State of Maryland (herein collectively called the "Companies"), by THOMAS O. MCCLELLAN, Vice President, in pursuance of authority granted by Article V, Section 8, of the By-Laws of said Companies, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, do hereby nominate, constitute, and appoint Ann MAY, Rana R. HUGHEY, Janice CLOOTEN, Michele A. HOLZ and Elizabeth MOSCA, all of Middleton, Wisconsin, EACH its true and lawful agent and Attorney-in-Fact, to make, execute, seal and deliver, for, and on its behalf as surety, and as its act and deed: any and all bonds and undertakings, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Companies, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the ZURICH AMERICAN INSURANCE COMPANY at its office in New York, New York., the regularly elected officers of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at its office in Owings Mills, Maryland., and the regularly elected officers of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at its office in Owings Mills, Maryland., in their own proper persons.

The said Vice President does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article V, Section 8, of the By-Laws of said Companies, and is now in force.

IN WITNESS WHEREOF, the said Vice-President has hereunto subscribed his/her names and affixed the Corporate Seals of the said ZURICH AMERICAN INSURANCE COMPANY, COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 14th day of May, A.D. 2013.

ATTEST:

ZURICH AMERICAN INSURANCE COMPANY COLONIAL AMERICAN CASUALTY AND SURETY COMPANY FIDELITY AND DEPOSIT COMPANY OF MARYLAND







Assistant Secretary Eric D. Barnes

Lie D. Bairf

Vice President Thomas O. McClellan

State of Maryland

City of Baltimore

On this 14th day of May, A.D. 2013, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, THOMAS O. MCCLELLAN, Vice President, and ERIC D. BARNES, Assistant Secretary, of the Companies, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and acknowledged the execution of same, and being by me duly sworn, deposeth and saith, that he/she is the said officer of the Company aforesaid, and that the seals affixed to the preceding instrument are the Corporate Seals of said Companies, and that the said Corporate Seals and the signature as such officer were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporations.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.

Constance a. Dunn

Constance A. Dunn, Notary Public My Commission Expires: July 14, 2015

EXTRACT FROM BY-LAWS OF THE COMPANIES

"Article V, Section 8, <u>Attorneys-in-Fact</u>. The Chief Executive Officer, the President, or any Executive Vice President or Vice President may, by written instrument under the attested corporate seal, appoint attorneys-in-fact with authority to execute bonds, policies, recognizances, stipulations, undertakings, or other like instruments on behalf of the Company, and may authorize any officer or any such attorney-in-fact to affix the corporate seal thereto; and may with or without cause modify of revoke any such appointment or authority at any time."

CERTIFICATE

I, the undersigned, Vice President of the ZURICH AMERICAN INSURANCE COMPANY, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, do hereby certify that the foregoing Power of Attorney is still in full force and effect on the date of this certificate; and I do further certify that Article V, Section 8, of the By-Laws of the Companies is still in force.

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the ZURICH AMERICAN INSURANCE COMPANY at a meeting duly called and held on the 15th day of December 1998.

RESOLVED: "That the signature of the President or a Vice President and the attesting signature of a Secretary or an Assistant Secretary and the Seal of the Company may be affixed by facsimile on any Power of Attorney...Any such Power or any certificate thereof bearing such facsimile signature and seal shall be valid and binding on the Company."

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at a meeting duly called and held on the 5th day of May, 1994, and the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the 10th day of May, 1990.

RESOLVED: "That the facsimile or mechanically reproduced seal of the company and facsimile or mechanically reproduced signature of any Vice-President, Secretary, or Assistant Secretary of the Company, whether made heretofore or hereafter, wherever appearing upon a certified copy of any power of attorney issued by the Company, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

IN TESTIMONY WHEREOF, I have hereunto subscribed my name and affixed the corporate seals of the said Companies,







Loffrey Delisio, Vice President

SECTION J: PREVAILING WAGE RATES

PREVAILING WAGE RATE DETERMINATION

Issued by the State of Wisconsin Department of Workforce Development Pursuant to s. 66.0903, Wis. Stats. Issued On: 01/06/2014

Amended On: 02/28/2014

201400001

DETERMINATION NUMBER:

Prime Contracts MUST Be Awarded or Negotiated On Or Before **EXPIRATION DATE:**

12/31/2014. If NOT, You MUST Reapply.

ALL PUBLIC WORKS PROJECTS UNDER SEC 66.0903, STATS - CITY OF MADISON PROJECT NAME:

MADISON CITY, DANE COUNTY, WI PROJECT LOCATION:

CONTRACTING AGENCY: CITY OF MADISON-ENGINEERING

worker on this project.

Contractors are responsible for correctly classifying their workers. Either call the Department of CLASSIFICATION: Workforce Development (DWD) with trade or classification questions or consult DWD's Dictionary of Occupational Classifications & Work Descriptions on the DWD website at: dwd.wisconsin.gov/er/prevailing wage rate/Dictionary/dictionary_main.htm. Time and one-half must be paid for all hours worked: OVERTIME: - over 10 hours per day on prevailing wage projects - over 40 hours per calendar week - Saturday and Sunday - on all of the following holidays: January 1; the last Monday in May; July 4; the 1st Monday in September; the 4th Thursday in November; December - The day before if January 1, July 4 or December 25 falls on a Saturday: - The day following if January 1, July 4 or December 25 falls on a Sunday. Apply the time and one-half overtime calculation to whichever is higher between the Hourly Basic Rate listed on this project determination or the employee's regular hourly rate of pay. Add any applicable Premium or DOT Premium to the Hourly Basic Rate before calculating overtime. A DOT Premium (discussed below) may supersede this time and one-half requirement. When a specific trade or occupation requires a future increase, you MUST add the full hourly increase FUTURE INCREASE: to the "TOTAL" on the effective date(s) indicated for the specific trade or occupation. If indicated for a specific trade or occupation, the full amount of such pay MUST be added to the PREMIUM PAY: "HOURLY BASIC RATE OF PAY" indicated for such trade or occupation, whevenever such pay is applicable. This premium only applies to highway and bridge projects owned by the Wisconsin Department of DOT PREMIUM: Transportation and to the project type heading "Airport Pavement or State Highway Construction." DO NOT apply the premium calculation under any other project type on this determination. Pay apprentices a percentage of the applicable journeyperson's hourly basic rate of pay and hourly APPRENTICES: fringe benefit contributions specified in this determination. Obtain the appropriate percentage from each apprentice's contract or indenture. Subjourney wage rates may be available for some of the trades or occupations indicated below with SUBJOURNEY: the exception of laborers, truck drivers and heavy equipment operators. Any employer interested in

using a subjourney classification on this project MUST complete Form ERD-10880 and request the applicable wage rate from the Department of Workforce Development PRIOR to using the subjourney This document MUST BE POSTED by the CONTRACTING AGENCY in at least one conspicuous and easily accessible place on the site of the project. A local governmental unit may post this document at the place normally used to post public notices if there is no common site on the project. This document MUST remain posted during the entire time any worker is employed on the project and MUST be physically incorporated into the specifications and all contracts and subcontracts. If you have any questions, please write to the Equal Rights Division, Labor Standards Bureau, P.O. Box 8928, Madison, Wisconsin 53708 or call (608) 266-6861.

The following statutory provisions apply to local governmental unit projects of public works and are set forth below pursuant to the requirements of s. 66.0903(8), Stats.

- s. 66.0903 (1) (f) & s. 103.49 (1) (c) "PREVAILING HOURS OF LABOR" for any trade or occupation in any area means 10 hours per day and 40 hours per week and may not include any hours worked on a Saturday or Sunday or on any of the following holidays:
 - 1. January 1.
 - 2. The last Monday in May.
 - 3. July 4.
 - 4. The first Monday in September.
 - 5. The 4th Thursday in November.
 - 6. December 25.
 - 7. The day before if January 1, July 4 or December 25 falls on a Saturday.
 - 8. The day following if January 1, July 4 or December 25 falls on a Sunday.

s. 66.0903 (10) RECORDS; INSPECTION; ENFORCEMENT.

(a) Each contractor, subcontractor, or contractor's or subcontractor's agent performing work on a project of public works that is subject to this section shall keep full and accurate records clearly indicating the name and trade or occupation of every person performing the work described in sub. (4) and an accurate record of the number of hours worked by each of those persons and the actual wages paid for the hours worked.

s. 66.0903 (11) LIABILITY AND PENALTIES.

- (a) 1. Any contractor, subcontractor, or contractor's or subcontractor's agent who fails to pay the prevailing wage rate determined by the department under sub. (3) or who pays less than 1.5 times the hourly basic rate of pay for all hours worked in excess of the prevailing hours of labor is liable to any affected employee in the amount of his or her unpaid wages or his or her unpaid overtime compensation and in an additional amount as liquidated damages as provided under subd. 2., 3., whichever is applicable.
- 2. If the department determines upon inspection under sub. (10) (b) or (c) that a contractor, subcontractor, or contractor's or subcontractor's agent has failed to pay the prevailing wage rate determined by the department under sub. (3) or has paid less than 1.5 times the hourly basic rate of pay for all hours worked in excess of the prevailing hours of labor, the department shall order the contractor to pay to any affected employee the amount of his or her unpaid wages or his or her unpaid overtime compensation and an additional amount equal to 100 percent of the amount of those unpaid wages or that unpaid overtime compensation as liquidated damages within a period specified by the department in the order.
- 3. In addition to or in lieu of recovering the liability specified in subd. 1. as provided in subd. 2., any employee for and in behalf of that employee and other employees similarly situated may commence an action to recover that liability in any court of competent jurisdiction. If the court finds that a contractor, subcontractor, or contractor's or subcontractor's agent has failed to pay the prevailing wage rate determined by the department under sub. (3) or has paid less than 1.5 times the hourly basic rate of pay for all hours worked in excess of the prevailing hours of labor, the court shall order the contractor, subcontractor, or agent to pay to any affected employee the amount of his or her unpaid wages or his or her unpaid overtime compensation and an additional amount equal to 100 percent of the amount of those unpaid wages or that unpaid overtime compensation as liquidated damages. 5. No employee may be a party plaintiff to an action under subd. 3. unless the employee consents in writing to become a party and the consent is filed in the court in which the action is brought. Notwithstanding s. 814.04 (1), the court shall, in addition to any

judgment awarded to the plaintiff, allow reasonable attorney fees and costs to be paid by the defendant.

BUILDING OR HEAVY CONSTRUCTION

Includes sheltered enclosures with walk-in access for the purpose of housing persons, employees, machinery, equipment or supplies and non-sheltered work such as canals, dams, dikes, reservoirs, storage tanks, etc. A sheltered enclosure need not be "habitable" in order to be considered a building. The installation of machinery and/or equipment, both above and below grade level, does not change a project's character as a building. On-site grading, utility work and landscaping are included within this definition. Residential buildings of four (4) stories or less, agricultural buildings, parking lots and driveways are NOT included within this definition.

	SKILLED TRADES			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
101	Acoustic Ceiling Tile Installer	30.48	15.90	46.38
102	Boilermaker Future Increase(s): Add \$1.50/hr on 1/01/2015; Add \$1.50/hr. on 01/01/2016	32.05	28.04	60.09
103	Bricklayer, Blocklayer or Stonemason Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	32.01	17.35	49.36
104	Cabinet Installer	30.48	15.90	46.38
105	Carpenter	30.48	15.90	46.38
106	Carpet Layer or Soft Floor Coverer	30.48	15.90	46.38
107	Cement Finisher	31.58	16.13	47.71
108	Drywall Taper or Finisher	24.80	16.60	41.40
109 .	Electrician Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	34.07	19.25	53.32
110	Elevator Constructor	42.86	23.84	66.70
111	Fence Erector	24,72	0.00	24.72
112	Fire Sprinkler Fitter	36.07	18.73	54.80
113	Glazier	38.03	13.42	51.45
114	Heat or Frost Insulator	33.68	24.31	57.99
115	Insulator (Batt or Blown)	15.00	9.50	24.50
116	ironworker	31.25	19.46	50.71
117	Lather	30.48	15.90	46.38

CODE	Fringe Benefits Must Be Paid On All Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
118	Line Constructor (Electrical)	38.25	17.31	55.56
119	Marble Finisher	26.89	19.18	46.07
120	Marble Mason	32.01	17.35	49.36
121	Metal Building Erector	22.00	10.00	32.00
122	Millwright	32.11	15.95	48.06
123	Overhead Door Installer	20.95	4.94	25.89
124	Painter	24.50	16.60	41.10
125	Pavement Marking Operator	30.00	0.00	30.00
126	Piledriver	30.98	15.90	46.88
127	Pipeline Fuser or Welder (Gas or Utility)	30.79	19.74	50.53
129	Plasterer	31.03	17.71	48.74
130	Plumber Future Increase(s): Add \$1/hr on 6/1/2014.	36.42	16.87	53.29
132	Refrigeration Mechanic	41.60	16.71	58.31
133	Roofer or Waterproofer	29.40	6.25	35.65
134	Sheet Metal Worker	34.45	22.57	57.02
135	Steamfitter Future Increase(s): Add \$1.70/hr on 6/1/2014.	42.95	17.81	60.76
137	Teledata Technician or Installer Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	22.25	12.24	34.49
138	Temperature Control Installer	32.94	18.80	51.74
139	Terrazzo Finisher	26.89	19.18	46.07
140	Terrazzo Mechanic	30.20	18.42	48.62
141 .	Tile Finisher	23.85	17.18	41.03
142	Tile Setter	29.81	17.18	46.99
143	Tuckpointer, Caulker or Cleaner	35.25	13.15	48.40
144	Underwater Diver (Except on Great Lakes)	34.48	15.90	50.38
146	Well Driller or Pump Installer	25.32	15.65	40.97
147	Siding Installer	25.92	18.04	43.96

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	
CODE	TRADE OR OCCUPATION	OF PAY	BENEFITS \$	TOTAL \$
150	Heavy Equipment Operator - ELECTRICAL LINE CONSTRUCTION ONLY	29.16	14.34	43.50
151	Light Equipment Operator -ELECTRICAL LINE CONSTRUCTION ONLY	30.60	14.86	45.46
152	Heavy Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	26.78	13.63	40.41
153	Light Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	24.86	12.97	37.83
154	Groundman - ELECTRICAL LINE CONSTRUCTION ONLY	21.75	12.70	34.45
	TRUCK DRIVERS			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	<u>TOTAL</u> \$
201	Single Axle or Two Axle	32.39	18.46	50.85
203	Three or More Axle	18.00	22.88	40.88
204	Articulated, Euclid, Dumptor, Off Road Material Hauler	32.89	18.96	51.85
205	Pavement Marking Vehicle	18.00	22.88	40.88
207	Truck Mechanic	18.00	22.88	40.88
	LABORERS			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY	HOURLY FRINGE BENEFITS	<u>TOTAL</u>
		\$	\$	\$
301	General Laborer Premium Increase(s): Add \$1.00/hr for certified welder; Add \$.25/hr for mason tender	24.21	14.63	38.84
302	Asbestos Abatement Worker	24.36	14.44	38.80
303	Landscaper	21.01	9.37	30.38
310	Gas or Utility Pipeline Laborer (Other Than Sewer and Water)	21.01	13.63	34.64
311	Fiber Optic Laborer (Outside, Other Than Concrete Encased) Premium Increase(s): DOT PREMIUMS: Pay two times the hourly basic rate on New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	18.33	13.65	31.98
314	Railroad Track Laborer	23.46	3.30	26.76
315	Final Construction Clean-Up Worker	16.00	0.00	16.00

HEAVY EQUIPMENT OPERATORS SITE PREPARATION, UTILITY OR LANDSCAPING WORK ONLY

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY	HOURLY	-
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE BENEFITS \$	TOTAL \$
501	Air Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Asphalt Milling Machine; Boring Machine (Directional, Horizontal or Vertical); Backhoe (Track Type) Having a Mfgr's Rated Capacity of 130,000 Lbs. or Over; Backhoe (Track Type) Having a Mfgr's Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. & Under); Bulldozer or Endloader (Over 40 hp); Compactor (Self-Propelled 85 Ft Total Drum Width & Over, or Tractor Mounted, Towed & Light Equipment); Concrete Batch Plant, Batch Hopper; Concrete Breaker (Large, Auto, Vibratory/Sonic, Manual or Remote); Crane, Shovel, Dragline, Clamshells; Forklift (Machinery Moving or Steel Erection, 25 Ft & Over); Gradall (Cruz-Aire Type); Grader or Motor Patrol; Master Mechanic; Mechanic or Welder; Robotic Tool Carrier (With or Without Attachments); Scraper (Self Propelled or Tractor Drawn) 5 cu yds or More Capacity; Tractor or Truck Mounted Hydraulic Backhoe; Tractor or Truck Mounted Hydraulic Crane (10 Tons or Under); Tractor (Scraper, Dozer, Pusher, Loader); Trencher (Wheel Type or Chain Type Having Over 8 Inch Bucket).		18.96	52.38
502	Backfiller; Broom or Sweeper; Bulldozer or Endloader (Under 40 hp); Environmental Burner; Forestry Equipment, Timbco, Tree Shear, Tub Grinder, Processor; Jeep Digger; Screed (Milling Machine); Skid Rig; Straddle Carrier or Travel Lift; Stump Chipper; Trencher (Wheel Type or Chain Type Having 8 Inch Bucket & Under).	32.89	18.96	51.85
503	Air Compressor (&/or 400 CFM or Over); Augers (Vertical & Horizontal); Compactor (Self-Propelled 84 Ft Total Drum Width & Under, or Tractor Mounted, Towed & Light Equipment); Crusher, Screening or Wash Plant; Farm or Industrial Type Tractor; Forklift; Generator (&/or 150 KW or Over); Greaser; High Pressure Utility Locating Machine (Daylighting Machine); Mulcher; Oiler; Post Hole Digger or Driver; Pump (3 Inch or Over) or Well Points; Refrigeration Plant or Freeze Machine; Rock, Stone Breaker; Skid Steer Loader (With or Without Attachments); Vibratory Hammer or Extractor, Power Pack.	30.82	18.96	49.78
04	Work Performed on the Great Lakes Including Diver, Wet Tender or Hydraulic Dredge Engineer.	38.80	20,17	58.97
05	Work Performed on the Great Lakes Including Crane or Backhoe Operator; Assistant Hydraulic Dredge Engineer; Hydraulic Dredge Leverman or Diver's Tender; Mechanic or Welder; 70 Ton & Over Tug Operator.	41.65	21.71	63.36
	Premium Increase(s): Add \$.50/hr for Friction Crane, Lattice Boom or Crane Certification (CCO).		· · · · · · · · · · · · · · · · · · ·	
06	Work Performed on the Great Lakes Including Deck Equipment Operator or Machineryman (Maintains Cranes Over 50 Tons or Backhoes 115,000 Lbs. or More); Tug, Launch or Loader, Dozer or Like Equipment When Operated on a Barge, Breakwater Wall, Slip, Dock or Scow, Deck Machinery.	37.10	21.57	58.67

Page	7	of	28

54.54

507	Work Performed on the Great Lakes Including Deck Equipment Operator, Machineryman or Fireman (Operates 4 Units or More or Maintains Cranes 50 Tons or Under or Backhoes 115,000 Lbs. or Under); Deck Hand, Deck
	Engineer or Assistant Tug Operator, Off Road Trucks - Great Lakes ONLY.

34.50 20.04

HEAVY EQUIPMENT OPERATORS EXCLUDING SITE PREPARATION, UTILITY, PAVING LANDSCAPING WORK

~~ ~	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	TOTAL
CODE	TRADE OR OCCUPATION	OF PAY \$	<u>BENEFITS</u> \$	\$
508	Boring Machine (Directional); Crane, Tower Crane, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of Over 100 Tons, Self-Erecting Tower Crane With a Lifting Capacity of Over 4,000 Lbs., Crane With Boom Dollies; Crane, Tower Crane, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 176 Ft or Over; Master Mechanic. Premium Increase(s): Add \$.50/hr for >200 Ton / Add \$1/hr at 300 Ton / Add \$1.50/hr at 400 Ton / Add \$2/hr at 500 Ton & Over.	35.62	18.96	54,58
509	Backhoe (Track Type) Having a Mfgr's Rated Capacity of 130,000 Lbs. or Over; Boring Machine (Horizontal or Vertical); Caisson Rig; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of 100 Tons or Under, Self-Erecting Tower Crane With A Lifting Capacity Of 4,000 Lbs. & Under; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 175 Ft or Under; Pile Driver; Versi Lifts, Tri-Lifts & Gantrys (20,000 Lbs. & Over).	36.35	6.95	43.30
510	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. & Under); Concrete Bump Cutter, Grinder, Planing or Grooving Machine; Concrete Laser/Screed; Concrete Paver (Slipform); Concrete Pump (Over 46 Meter), Concrete Conveyor (Rotec or Bidwell Type); Concrete Slipform Placer Curb & Gutter Machine; Concrete Spreader & Distributor; Dredge (NOT Performing Work on the Great Lakes); Forklift (Machinery Moving or Steel Erection, 25 Ft & Over); Gradall (Cruz-Aire Type); Hydro-Blaster (10,000 PSI or Over); Milling Machine; Skid Rig; Traveling Crane (Bridge Type).	33.42	18.96	52.38
511	Air, Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Bulldozer or Endloader (Over 40 hp); Compactor (Self-Propelled 85 Ft Total Drum Width & Over, or Tractor Mounted, Towed & Light Equipment); Concrete Pump (46 Meter & Under), Concrete Conveyor (Rotec or Bidwell Type); Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Environmental Burner; Gantrys (Under 20,000 Lbs.); Grader or Motor Patrol; High Pressure Utility Locating Machine (Daylighting Machine); Manhoist; Material or Stack Hoist; Mechanic or Welder; Railroad Track Rail Leveling Machine, Tie Placer, Extractor, Tamper, Stone Leveler or Rehabilitation Equipment; Roller (Over 5 Ton); Scraper (Self Propelled or Tractor Drawn) 5 cu yd or More Capacity; Screed (Milling Machine); Sideboom; Straddle Carrier or Travel Lift; Tining or Curing Machine; Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck Mounted Hydraulic Backhoe; Tractor or Truck Mounted Hydraulic Crane (10 Tons or Under); Trencher (Wheel Type or Chain Type Having Over 8-Inch Bucket).		18.96	51.85

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY	HOURLY		
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE BENEFITS \$	TOTAL \$	
512	Backfiller; Broom or Sweeper; Bulldozer or Endloader (Under 40 hp); Compactor (Self-Propelled 84 Ft Total Drum Width & Under, or Tractor Mounted, Towed & Light Equipment); Concrete Batch Plant, Batch Hopper; Concrete Breaker (Large, Auto, Vibratory/Sonic, Manual or Remote); Concrete Conveyor System; Concrete Finishing Machine (Road Type); Fireman (Pile Driver & Derrick NOT Performing Work on the Great Lakes); Grout Pump; Hoist (Tugger, Automatic); Industrial Locomotives; Jeep Digger; Lift Slab Machine; Mulcher; Roller (Rubber Tire, 5 Ton or Under); Screw or Gypsum Pumps; Stabilizing or Concrete Mixer (Self-Propelled or 14S or Over); Stump Chipper; Trencher (Wheel Type or Chain Type Having 8-Inch Bucket & Under); Winches & A-Frames.	30.82	18.96	49.78	
513	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Augers (Vertical & Horizontal); Boatmen (NOT Performing Work on the Great Lakes); Boiler (Temporary Heat); Crusher, Screening or Wash Plant; Elevator; Farm or Industrial Type Tractor; Fireman (Asphalt Plant NOT Performing Work on the Great Lakes); Forklift; Generator (&/or 150 KW or Over); Greaser; Heaters (Mechanical); Loading Machine (Conveyor); Oiler; Post Hole Digger or Driver; Prestress Machine; Pump (3 Inch or Over) or Well Points; Refrigeration Plant or Freeze Machine; Robotic Tool Carrier (With or Without Attachments); Rock, Stone Breaker; Skid Steer Loader (With or Without Attachments); Vibratory Hammer or Extractor, Power Pack.	24.19	17.89	42.08	
514	Gas or Utility Pipeline, Except Sewer & Water (Primary Equipment).	36.34	21.14	57.48	
515	Gas or Utility Pipeline, Except Sewer & Water (Secondary Equipment). Future Increase(s): Add \$1.60/hr on 06/01/2014; Add \$1.65/hr on 06/01/2015.	32.32	18.55	50.87	
516	Fiber Optic Cable Equipment Future Increase(s): Add \$1.75/hr on 02/01/2014.	27.89	17.20	45.09	

SEWER, WATER OR TUNNEL CONSTRUCTION

includes those projects that primarily involve public sewer or water distribution, transmission or collection systems and related tunnel work (excluding buildings).

	SKILLED TRADES				
CODE	Fringe Benefits Must Be Paid On All Hours Worked TRADE OR OCCUPATION	HOUF BASIO OF PA \$	RATE	HOURLY FRINGE BENEFITS \$	TOTAL \$
103	Bricklayer, Blocklayer or Stonemason Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	.3	5.10	18.40	53.50
105	Carpenter Future Increase(s): Add \$1.25/hr on 6/2/2014. Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	3:	3,68	19.81	53.49
107	Cement Finisher Future Increase(s): Add \$1.87 on 6/1/14; Add \$1.87 on 6/1/15; Add \$1.75 on 6/1/16. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.40/hr when the Wisconsin Department of Transportation or responsible governing agency requires that work be performed at night under artificial illumination with traffic control and the work is completed after sunset and before sunrise.	3:	3.51	16.13	49.64
109	Electrician Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	3:	2.82	22.61	55.43
111	Fence Erector	24	4.72	0.00	24.72
116	Ironworker	. 3	1.25	19.46	50.71
118	Line Constructor (Electrical)	38	3.25	17.31	55.56
125	Pavement Marking Operator	16	6.00	7.35	23.35
126	Piledriver	30	0.98	15.90	46.88
130	Plumber	c 33	3.75	14.07	47.82
135	Steamfitter	42	2.45	16.71	59.16
137	Teledata Technician or Installer	2	1.89	11.85	33.74

CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
143	Tuckpointer, Caulker or Cleaner	35.25	13.15	48.40
144	Underwater Diver (Except on Great Lakes)	38.80	20.17	58.97
146	Well Driller or Pump Installer	25.32	15.65	40.97
150	Heavy Equipment Operator - ELECTRICAL LINE CONSTRUCTION ONLY	29.16	14.34	43.50
151	Light Equipment Operator -ELECTRICAL LINE CONSTRUCTION ONLY	30.60	14.86	45.46
152	Heavy Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	26.78	13.63	40.41
153	Light Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	24.86	12.97	37.83
154	Groundman - ELECTRICAL LINE CONSTRUCTION ONLY	21.75	12.70	34.45
	TRUCK DRIVERS			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
201	Single Axle or Two Axle	30.00	15.00	45.00
203	Three or More Axle	16.00	7.35	23.35
204	Articulated, Euclid, Dumptor, Off Road Material Hauler	32.89	18.96	51.85
205	Pavement Marking Vehicle	16.00	7.35	23.35
207	Truck Mechanic	16.00	7.35	23.35
	LABORERS			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
301	General Laborer Premium Increase(s): Add \$.20 for blaster, bracer, manhole builder, caulker, bottomman and power tool; Add \$.55 for pipelayer; Add \$1.00 for tunnel work 0-15 lbs. compressed air; Add \$2.00 for over 15-30 lbs. compressed air; Add \$3.00 for over 30 lbs. compressed air.	25.60	14.62	40.22
303	Landscaper	25.28	11.46	36.74
304	Flagperson or Traffic Control Person	24.70	10.72	35.42
311	Fiber Optic Laborer (Outside, Other Than Concrete Encased)	18.31	12.67	30.98
314	Railroad Track Laborer	23.46	3.30	26.76

HEAVY EQUIPMENT OPERATORS SEWER, WATER OR TUNNEL WORK

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	ı.
CODE	TRADE OR OCCUPATION	OF PAY	BENEFITS	TOTAL
		\$	\$	\$
521	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of 130,000 Lbs. or Over; Caisson Rig; Crane, Tower Crane, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 176 Ft or Over; Crane, Tower Crane, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of Over 100 Tons, Self-Erecting Tower Crane With a	34.62	18.96	53.58
	Lifting Capacity Of Over 4,000 Lbs., Crane With Boom Dollies; Master Mechanic; Pile Driver.			
	Premium Increase(s): Add \$.25/hr for all >45 Ton lifting capacity cranes			
522	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. & Under); Boring Machine (Directional); Concrete Bump Cutter, Grinder, Planing or Grooving Machine; Concrete	33.42	18.96	52.38
	Laser/Screed; Concrete Paver (Slipform); Concrete Pump (Over 46 Meter), Concrete Conveyor (Rotec or Bidwell Type); Concrete Spreader & Distributor; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 175 Ft or Under;			
	Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of 100 Tons or Under, Self-Erecting Tower Crane With a Lifting Capacity of 4,000 Lbs. & Under;	· ·		
	Dredge (NOT Performing Work on the Great Lakes); Milling Machine; Skid Rig; Telehandler; Traveling Crane (Bridge Type).		•	
523	Air Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Boring Machine (Horizontal or Vertical); Bulldozer or Endloader (Over 40 hp); Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Concrete Pump (46 Meter & Under), Concrete Conveyor (Rotec		18.96	51,85
	or Bidwell Type); Concrete Slipform Placer Curb & Gutter Machine; Gradall (Cruz-Aire Type); Grader or Motor Patrol; Hydro-Blaster (10,000 PSI or Over); Manhoist; Material or Stack Hoist; Mechanic or Welder;	,		
	Roller (Over 5 Ton); Scraper (Self Propelled or Tractor Drawn) 5 cu yd or More Capacity; Screed (Milling Machine); Sideboom; Straddle Carrier or Travel Lift; Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck			
	Mounted Hydraulic Backhoe; Tractor or Truck Mounted Hydraulic Crane (10 Tons or Under); Trencher (Wheel Type or Chain Type Having Over 8-Inch Bucket).			

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	
CODE	TRADE OR OCCUPATION	OF PAY	BENEFITS \$	TOTAL \$
524	Backfiller; Broom or Sweeper; Bulldozer or Endloader (Under 40 hp); Compactor (Self-Propelled 85 Ft Total Drum Width & Over, or Tractor Mounted, Towed & Light Equipment); Concrete Batch Plant, Batch Hopper; Concrete Breaker (Large, Auto, Vibratory/Sonic, Manual or Remote); Concrete Conveyor System; Concrete Finishing Machine (Road Type); Environmental Burner; Fireman (Pile Driver & Derrick NOT Performing Work on the Great Lakes); Forestry Equipment, Timbco, Tree	35.11	19.45	54.56
	Shear, Tub Grinder, Processor; Hoist (Tugger, Automatic); Grout Pump; Jeep Digger; Lift Slab Machine; Mulcher; Power Subgrader; Pump (3 Inch or Over) or Well Points; Robotic Tool Carrier (With or Without Attachments); Roller (Rubber Tire, 5 Ton or Under); Screw or Gypsum Pumps; Stabilizing or Concrete Mixer (Self-Propelled or 14S or Over);			
	Stump Chipper; Tining or Curing Machine; Trencher (Wheel Type or Chain Type Having 8-Inch Bucket & Under); Winches & A-Frames. Future Increase(s): Add \$1.05/hr on 6/2/2014; Add \$1.55/hr on 6/1/2015. Premium Increase(s): Add \$.25/hr for operating tower crane.			·
525	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Augers (Vertical & Horizontal); Compactor (Self-Propelled 84 Ft Total Drum Width & Under, or Tractor Mounted, Towed & Light Equipment); Crusher, Screening or Wash Plant; Farm or Industrial Type Tractor; Fireman (Asphalt Plant NOT Performing Work on the Great	30.19	20.94	51.13
	Lakes); Generator (&/or 150 KW or Over); Heaters (Mechanical); High Pressure Utility Locating Machine (Daylighting Machine); Loading Machine (Conveyor); Post Hole Digger or Driver; Refrigeration Plant or Freeze Machine; Rock, Stone Breaker; Skid Steer Loader (With or Without Attachments); Vibratory Hammer or Extractor, Power Pack.			
526	Boiler (Temporary Heat); Forklift; Greaser; Oiler.	24.19	17.89	42.08
527	Work Performed on the Great Lakes Including Diver; Wet Tender or Hydraulic Dredge Engineer.	38.80	20.17	58.97
528	Work Performed on the Great Lakes Including 70 Ton & Over Tug Operator; Assistant Hydraulic Dredge Engineer; Crane or Backhoe Operator; Hydraulic Dredge Leverman or Diver's Tender; Mechanic or Welder.	38.80	20.17	58.97
529	Work Performed on the Great Lakes Including Deck Equipment Operator or Machineryman (Maintains Cranes Over 50 Tons or Backhoes 115,000 Lbs. or More); Tug, Launch or Loader, Dozer or Like Equipment When Operated on a Barge, Breakwater Wall, Slip, Dock or Scow, Deck Machinery.	34.50	20.04	54.54
530	Work Performed on the Great Lakes Including Deck Equipment Operator; Machineryman or Fireman (Operates 4 Units or More or Maintains Cranes 50 Tons or Under or Backhoes 115,000 Lbs. or Under), Deck Hand, Deck Engineer or Assistant Tug Operator; Off Road Trucks - Great Lakes ONLY.	34.50	20.04	54.54

AIRPORT PAVEMENT OR STATE HIGHWAY CONSTRUCTION

Includes all airport projects (excluding buildings) and all projects awarded by the Wisconsin Department of Transportation (excluding buildings).

	SKILLED TRADES			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL
103	Bricklayer, Blocklayer or Stonemason	32.01	17.35	49.36
105	Carpenter	30.48	15.90	46.38
107	Cement Finisher Future Increase(s): Add \$1.87 on 6/1/14; Add \$1.87 on 6/1/15; Add \$1.75 on 6/1/16. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic	33.51	16.13	49.64
	rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.40/hr when the Wisconsin Department of Transportation or responsible governing agency requires that work be performed at night under artificial illumination with traffic control and the work is completed after sunset and before sunrise.			
109	Electrician Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	34.07	19.25	53.32
111	Fence Erector	24.72	0.00	24.72
116	Ironworker	31.25	19.46	50.71
118	Line Constructor (Electrical)	38.25	17.31	55.56
124	Painter	21.87	11.37	. 33.24
125	Pavement Marking Operator	30.00	0.00	30.00
126	Piledriver	30.98	15.90	46.88
133	Roofer or Waterproofer	29.40	6.25	35.6 <u>5</u>
137	Teledata Technician or Installer	21.89	11.85	33.74
143	Tuckpointer, Caulker or Cleaner	35.25	13.15	48.40
144	Underwater Diver (Except on Great Lakes)	34.48	15.90	50.38
150	Heavy Equipment Operator - ELECTRICAL LINE CONSTRUCTION ONLY	34.43	15.24	49.67
151	Light Equipment Operator -ELECTRICAL LINE CONSTRUCTION ONLY	35.50	15.89	51.39

CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL
152	Heavy Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	26.78	13.63	40.41
153	Light Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	24.86	12.97	37.83
154	Groundman - ELECTRICAL LINE CONSTRUCTION ONLY	21.75	12.70	34.45
	TRUCK DRIVERS		V-10-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1	
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE <u>BENEFITS</u> \$	TOTAL \$
201	Single Axle or Two Axle	34.22	19.90	54.12
203	Three or More Axle Future Increase(s): Add \$1.30/hr on 6/1/2014. Premium Increase(s): DOT PREMIUM: Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.	24.52	17.77	42.29
204	Articulated, Euclid, Dumptor, Off Road Material Hauler Future Increase(s): Add \$1.75/hr on 6/1/14); Add \$1.25/hr on 6/1/15); Add \$1.30/hr on 6/1/16); Add \$1.25/hr on 6/1/17. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine ss/civilrights/laborwages/pwc.htm.	29.27	20.40	49.67
205	Pavement Marking Vehicle	23.31	17.13	40.44
206	Shadow or Pilot Vehicle	34.22	19.90	54.12
207	Truck Mechanic	23.31	17,13	40.44

	LABORERS				
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION		HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL
301	General Laborer		29.32	14.63	43.95
	Future Increase(s): Add \$1.60/hr on 6/1/2014.				j.
	Premium Increase(s): Add \$.10/hr for topman, air tool operator, vibrator or tamper operator (mechanical hand operated), chain saw operator and demolition burning torch laborer; Add \$.15/hr for bituminous worker (raker and luteman), formsetter (curb, sidewalk and pavement) and strike off man; Add \$.20/hr for blaster and powderman; Add				
	\$.25/hr for bottomman; Add \$.35/hr for line and grade specialist; Add \$.45/hr for pipelayer. / DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New				
	Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.25/hr for work on projects involving temporary traffic control setup, for lane and shoulder closures, when work under artificial illumination conditions is necessary as required by the project provisions (including prep	· · · · · · · · · · · · · · · · · · ·			
	time prior to and/or cleanup after such time period).				
302	Asbestos Abatement Worker	•	24.36	14.44	38.80
303	Landscaper Future Increase(s): Add \$1.60/hr on 6/1/14. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day,		29.32	14.63	43.95
	Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.25/hr for work on projects involving temporary traffic control setup, for lane and shoulder closures, when work under artificial illumination conditions is necessary as required by the project provisions (including prep time prior to and/or cleanup after such time period).			-	Novego e e
304	Flagperson or Traffic Control Person Future Increase(s): Add \$1.60/hr on 6/1/2014. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day,		25.67	14.63	40.30
	Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.25/hr when the Wisconsin Department of Transportation or responsible governing agency requires that work be performed at night under artificial illumination with traffic control and the work is completed after sunset and before sunrise.				
311	Fiber Optic Laborer (Outside, Other Than Concrete Encased)		18.31	12.67	30.98
314	Railroad Track Laborer		23.46	3.30	26.76

HEAVY EQUIPMENT OPERATORS AIRPORT PAVEMENT OR STATE HIGHWAY CONSTRUCTION

<i>'</i>	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY	HOURLY	
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE BENEFITS \$	TOTAL \$
531	Crane, Tower Crane, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 176 Ft or Over; Crane, Tower Crane, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of Over 100 Tons, Self-Erecting Tower Crane With a Lifting Capacity Of Over 4,000 Lbs., Crane With Boom Dollies; Traveling Crane (Bridge Type). Future Increase(s):	36.72	20.40	57.12.
- -	Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine			
532	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of 130,000 Lbs. or Over; Caisson Rig; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 175 Ft or Under; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of 100 Tons or Under, Self-Erecting Tower Crane With A Lifting Capacity Of 4,000 Lbs., & Under; Dredge (NOT Performing Work on the Great Lakes); Licensed Boat Pilot (NOT Performing Work on the Great Lakes); Pile Driver. Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine ss/civilrights/laborwages/pwc.htm.	36.22	20.40	56.62

	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	
<u>CODE</u>	TRADE OR OCCUPATION	OF PAY	BENEFITS	TOTAL \$
		Ψ	Ψ	
533	Air Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Asphalt Heater, Planer & Scarifier; Asphalt Milling Machine; Asphalt Screed; Automatic Subgrader (Concrete); Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. & Under); Bituminous (Asphalt) Plant & Paver, Screed; Boatmen (NOT Performing Work on the Great Lakes); Boring Machine (Directional, Horizontal or Vertical); Bridge (Bidwell) Paver; Bulldozer or Endloader; Concrete Batch Plant, Batch Hopper; Concrete Breaker (Large, Auto, Vlbratory/Sonic, Manual or Remote); Concrete Bump Cutter, Grinder, Planing or Grooving Machine; Concrete Conveyor System; Concrete Laser/Screed; Concrete Paver (Slipform); Concrete Pump, Concrete Conveyor (Rotec or Bidwell Type); Concrete Slipform Placer Curb & Gutter Machine; Concrete Spreader & Distributor; Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Crane With a Lifting Capacity of 25 Tons or Under; Forestry Equipment, Timbco, Tree Shear, Tub Grinder, Processor; Gradall (Cruz-Aire Type); Grader or Motor Patrol; Grout Pump; Hydro-Blaster (10,000 PSI or Over); Loading Machine (Conveyor); Material or Stack Hoist; Mechanic or Welder; Milling Machine;		20.40	56.12
	Post Hole Digger or Driver; Roller (Over 5 Ton); Scraper (Self Propelled or Tractor Drawn) 5 cu yds or More Capacity; Shoulder Widener; Sideboom; Skid Rig; Stabilizing or Concrete Mixer (Self-Propelled or 14S or Over); Straddle Carrier or Travel Lift; Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck Mounted Hydraulic Backhoe; Trencher (Wheel Type or Chain Type); Tube Finisher; Tugger (NOT Performing Work on the Great			
	Lakes); Winches & A-Frames.			

Future Increase(s):

Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017.

Premium Increase(s):

DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/business/civilrights/laborwages/pwc.htm.

:	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	
CODE	TRADE OR OCCUPATION	OF PAY	<u>BENEFITS</u>	TOTAL
534	Belting, Burlap, Texturing Machine; Broom or Sweeper; Compactor (Self-Propelled or Tractor Mounted, Towed & Light Equipment); Concrete Finishing Machine (Road Type); Environmental Burner; Farm or Industrial Type Tractor; Fireman (Asphalt Plant, Pile Driver & Derrick NOT Performing Work on the Great Lakes); Forklift; Greaser; Hoist (Tugger,	35.46	\$ 20.40	55.86
	Automatic); Jeep Digger; Joint Sawer (Multiple Blade); Launch (NOT Performing Work on the Great Lakes); Lift Slab Machine; Mechanical Float; Mulcher; Power Subgrader; Robotic Tool Carrier (With or Without Attachments); Roller (Rubber Tire, 5 Ton or Under); Self Propelled Chip Spreader; Shouldering Machine; Skid Steer Loader (With or Without Attachments); Telehandler; Tining or Curing Machine. Future Increase(s):			
	Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic			
	rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/business/civilrights/laborwages/pwc.htm.			.*
535	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Augers (Vertical & Horizontal); Automatic Belt Conveyor & Surge Bin; Boiler (Temporary Heat); Concrete Proportioning Plant; Crusher, Screening or Wash Plant; Generator (&/or 150 KW or Over); Heaters (Mechanical); High Pressure Utility Locating Machine (Daylighting Machine); Mudjack; Oiler; Prestress Machine; Pug Mill; Pump (3 Inch or Over) or Well Points; Rock, Stone Breaker; Screed (Milling Machine); Stump Chipper; Tank Car Heaters; Vibratory Hammer or Extractor, Power	35.17	20.40	55.57
	Pack. Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day,			
	Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/business/civilrights/laborwages/pwc.htm.			
536	Fiber Optic Cable Equipment.	26.69	16.65	43.34
537	Work Performed on the Great Lakes Including Diver; Wet Tender or Hydraulic Dredge Engineer.	38.80	20.17	58.97
538	Work Performed on the Great Lakes Including 70 Ton & Over Tug Operator; Assistant Hydraulic Dredge Engineer; Crane or Backhoe Operator; Hydraulic Dredge Leverman or Diver's Tender; Mechanic or Welder.	38.80	20.17	58.97

CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
539	Work Performed on the Great Lakes Including Deck Equipment Operator or Machineryman (Maintains Cranes Over 50 Tons or Backhoes 115,000 Lbs. or More); Tug, Launch or Loader, Dozer or Like Equipment When Operated on a Barge, Breakwater Wall, Slip, Dock or Scow, Deck Machinery.	34.50	20.04	54.54
540	Work Performed on the Great Lakes Including Deck Equipment Operator, Machineryman or Fireman (Operates 4 Units or More or Maintains Cranes 50 Tons or Under or Backhoes 115,000 Lbs. or Under); Deck Hand, Deck Engineer or Assistant Tug Operator; Off Road Trucks-Great Lakes ONLY.	S	20.04	54.54

LOGAL STREET OR MISCELLANEOUS PAVING CONSTRUCTION

Includes roads, streets, alleys, trails, bridges, paths, racetracks, parking lots and driveways (except residential or agricultural), public sidewalks or other similar projects (excluding projects awarded by the Wisconsin Department of Transportation).

	SKILLED TRADES	-		
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL
103	Bricklayer, Blocklayer or Stonemason	32.01	17.35	49.36
105	Carpenter	32.93	19.93	52.86
107	Cement Finisher	31.48	15.68	47.16
109	Electrician	31.27	22.81	54.08
111	Fence Erector	24.72	0.00 (24.72
116	Ironworker	31.25	19.46	50.71
118	Line Constructor (Electrical)	38.25	17.31	55,56
124	Painter	24.50	16.60	41.10
125	Pavement Marking Operator	30.00	0.00	30.00
126	Piledriver	30.98	15.90	46.88
133	Roofer or Waterproofer	29.40	6.25	35.65
137	Teledata Technician or Installer	21.89	11.85	33.74
143	Tuckpointer, Caulker or Cleaner	35.25	13.15	48.40
144	Underwater Diver (Except on Great Lakes)	38.80	20.17	58.97
150	Heavy Equipment Operator - ELECTRICAL LINE CONSTRUCTION ONLY	34.43	15.24	49.67
151	Light Equipment Operator -ELECTRICAL LINE CONSTRUCTION ONLY	30.60	14.86	45.46
152	Heavy Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	26.78	13.63	40.41
153	Light Truck Driver - ELECTRICAL LINE CONSTRUCTION ONLY	24.86	12.97	37.83
154	Groundman - ELECTRICAL LINE CONSTRUCTION ONLY	21.75	12.70	34.45
	TRUCK DRIVERS			
ODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
201	Single Axle or Two Axle	30.00	15.00	45.00

Detern	nination No. 201400001			Page 21 of 28
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL
203	Three or More Axle	17.00	0.00	17.00
204	Articulated, Euclid, Dumptor, Off Road Material Hauler	32.89	18.96	51.85
205	Pavement Marking Vehicle	17.00	0.00	17.00
206	Shadow or Pilot Vehicle	30.00	15.00	45.00
207	Truck Mechanic	17.00	0.00	17.00
	LABORERS			
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
301	General Laborer	28.07	13.25	41.32
303	Landscaper Future Increase(s): Add \$1.60/hr on 6/1/14. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.25/hr for work on projects involving temporary traffic control setup, for lane and shoulder closures, when work under artificial illumination conditions is necessary as required by the project provisions (including prep time prior to and/or cleanup after such time period).	29.04	14.63	43.67
304	Flagperson or Traffic Control Person	24.70	10.72	35.42
311	Fiber Optic Laborer (Outside, Other Than Concrete Encased)	18.31	12.67	30.98
314	Railroad Track Laborer	23.46	3.30	26.76

HEAVY EQUIPMENT OPERATORS CONCRETE PAVEMENT OR BRIDGE WORK

CODE	Fringe Benefits Must Be Paid On All Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
541	Crane, Tower Crane, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of Over 100 Tons, Self-Erecting Tower Crane With a Lifting Capacity Of Over 4,000 Lbs., Crane With Boom Dollies; Crane, Tower Crane, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 176 Ft or Over; Master Mechanic. Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s):	36.72	20.40	-57.12
	DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine ss/civilrights/laborwages/pwc.htm.			
542	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of 130,000 Lbs. or Over; Caisson Rig; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of 100 Tons or Under, Self-Erecting Tower Crane With a Lifting Capacity of 4,000 Lbs. & Under; Crane, Tower Crane Portable Tower, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 175 Ft or Under; Dredge (NOT Performing Work on the Great Lakes); Licensed Boat Pilot (NOT Performing Work on the Great Lakes); Pile Driver.		20.40	56.62
	Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium.			

See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine

ss/civilrights/laborwages/pwc.htm.

CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
543	Air Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Automatic Subgrader (Concrete); Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. &	35.72	20.40	56.12
	Under); Boring Machine (Directional, Horizontal or Vertical); Bridge (Bidwell) Paver; Bulldozer or Endloader; Concrete Batch Plant, Batch Hopper; Concrete Breaker (Large, Auto, Vibratory/Sonic, Manual or			
	Remote); Concrete Bump Cutter, Grinder, Planing or Grooving Machine; Concrete Conveyor System; Concrete Laser/Screed; Concrete Paver (Slipform); Concrete Pump, Concrete Conveyor (Rotec or Bidwell Type); Concrete Slipform Placer Curb & Gutter Machine; Concrete Spreader &			
	Distributor; Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Crane With a Lifting Capacity of 25 Tons or Under; Forestry Equipment, Timbco, Tree Shear, Tub Grinder, Processor; Gradall (Cruz-Aire Type); Grader or Motor Patrol; Grout Pump, Hydro-Blaster			
	(10,000 PSI or Over); Loading Machine (Conveyor); Manhoist; Material or Stack Hoist; Mechanic or Welder; Milling Machine; Post Hole Digger or Driver; Scraper (Self Propelled or Tractor Drawn) 5 cu yds or More Capacity; Shoulder Widener; Sideboom; Skid Rig; Stabilizing or Concrete			
	Mixer (Self-Propelled or 14S or Over); Straddle Carrier or Travel Lift; Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck Mounted Hydraulic Backhoe; Trencher (Wheel Type or Chain Type); Tube Finisher; Tugger (NOT Performing Work on the Great Lakes); Winches & A-Frames.			
	Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic			
	rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/business/civilrights/laborwages/pwc.htm.			
544	Backfiller; Belting, Burlap, Texturing Machine; Broom or Sweeper; Compactor (Self-Propelled or Tractor Mounted, Towed & Light Equipment); Concrete Finishing Machine (Road Type); Environmental Burner; Farm or Industrial Type Tractor; Fireman (Pile Drivèr & Derrick	33.96	19.79	53.75
	NOT Performing Work on the Great Lakes); Forklift; Greaser; Jeep Digger; Joint Sawer (Multiple Blade); Launch (NOT Performing Work on the Great Lakes); Lift Slab Machine; Mechanical Float; Mulcher; Power Subgrader; Robotic Tool Carrier (With or Without Attachments); Self Propelled Chip Spreader; Shouldering Machine; Skid Steer Loader (With or Without Attachments); Telehandler; Tining or Curing Machine.			
545	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Automatic Belt Conveyor & Surge Bin; Boiler (Temporary Heat); Concrete Proportioning Plant; Crusher, Screening or Wash Plant;	30.32	18.46	48.78
	Generator (&/or 150 KW or Over); Heaters (Mechanical); High Pressure Utility Locating Machine (Daylighting Machine); Mudjack; Oiler; Prestress Machine; Pug Mill; Pump (3 Inch or Over) or Well Points; Rock, Stone Breaker; Screed (Milling Machine); Stump Chipper; Tank Car Heaters; Vibratory Hammer or Extractor, Power Pack.			
546	Fiber Optic Cable Equipment.	26.69	16.65	43.34

	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY	HOURLY	
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE <u>BENEFITS</u> \$	TOTAL \$
547	Work Performed on the Great Lakes Including Diver; Wet Tender or Hydraulic Dredge Engineer.	38.80	20.17	58.97
548	Work Performed on the Great Lakes Including 70 Ton & Over Tug Operator; Assistant Hydraulic Dredge Engineer; Crane or Backhoe Operator; Hydraulic Dredge Leverman or Diver's Tender; Mechanic or Welder.	38.80	20.17	58.97
549	Work Performed on the Great Lakes Including Deck Equipment Operator or Machineryman (Maintains Cranes Over 50 Tons or Backhoes 115,000 Lbs. or more); Tug, Launch or Loader, Dozer or Like Equipment When Operated on a Barge, Breakwater Wall, Slip, Dock or Scow, Deck Machinery.	34.50	20.04	54.54
550	Work Performed on the Great Lakes Including Deck Equipment Operator; Machineryman or Fireman (Operates 4 Units or More or Maintains Cranes 50 Tons or Under or Backhoes 115,000 Lbs. or Under); Deck Hand, Deck Engineer or Assistant Tug Operator; Off Road Trucks - Great Lakes ONLY.	34.50	20.04	54.54
	HEAVY EQUIPMENT OPERATORS ASPHALT PAVEMENT OR OTHER WO			*
	ASFRACI PAVEIMENT OR OTHER WC	JKN		1
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
551	Crane, Tower Crane, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of Over 100 Tons, Self Erecting Tower Crane With a Lifting Capacity of Over 4,000 Lbs., Crane With Boom Dollies; Crane, Tower Crane, Pedestal Tower or Derrick, With Boom, Leads and/or Jib Lengths Measuring 176 Ft or Over, Master Mechanic.	35.12	18.46	53.58
552	Backhoe (Track Type) Having a Mfgr.'s Rated Capacity of 130,000 Lbs. or Over; Caisson Rig; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With or Without Attachments, With a Lifting Capacity of 100 Tons or Under, Self-Erecting Tower Crane With a Lifting Capacity Of 4,000 Lbs. & Under; Crane, Tower Crane, Portable Tower, Pedestal Tower or Derrick, With Boom, Leads &/or Jib Lengths Measuring 175 Ft or Under; Dredge (NOT Performing Work on the Great Lakes); Licensed Boat Pilot (NOT Performing Work on the Great Lakes); Pile Driver. Future Increase(s):		20.40	56.62
-	Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015); Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic			
	rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/business/civilrights/laborwages/pwc.htm.			

CODE	Fringe Benefits Must Be Paid On All Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY	HOURLY FRINGE BENEFITS	TOTAL
Program of the Control of the Control		\$	\$	\$
553	Air, Track, Rotary or Percussion Drilling Machine &/or Hammers, Blaster; Asphalt Heater, Planer & Scarifier; Asphalt Milling Machine; Asphalt Screed; Backhoe (Track-Type) Having a Mfgr.'s Rated Capacity of Under 130,000 Lbs., Backhoe (Mini, 15,000 Lbs. & Under); Bituminous (Asphalt) Plant & Paver, Screed; Boring Machine (Directional, Horizontal or Vertical); Bulldozer or Endloader; Concrete Breaker (Large, Auto, Vibratory/Sonic, Manual or Remote); Concrete Conveyor System; Concrete Laser/Screed; Concrete Slipform Placer Curb & Gutter Machine; Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Crane With a Lifting Capacity of 25 Tons or Under; Forestry Equipment, Timbco, Tree Shear, Tub Grinder, Processor; Gradall (Cruz-Aire Type); Grader or Motor Patrol; Hydro-Blaster (10,000 PSI or Over); Loading Machine (Conveyor); Manhoist; Material or Stack Hoist; Mechanic or Welder; Milling Machine; Post Hole Digger or Driver; Railroad Track Rail Leveling Machine, Tie Placer, Extractor, Tamper, Stone Leveler or Rehabilitation Equipment; Roller (Over 5 Ton); Scraper (Self Propelled or Tractor Drawn) 5 cu yds or More Capacity; Shoulder Widener;		18.96	51.85
-	Sideboom; Skid Rig; Stabilizing or Concrete Mixer (Self-Propelled or 14S or Over); Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck Mounted Hydraulic Backhoe; Trencher (Wheel Type or Chain Type); Tube Finisher; Tugger (NOT Performing Work on the Great Lakes); Winches & A-Frames.			·
554	Backfiller; Broom or Sweeper; Compactor (Self-Propelled or Tractor Mounted, Towed & Light Equipment); Concrete Finishing Machine (Road Type); Environmental Burner; Farm or Industrial Type Tractor; Fireman (Asphalt Plant, Pile Driver & Derrick NOT Performing Work on the Great Lakes); Forklift; Greaser; Hoist (Tugger, Automatic); Jeep Digger; Joint Sawer (Multiple Blade); Launch (NOT Performing Work on the Great Lakes); Lift Slab Machine; Mechanical Float; Mulcher; Power Subgrader; Robotic Tool Carrier (With or Without Attachments); Roller (Rubber Tire, 5 Ton or Under); Self-Propelled Chip Spreader; Shouldering Machine; Skid Steer Loader (With or Without Attachments); Telehandler.	33.67	19.48	53.15
555	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Augers (Vertical & Horizontal); Automatic Belt Conveyor & Surge Bin; Boiler (Temporary Heat); Crusher, Screening or Wash Plant; Generator (&/or 150 KW or Over); Heaters (Mechanical); High Pressure Utility Locating Machine (Daylighting Machine); Mudjack; Oiler; Prestress Machine; Pug Mill; Pump (3 Inch or Over) or Well Points; Rock, Stone Breaker; Screed (Milling Machine); Stump Chipper; Tank Car Heaters; Vibratory Hammer or Extractor, Power Pack. Future Increase(s): Add \$1.75/hr on 6/1/2014); Add \$1.25/hr on 6/1/2015);	35.17	20.40	55.57
	Add \$1.30/hr on 6/1/2016); Add \$1.25/hr on 6/1/2017. Premium Increase(s): DOT PREMIUMS: 1) Pay two times the hourly basic rate on Sunday, New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day. 2) Add \$1.50/hr night work premium. See DOT'S website for details about the applicability of this night work premium at: http://www.dot.wi.gov/busine ss/civilrights/laborwages/pwc.htm.	00.00	40.05	42.24
556	Fiber Optic Cable Equipment.	26.69	16.65	43.34

RESIDENTIAL OR AGRICULTURAL CONSTRUCTION

Includes single family houses or apartment buildings of no more than four (4) stories in height and all buildings, structures or facilities that are primarily used for agricultural or farming purposes, excluding commercial buildings. For classification purposes, the exterior height of a residential building, in terms of stories, is the primary consideration. All incidental items such as site work, driveways, parking lots, private sidewalks, private septic systems or sewer and water laterals connected to a public system and swimming pools are included within this definition. Residential buildings of five (5) stories and above are NOT included within this definition.

SKII	1	ED	TP	ΔD	EC
	_ Ł		15.	~_	

	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY	HOURLY	
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE <u>BENEFITS</u> \$	TOTAL \$
101	Acoustic Ceiling Tile Installer Future Increase(s): Add \$1.25/hr on 6/2/2014.	33.68	19.81	53.49
102	Boilermaker	26.00	4.73	30.73
103	Bricklayer, Blocklayer or Stonemason	32.01	13.26	45.27
104	Cabinet Installer	22.00	1.05	23.05
105	Carpenter	30.48	3.24	33.72
106	Carpet Layer or Soft Floor Coverer	23.68	3.20	26.88
107	Cement Finisher	20:93	5.94	26.87
108	Drywall Taper or Finisher	22.50	0.88	23.38
109-	Electrician	27.50	7.47	34.97
110	Elevator Constructor	42.86	23.84	66.70
111	Fence Erector	18.52	4.89	23.41
112	Fire Sprinkler Fitter	52.82	5.54	58.36
113	Glazier	38.03	13.42	51.45
114	Heat or Frost Insulator	30.00	0.00	30.00
115	Insulator (Batt or Blown)	19.00	14.33	33.33
116	lronworker	31.25	19.46	50.71
117	Lather	30.48	3.24	33.72
119	Marble Finisher	26.89	19.18	46.07
120	Marble Mason	32.01	13.26	45.27
121	Metal Building Erector	17.00	3.82	20.82
123	Overhead Door Installer	12.00	0.00	12.00
124	Painter	20.00	4.22	24.22

	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE	
CODE	TRADE OR OCCUPATION	OF PAY \$	<u>BENEFITS</u> \$	TOTAL \$
125	Pavement Marking Operator	30.00	0.00	30.00
129	Plasterer	25.00	0.00	25.00
130	Plumber	30.00	10.62	40.62
132	Refrigeration Mechanic	19.75	8.56	28.31
133	Roofer or Waterproofer	17.00	3.72	20.72
134	Sheet Metal Worker	21.03	3.40	24.43
135	Steamfitter	31.72	16.10	47.82
137	Teledata Technician or Installer	24.75	8.09	32.84
138	Temperature Control Installer	22.50	0.70	23.20
139	Terrazzo Finisher	26.89	19.18	46.07
140	Terrazzo Mechanic	30.20	18.42	48.62
141	Tile Finisher	23.77	16.50	40.27
142	Tile Setter	21.00	0.00	21.00
143	Tuckpointer, Caulker or Cleaner	32.50	0.02	32.52
146	Well Driller or Pump Installer	27.60	5.80	33.40
147	Siding Installer	20.18	0.00	20.18
	TRUCK DRIVERS	3		
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	<u>TOTAL</u> \$
201	Single Axle or Two Axle	28.05	4.16	32.21
203	Three or More Axle	18.00	2.37	20.37
205	Pavement Marking Vehicle	18.00	2.37	20.37
207	Truck Mechanic	19.00	1.85	20.85
	LABORERS			, ,
CODE	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked TRADE OR OCCUPATION	HOURLY BASIC RATE OF PAY \$	HOURLY FRINGE BENEFITS \$	TOTAL \$
301	General Laborer	18.14	10.16	28.30
302	Asbestos Abatement Worker	17.00	3.86	20.86

	Fringe Benefits Must Be Paid On All Hours Worked	HOURLY	HOURLY		
CODE	TRADE OR OCCUPATION	BASIC RATE OF PAY \$	FRINGE <u>BENEFITS</u> \$	TOTAL \$	
303	Landscaper	30.00	0.00	30.00	
311	Fiber Optic Laborer (Outside, Other Than Concrete Encased)	18.31	12.67	30.98	
315	Final Construction Clean-Up Worker	16.00	0.00	16.00	
	HEAVY EQUIPMENT OPERATORS RESIDENTIAL OR AGRICULTURAL CONST				
	Fringe Benefits Must Be Paid On <u>All</u> Hours Worked	HOURLY BASIC RATE	HOURLY FRINGE		
CODE	TRADE OR OCCUPATION	OF PAY \$	BENEFITS \$	TOTAL \$	
557	Asphalt Heater, Planer & Scarifier; Asphalt Milling Machine; Asphalt Screed; Backhoe (Track Type); Backhoe (Mini, 15,000 Lbs. & Under); Bituminous (Asphalt) Plant & Paver, Screed; Boring Machine (Directional, Horizontal or Vertical); Bulldozer or Endloader; Concrete Breaker (Large, Auto, Vlbratory/Sonic, Manual or Remote); Concrete Bump Cutter, Grinder, Planing or Grooving Machine; Concrete Conveyor System; Concrete Laser/Screed; Concrete Paver (Slipform); Concrete Pump, Concrete Conveyor (Rotec or Bidwell Type); Concrete Slipform Placer	29.70	20.08	49.78	
	Curb & Gutter Machine; Concrete Spreader & Distributor; Crane (Carry Deck, Mini) or Truck Mounted Hydraulic Crane (10 Tons or Under); Crane With a Lifting Capacity of 25 Tons or Under; Crane, Shovel, Dragline, Clamshells; Forestry Equipment, Timbco, Tree Shear, Tub Grinder, Processor; Grader or Motor Patrol; Grout Pump; Hydro-Blaster (10,000 PSI or Over); Loading Machine (Conveyor); Manhoist; Material or Stack				
	Hoist; Mechanic or Welder; Milling Machine; Roller (Over 5 Ton); Scraper (Self Propelled or Tractor Drawn) 5 cu yds or More Capacity; Shoulder Widener; Skid Rig; Stabilizing or Concrete Mixer (Self-Propelled or 14S or Over); Tractor (Scraper, Dozer, Pusher, Loader); Tractor or Truck Mounted Hydraulic Backhoe; Tractor or Truck Mounted Hydraulic Crane (10 Tons or Under); Trencher (Wheel Type or Chain Type); Winches & A-Frames.				
558	Air Compressor (&/or 400 CFM or Over); Air, Electric or Hydraulic Jacking System; Backfiller; Belting, Burlap, Texturing Machine; Boiler (Temporary Heat); Broom or Sweeper; Compactor (Self-Propelled or Tractor Mounted, Towed & Light Equipment); Concrete Finishing Machine (Road Type); Farm or Industrial Type Tractor; Forklift; Generator (&/or 150 KW or Over); Heaters (Mechanical); High Pressure Utility Locating Machine (Daylighting Machine); Jeep Digger; Lift Slab Machine; Mulcher; Oiler; Post Hole Digger or Driver; Power Subgrader; Pump (3 Inch or Over) or Well Points; Robotic Tool Carrier (With or Without Attachments); Rock, Stone Breaker; Roller (Rubber Tire, 5 Tons or Under); Screed (Milling Machine); Self Propelled Chip Spreader; Shouldering Machine; Skid Steer Loader (With or Without Attachments); Stump Chipper; Telehandler; Vibratory Hammer or Extractor, Power Pack.	29.70	16.00	45.70	

*			
			·
		* '	
★.			
	and the second second		
•	•		
•			
	•		•
*			
-			
			**
•			
		*	
